

## APPLICATION/AGREEMENT

Permit # 1406-2022

For Trench/Disturbance Permit within the City of New Bedford

Dig Safe#20223411816

Date: 08/25/2022

TO THE MAYOR AND CITY COUNCIL:

DISTURBANCE PERMIT/TRENCH SAFETY PERMIT

Permission is hereby requested to excavate the surface of: X City Property and/or X Private Property

Provide Sketch

Location of Work: Court St. @ Cottage St.Between Cottage St & Cedar St. Working in street & street to house and 50 ft in each direction at intersections.Emergency gas line maintenance.Work will begin (weather permitting) on: August 25, 2022ROADWAY CLOSURES WILL REQUIRE  
AUTHORIZATION FROM THE  
COMMISSIONER OF PUBLIC  
INFRASTRUCTURE. TRAFFIC MANAGEMENT  
PLANS MAY BE REQUIRED.Applicant Name: Steven Botelho (gk)

Excavator(s) Name: \_\_\_\_\_

Company Name: Eversource

Hoisting Equipment License Number: \_\_\_\_\_

Grade: \_\_\_\_\_ Expiration Date: \_\_\_\_\_

Contact Number: 339-987-8010

Name &amp; Contact Number of Insurer: \_\_\_\_\_

Competent Person on Work Site: ON FILEAPPROVED BY: Stephen Cyphar DATE: 9-21-2022

TITLE: \_\_\_\_\_

**This permit shall be posted at the work site, and shall remain until the work is completed. It is subject to inspection at all times.**Work completed prior to D.P.I. approval under  
emergency work order for Class II LeakEmergency work completed  
prior to DPI sign off of  
permit**Trenches must be maintained  
weekly until final paving is  
completed**Permit only valid for three months  
from date of approval

2 Digsafes called:  
Court @ Cottage  
Cottage from Cottage to Ash St.

**EVERSOURCE**

**DAILY ACTIVITY REPORT**

DigSafe/ CBYD Number		PERMIT #		PROJECT #	GAS-EMGGAS2Y	Unique ID :	10231720-10-[VQ81]
ADDRESS:	95 COURT ST	TOWN:	NEW BEDFORD	DATE:	08/25/22	WORK ORDER- TASK:	10231720-10
SHEET 1 of 77		LEAK REPORT #		LEAK CLASS		TYPE OF WORK:	GASMAINTENANCE
		Contractor:		WAMFWO:	30419200	WAMCTE #	956839

**PIPE RETIREMENT**

FACILITY_TYPE	MATERIAL	SIZE	LENGTH	PRESSURE	VIN YR
	Plastic	3/4	24	LI	1974

**PIPE INSPECTION**

No

**PIPE INSTALL**

FACILITY TYPE	MATERIAL	SIZE	LENGTH	PRESSURE	METHOD	OVERALL PIPE LENGTH	INSTALLED/ REPLACED	DEPTH OF COVER	CONNECTION AT MAIN	EFV INSTALLED	EFV SUBTYPE	EFV COMMENTS
Main	Plastic	2"	1'	LI	Direct Bury			2' 0"				
Service	Plastic	0.50"	24'	LI	Insert	60' or Less	Main to Valve	2' 0"	Fused	No		Large volume meter per carlos

**PRESSURE TEST**

MEDIUM	TYPE	START TIME	START PRESSURE(PSIG)	FINISH TIME	FINISH PRESSURE(PSIG)	TEST DURATION	PERFORMED BY	SOAP TESTED	NOTES
Air	Service below 200 ft	2022-08-25 14:04:00	100	2022-08-25 14:19:00	100	15min	Jason arruda	Yes	At all connections
Air	Main	2022-08-25 13:00:00	100	2022-08-25 14:00:00	100	60min	Jason arruda	Yes	At all connections

**RESTORATION**

CONSTRUCTION MATERIAL	LOCATION	EXISTING SURFACE FINISH	EXISTING DEPTH	LENGTH	WIDTH	REQUIRED DEPTH	TEMPORARY REPAIR ACTION	COMPACTION METHOD	% COMPACTED
Hot Asphalt	Street	Asphalt	4	6' 0"	5' 0"	4"		Compacted per O&M Standards	90
Concrete	Sidewalk	Concrete	4	6' 0"	4' 0"	4"		Compacted per O&M Standards	93

**MATERIALS**

No

**DESCRIPTION OF WORK COMPLETED**

Bar and tested Dug on highest reading found leak on T... Retired 1 foot of plastic 2 inch main and 24 feet of three-quarter inch plastic... Installed new 1 foot of 2 inch plastic and a new tee and inserted 24 feet of half-inch plastic through old three-quarter inch plastic from valve to main

**PERSONNEL**


FOREMAN / WORKING LEADER / INSPECTOR

SIGNATURE:

DigSafe/ CBYD Number		PERMIT#		PROJECT#	GAS-EMGGAS2Y	Unique ID :	10231720-10- [VQ81]
ADDRESS:	95 COURT ST	TOWN:	NEW BEDFORD	DATE:	08/25/22	WORK ORDER- TASK:	10231720-10
URL:	<a href="http://CWV-CLKSOPRD1/Repository/Files/cdy_photo_001_035530(NAztEhV2).jpg">http://CWV-CLKSOPRD1/Repository/Files/cdy_photo_001_035530(NAztEhV2).jpg</a>	LEAK REPORT #		LEAK CLASS		TYPE OF WORK:	GASMAINTENANCE
SHEET 2 of 77		Contractor:		WAMFWO:	30419200	WAMCTE #	956839

7:04 AM Fri Aug 26

LTE (VPN) 43%

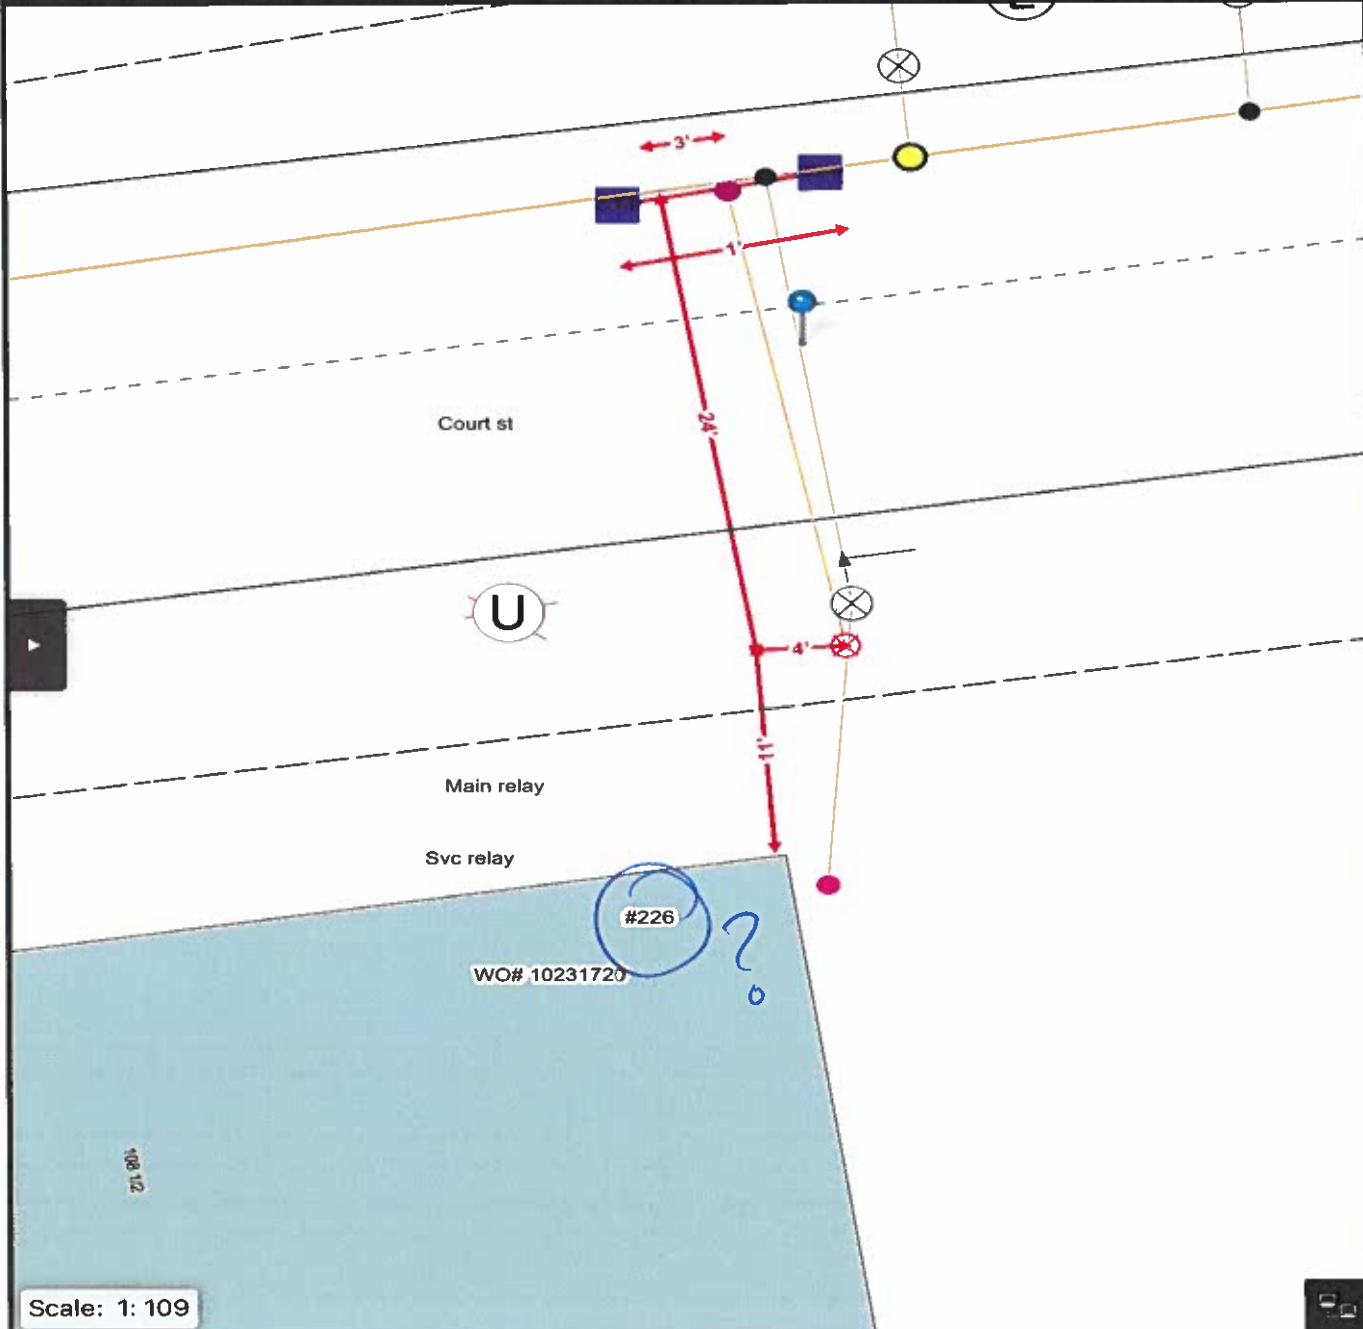

User jason.arruda@eversour Portal

EpochFieldCloud\_Prod41\_Ga

Mod Map Markup - Arial
