

NOTICE TO COMMISSIONER OF PUBLIC WORKS

49

Length of drain.....⁷² 30

Sewer depth.....^{5 1/2}

Surf. drain.....

Bill 12/14/72

.....1.....pipe system

Drain Permit **N^o 19499**

City of New Bedford,

Office of City Clerk, *11/16/72*

To Commissioner of Public Works.

Permission has this day been issued to

Reliable Homes Inc
Property owner

22 Tarkenton Hill Rd
Address

By.....

Address.....

to lay drain from the premises of *SS. Fulmore St, 225' ± E of*
Mt Pleasant St.

to connect with the sewer in *Seemmer* street.

✓ Laid from main in street to ~~iron~~ *line* pipe in property.

✓ Owner agrees to supply all necessary

transite

pipe.

Ellen M. Gaughan
City Clerk.

Requires separate entrance for sewage and roof water

To be laid in conjunction with Permit # 19357 - see attached sketch.
per instructions F.S. Toomey 11-16-72

(P)

RETURN OF FOREMAN

Entered NOV. 27 19 72
 Time 4 P.M.
 By Jesse M. Torres

COST

Labor	hours @		
Josse Torres 6	" 3.75	\$22.50	✓
Joseph Alfonso 6	" 3.32	19.92	✓
Norbert St. Pierre 6	" 3.32	19.92	✓
Wm. Corriero 6	" 3.10	18.54	✓
- Tom Burke 6	" 3.43	20.60	✓
Joseph Macedo 6	" 3.60	21.63	✓
		<u>\$123.11</u>	✓

Stock			
1/2 bag Cement @1.95		.98	✓
100 lbs Sand @.12 cwt		.12	✓
Repair 12 x 3 Oiled Stones @1.00 + 5-		17.00	

Trucking			
#35-3-HRS. @6.55		19.10	65
67-1-HR. @3.00		3.00	
52-1-HR. @3.35		3.35	

Total Cost		167.21
Estimate-cost of laying drain	58 00	
Entrance charges		
Total deposit		
Balance due	City	109.21

Pieces pipe to curb ① 1-10 ft. 1-2 ft.
 " " curb to house ② 1-10 ft. 1-8 ft.
 Cut at sewer 5 ft.
 Cut at curb 3 ft.
 Size of pipe 6" Trans. to - 30 ft.
 Correct

Jesse M. Torres Foreman

owner supplied

11/27/72

Reliable Homes - 22 Tarkiln Hill Rd.

Portion of drain from existing M.H.
in Summer st. to new M.H. in Filmore st
to be given to City as public sewer-


Following is Jesse Tavares report-

Filmore st. e. of Summer st.-
lay 160 ft. transite to extend existing
sewer line plus 1 manhole.

labor	225.70
trucking 8 hr. @ 3.00	24.00
backhoe 8 hr. @ 6.55	52.40
M.H. casting & cover (1)	62.50
barrel blocks 36 @ 31¢	11.16
arch blocks 45 @ 33¢	14.85
bags mortar 2 @ 1.75	3.50
reg. cement 1 bag	1.95
cement bricks 30 @ 06¢	1.80
cwt. sand 2 @ 12¢	.24

398.10

(24)

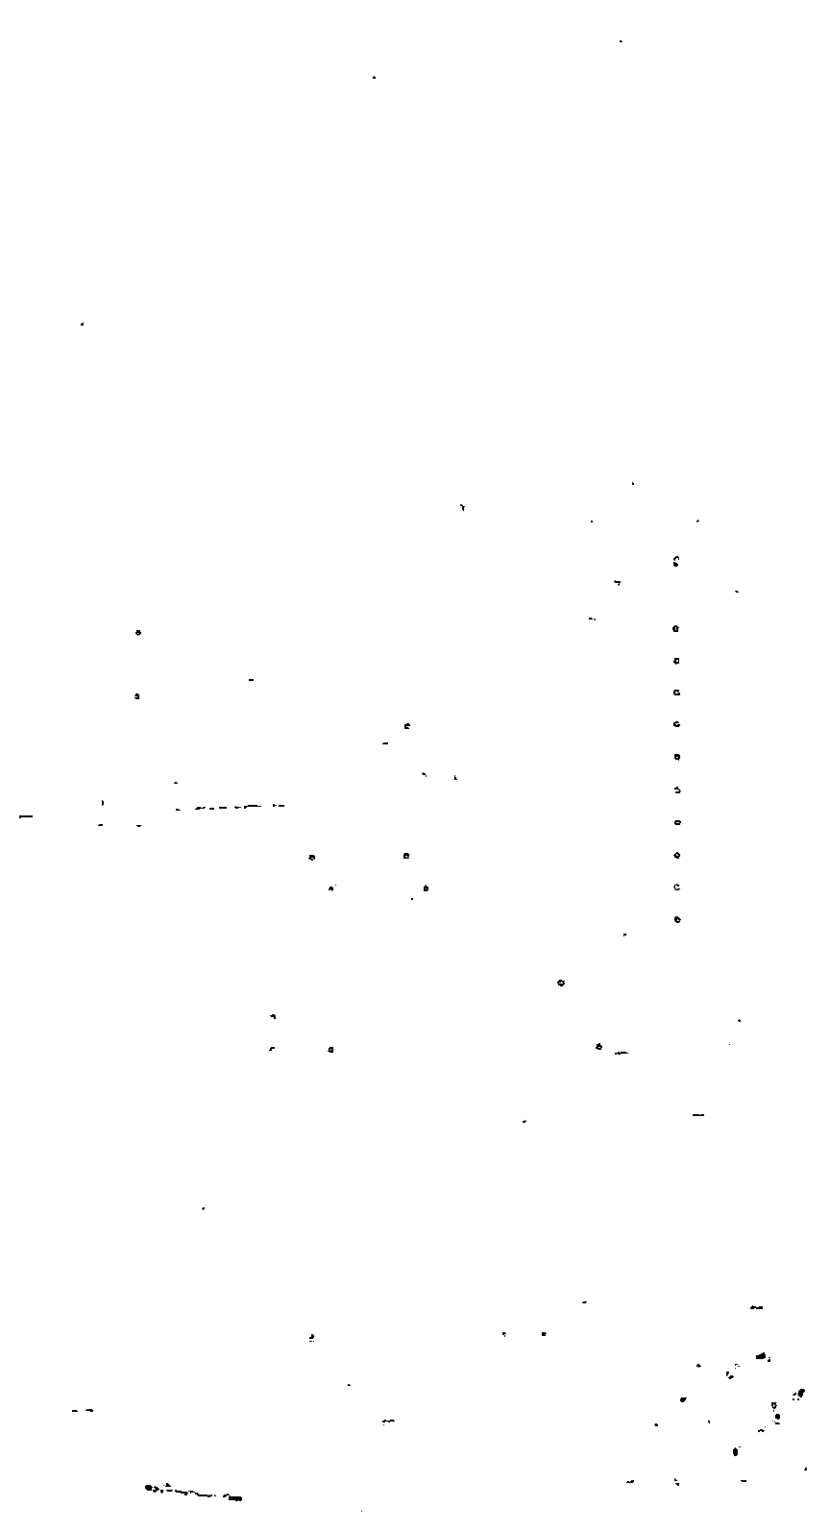


Filmore East. of Samson
 lay 160 ft. Trunk to
 To extend existing ^(sewer) line
 plus 1-Man-hole.

Man	hrs.		
José Torres -	11 ✓	—	41.25 ✓
Joseph Alfonso -	11 ✓	—	36.52 ✓
Vorbert St. Pierre -	11	—	36.52 ✓
Wm. Coniers -	11 ✓	—	33.99 ✓
Tom Bark -	11 ✓	—	37.78 ✓
Joseph Macedo -	11 ✓	—	39.65 ✓
	<u>66</u>		<u>225.71</u>

Foreman
 Nov. 27 - 4 P. M. Paul W. Jones

Materials on other
 do

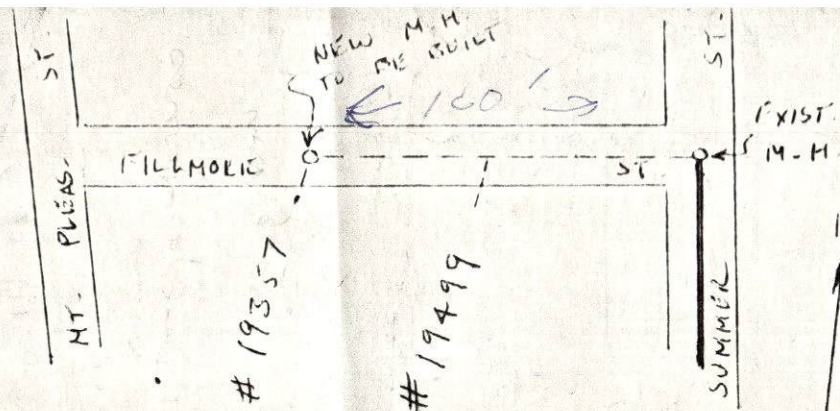

PORTION OF DRAIN FROM EXIST. M.H. IN SUMMER ST. TO NEW M.H. IN FILLMORE ST. TO BE GIVEN TO CITY AS PUBLIC SEWER BY RELIABLE HOMES. 11-16-72

job completed 11/27/72
will come down on street sheet for R 49

sewer Supplied
pipe only

- (cover)
- 1-Man-hole Casting ✓
- 1-Manhole-Cover ✓

- 36 Barrel Blocks ✓
- 45 Arch Blocks ✓
- 2-Bags Mortar ✓
- 1-Bag - Portland Cement ✓
- 30 Cement-Bricks ✓

#19499 - completed-
on Friday, 11/24/72

(2 hrs., Wed; 4 hrs., Fri.)

avares, J.	-6	@3.75-	\$22.50
lfonso, J.	-6	@3.32-	19.92
urke, T.	-6	@3.43-	20.60
acedo, J.	-6	@3.60-	21.63
t. Pierre, N.	-6	@3.32-	19.92
orreia, W.	-6	@3.10-	18.54

\$123.11

#19499 - Reliable Homes -

• Filed with D.J.Realty-

Reliable Homes, Gerardo Realty

and D.J.Realty all owned by

Gerard Guillotte - Balance due was

deducted from deposit made by

D.J.Realty.

dt

- several children - 2000

- 1800, 1800, 1800, 1800

1800, 1800, 1800, 1800

1800, 1800, 1800, 1800

1800, 1800, 1800, 1800

1800, 1800, 1800, 1800

1800, 1800, 1800, 1800

SUMMARY:

	#19357	
	Tuesday	
	11/21/72	
Correia, W.	- - - - -	
Tavares, J.	- 6 hrs. @3.75-	22.50
Alfonso, J.	- 6 " @3.32-	19.92
Correia, W.	- 6 " @3.32-	19.92
Burke, T.	- 6 " @3.43-	20.60
Macedo, J.	- 6 " @3.60-	21.63
Ferreira, F.	- 6 " @3.10-	18.54
		<u>\$123.11</u>

	#19499	
	Wed., 2 hrs. 11/22	
	Fri., 4 hrs. 11/24	
	6 hrs. @3.10-	18.54
	6 hrs. @3.75-	22.50
	6 " @3.32-	19.92
	- - - - -	- - - - -
	6 " @3.43-	20.60
	6 " @3.60-	21.63
	- - - - -	- - - - -
		<u>\$123.11</u>

Labor performed on the
Fillmore St. Sewer Line
Fri., 11/24/72

3 hrs. @3.10-	\$19.27
3 " @3.75-	11.25
3 " @3.32-	9.96
- - - - -	- - - - -
3 " @3.43-	10.30
3 " @3.60-	10.81
- - - - -	- - - - -
	<u>\$61.55</u>

Monday, 11/27/72:
(Roll #49)

Tavares, J.	- 8 @3.75-	\$30.00
Alfonso, J.	- 8 @3.32-	26.26
Burke, T.	- 8 @3.43-	27.47
Macedo, J.	- 8 @3.60-	28.82
St. Pierre,	- 8 @3.32-	26.56
Correia, W.	- 8 @3.10-	34.72
		<u>\$164.15</u>

\$164.15
<u>61.55</u>
<u>\$225.70</u>

10-2-52

10-2-52

10-2-52

10-2-52

10-2-52

10-2-52

10-2-52

10-2-52

10-2-52

10-2-52

10-2-52

10-2-52

10-2-52

10-2-52

10-2-52

10-2-52

10-2-52

10-2-52

10-2-52

10-2-52

10-2-52

10-2-52

10-2-52

CITY OF NEW BEDFORD
APPLICATION FOR LAYING DRAIN

Application **Nº 19499**

Board of Health Permit No.

To the Mayor and City Council:

New Bedford, Mass., 11/16/72

I hereby request that a drain be laid from the premises of S.S. Fulmore St,
225' ± E of Mt. Pleasant St

to connect with the sewer in Summer street,
the same to be laid in the street and the surface repaired as directed by the Commissioner of Public Works.

I hereby agree to pay at the office of the City Treasurer all cost of performing the above work in the manner specified, in excess of the deposit made herewith, within 10 days after the completion of the work.

It is understood and agreed that the deposit made with this application shall be applied to the payment of the cost of performing the work done, and that any excess of deposit over the cost shall be returned to me by the City Treasurer.

Witness E. Quadros

Ray Fulmore Bonds Ray
Property owner
29 Taylor Hill Rd
Address

By

Requires separate entrance
for roof water

Address

Consent of Owner of Private Drain

New Bedford, Mass.,

To the Mayor and City Council:

I hereby grant to
the privilege of draining premises

through the private drain owned by me connecting with sewer in
street.

Owner

Estimate and Deposit Requirement

Office of Commissioner of Public Works, 11/16/72

My estimate of the cost of laying the drain described in the above application is

58.00

Assessed
Entrance charges

Total deposit required 58.00
George H. Brightman
Commissioner of Public Works

Certificate of Issue

Office of City Clerk, 11/16/72


The above application, accompanied by City Treasurer's receipt presented this day; whereupon


Permit No. 19499 was issued, and the Commissioner of Public Works notified of the same.

Eileen M. Guaghan
City Clerk

☒ Laid from main in street to ~~iron~~ pipe in property. line
☒ Owner agrees to supply all necessary
transite pipe.

"See attached"

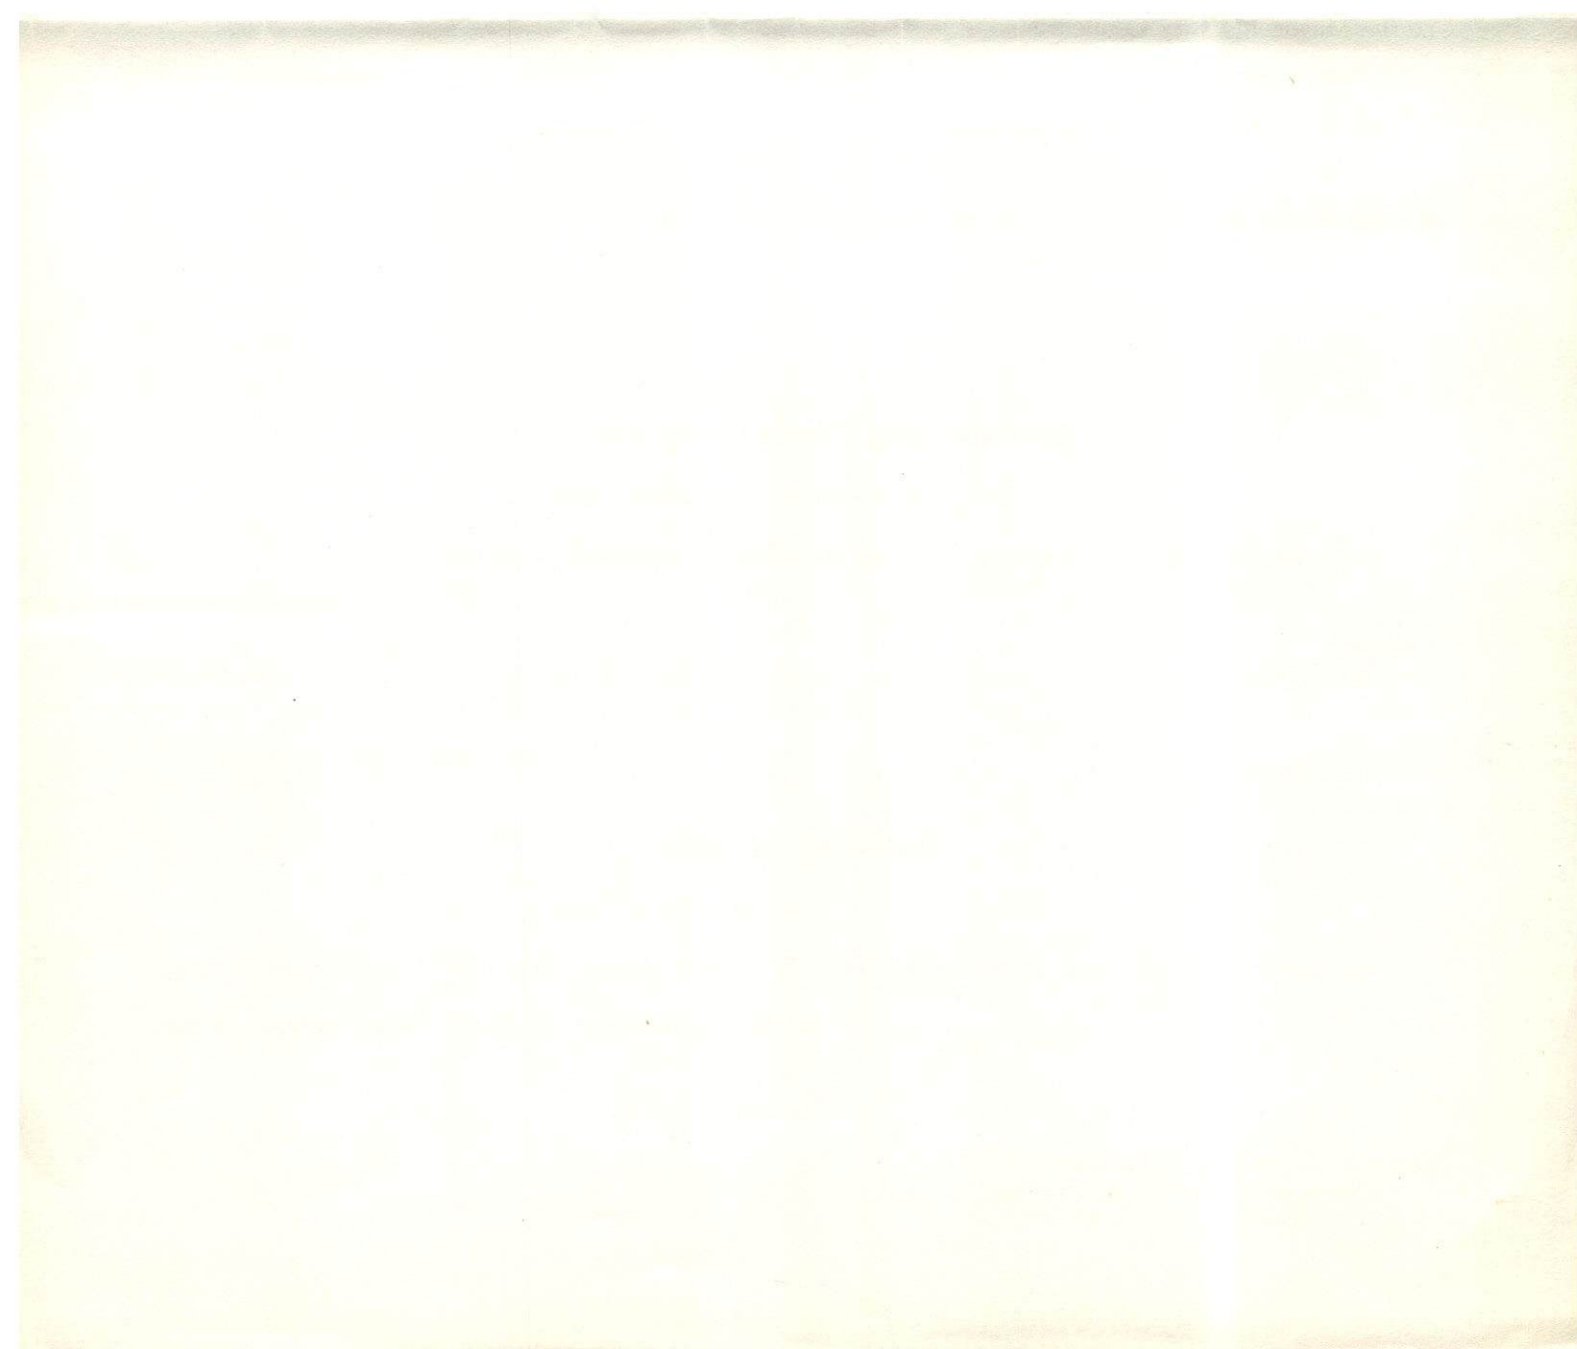

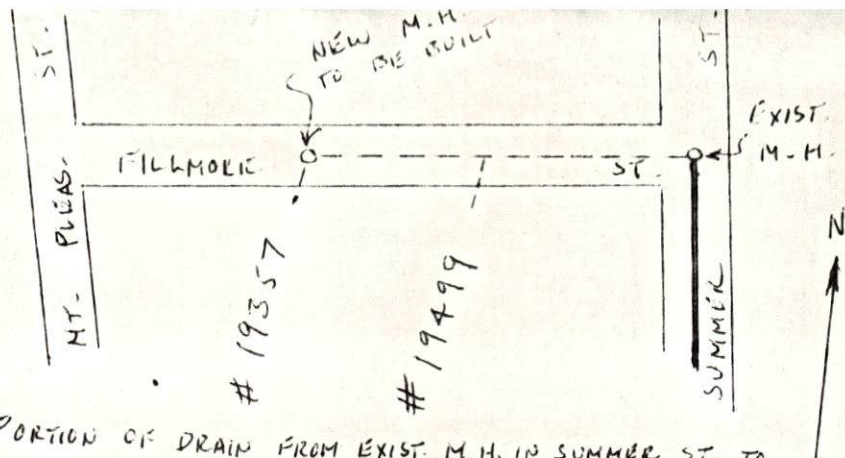

PORTION OF DRAIN FROM EXIST. M.H. IN SUMMER ST. TO
NEW M.H. IN FILLMORE ST. TO BE GIVEN TO CITY AS PUBLIC
SEWER BY RELIABLE HOMES. 11-16-72

