

NOTICE TO COMMISSIONER OF PUBLIC WORKS

24

Length of service 88'

Direct 8/29/74

Sewer depth 6'

1

pipe system

Surf. drain -

Contractor's Name
(if working on City Property)

City of New Bedford,

Drain Permit **Nº 19650**

Office of D. P. W., April 23, 1974
Date

To Commissioner of Public Works.

Permission has this day been issued to

New Bedford Housing Auth

Signature of Property Owner

Address

By *R. Arco R. Jr*

10 Orange St Everett

PAID BY

Concrete Cons. Co. of Everett, Inc. 165 Chelsea St., Everett, Mass.
Division Street n.s.

to lay a building sewer/drain service from the premises at
50'+ e. of First Street

to connect with the sewer/drain in First street.

Laid from main in street to property line.

Owner agrees to supply all necessary materials
transite

By *Eileen M. Gaughan*

and pipe.

Pipe to run from property line to center line of Division St. then
Pd. by Conc. Cons. Co. of
Requires separate entrance for sewage and roof water
Everett, Inc. 165 Chelsea



RETURN OF FOREMAN

Entered June 13 19 74
 Time 9.30 A.M.
 By Jesse M. Morris
 COST

Labor	hours @		
Super Jesse Torres 5 "	4.33	- - - -	21.6
labor: Joe Ferreira 5 "	3.74	18.70	✓
Robert St. Pierre 5 "	3.64	18.20	✓
Jim Lemos 5 "	3.11	15.55	✓
Tom Burke 5 "	3.68	18.40	✓
Joe Macedo 5 "	3.86	19.30	✓
	"		90.1
			111.8
Stock			
1/2 bag Cement @2.45-		1.23	✓
100 lbs Sand @ .10 cwt-		.10	✓
① 4x4 galv. walk Sg.			
1 1/4 sq. galv. @ 14.00		24.89	
Trucking			
Wardson #35-3-HRS @6.55 -		19.65	✓
Dodge #16-2-HRS, @3.00 -		6.00	✓
Comp. - 52-1-HR. @3.35 -		3.35	✓
Total Cost		142.13	
Estimate-cost of laying drain	657.00	762.54	
Entrance charges	15.60	904.67	
Total deposit		657.00	
Balance due	City	247.67	

Pieces pipe to curb 20 ft. 2-10 ft. lengths
 " " curb to house 1-10 ft. Piece

Cut at sewer.....
 Cut at curb 4 ft.
 Size of pipe 6" Transite
 Correct

Jesse M. Morris

Foreman

Owner Suppl. Pipe

DIVISION STREET SEWER EXTENSION

81' FROM THE CENTER LINE OF

WATER STREET WESTERLY TO MANHOLE

ON DIVISION ST. - completed Mon., 6/24/74

Roll #25:

	<u>Super</u>	<u>Labor</u>
6/18 -	25.98	108.78
6/19 -	17.32	72.52
6/20 -	17.32	72.52
6/21 -	34.64	145.04
	<u>95.26</u>	<u>398.86</u>

R. 19650
W. 6/22

Comp 13.40 ✓
Fordson 35 144.10 ✓
Dodge 116 66.00 ✓

Roll #26: *W. 6/29*

6/24 -	8.66	36.26
	<u>103.92</u>	<u>435.12</u>

Itemized:

Super:

Tavares, J. - 24 hrs. @ 4.33 - - - - = 103.92

Labor:

St. Pierre, N.	- 24	"	@ 3.74 -	89.76	
Ferreira, J.	- 24	"	@ 3.74 -	89.76	
Lemos, J.	- 24	"	@ 3.11 -	74.64	
Macedo, J.	- 22	"	@ 3.86 -	84.92	
Burke, T.	- 24	"	@ 3.68 -	88.32	
Jardin, J.	- 2	"	@ 3.86 -	7.72 =	435.12
					<u>539.04</u>

539.04
13.40
144.10
66.00

762.54


142.13
Drain - 167.02

Sewer - 762.54

929.56
657 -

Credit
Bal. due city 272.56 904.67

7/25/74 - Sam said Gus told him that
Concrete Concr. Co. supplied pipes
(Signature)

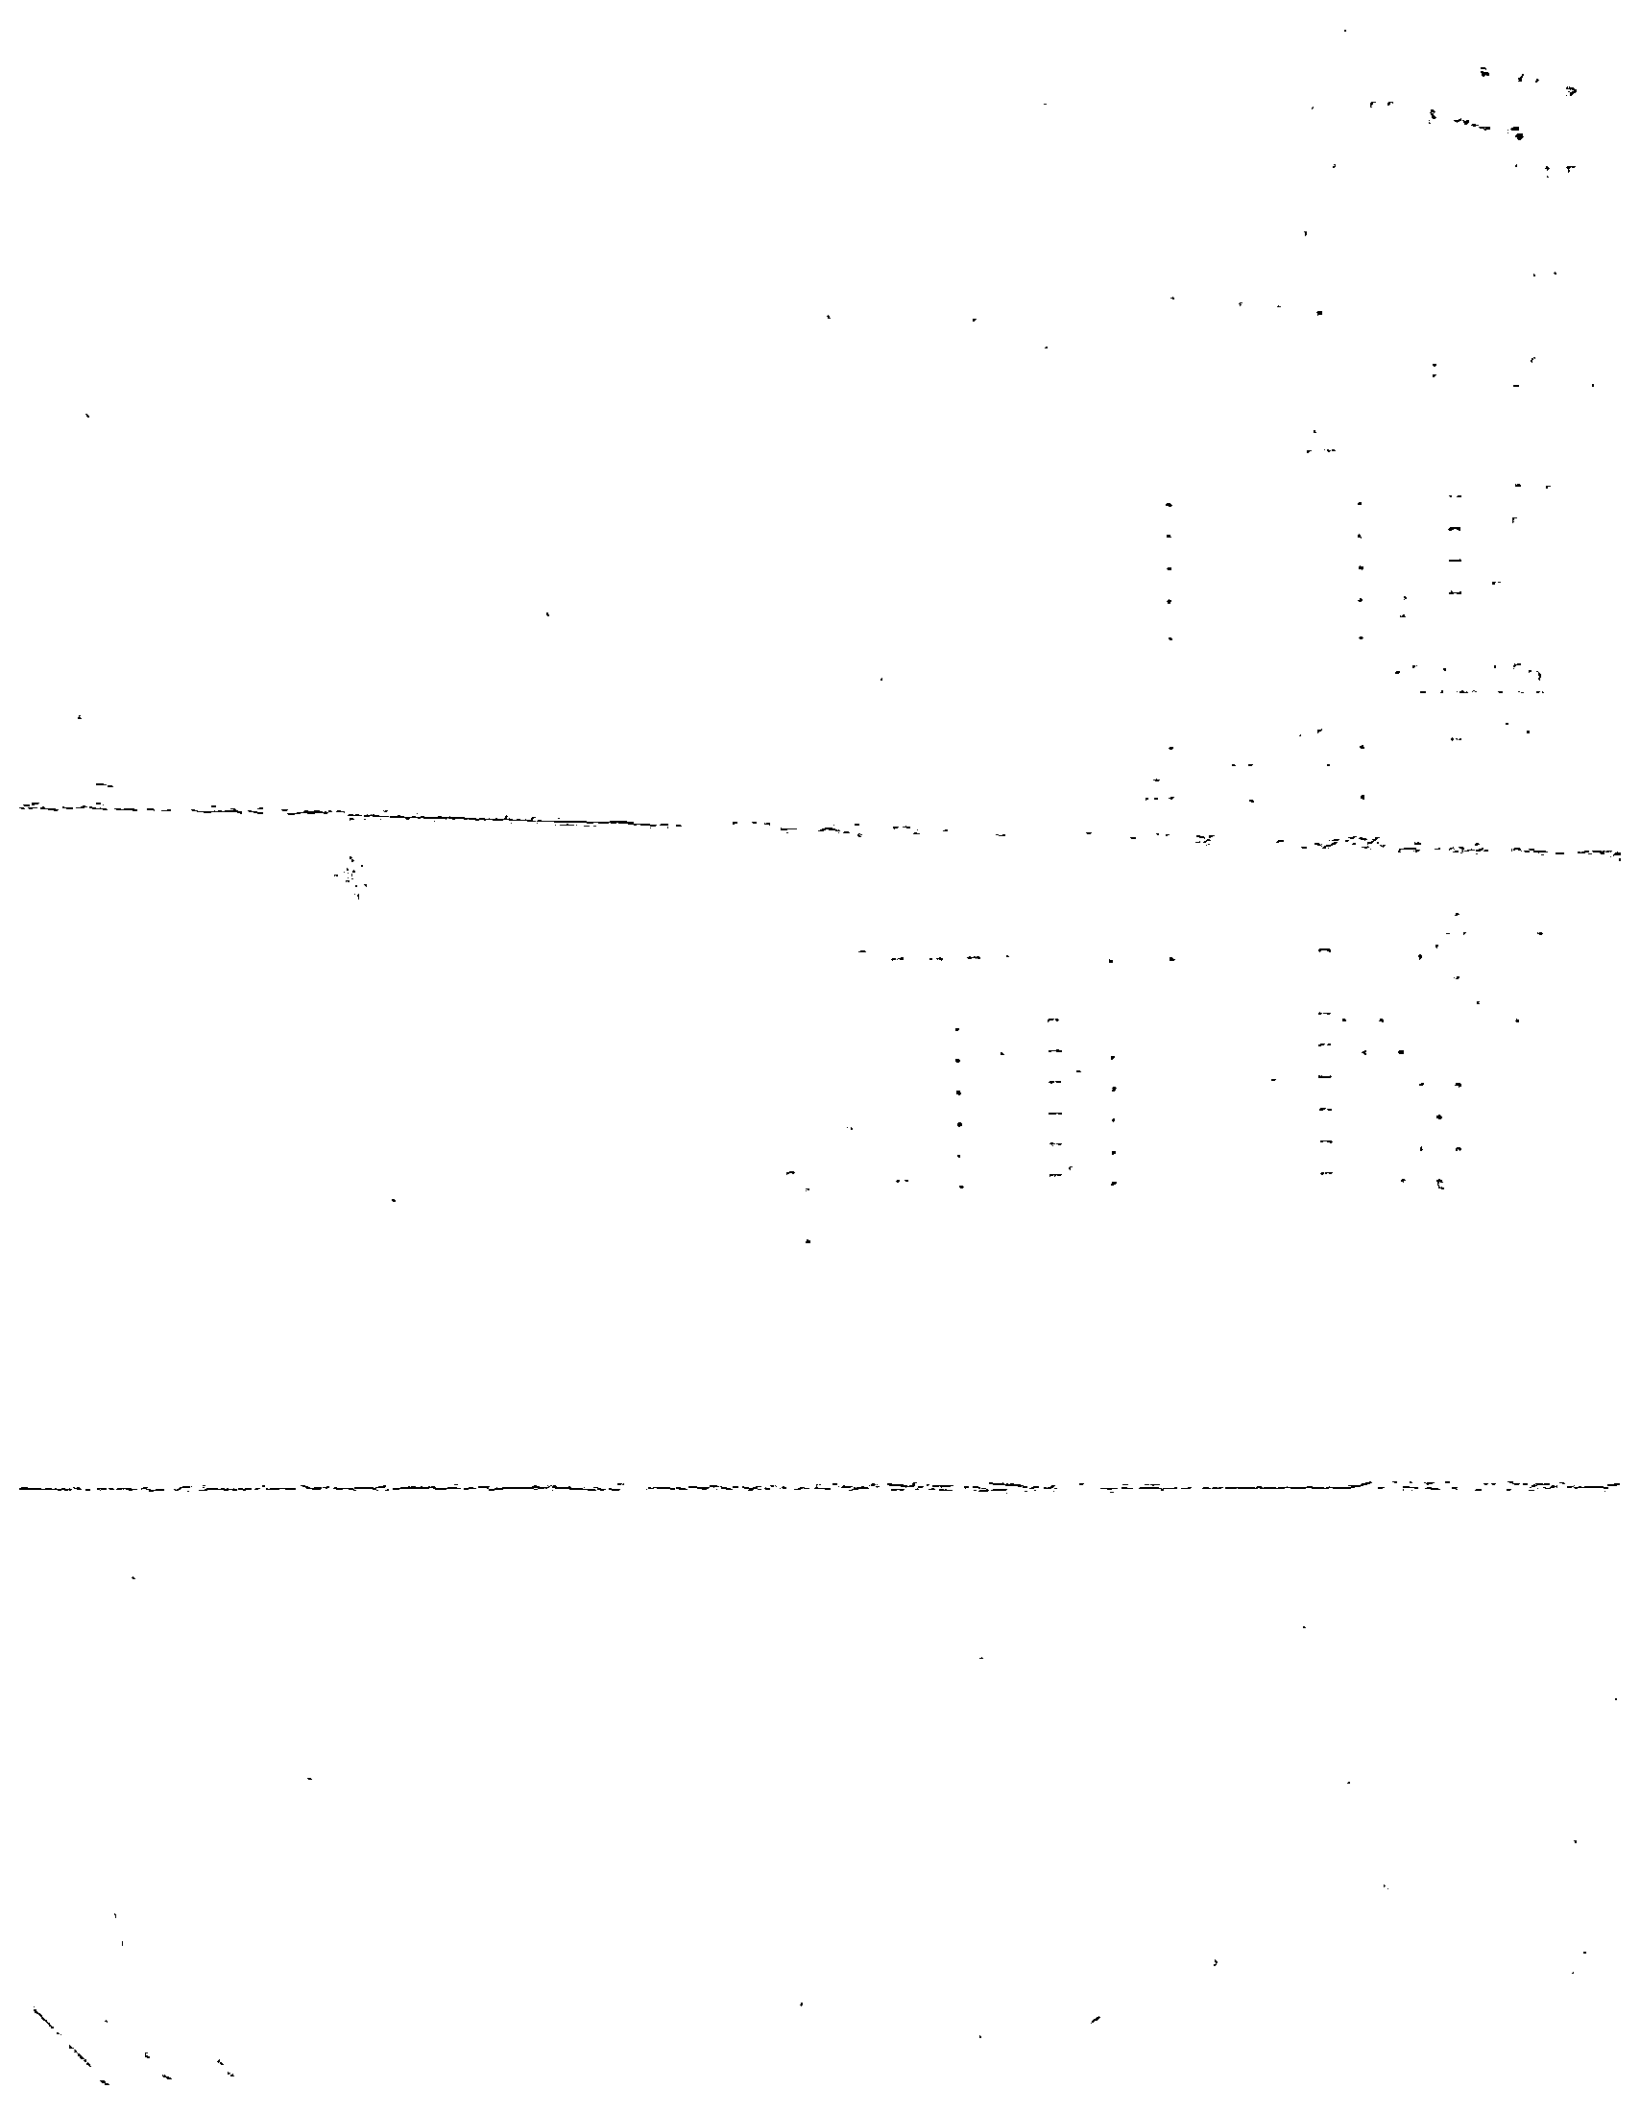

Division St. Secured ext.

81 ft. from the Center

line of water st. going

West to Manhole on Division

6-13 ft. lengths

1-3 ft. EL Bow

N.B. Housing Auth.

HRS.

24

Jesse Toranzo

24

Norbert ST. Riano

24

Joe Forrier

24

Jim Lemons

22

Joe Macedo

24

Tom Butte

2

Joe Tardin

HRS.

Lodge

Lodge

Lodge

#35-3-HRS.

#49-1-HRS.

11-1-1-HRS.

Completed
6/24/74

