

APPLICATION/AGREEMENT

For Trench/Disturbance Permit within the City of New Bedford

Permit # 375-2022Dig Safe# 20220803548Date: 2/23/2022

TO THE MAYOR AND CITY COUNCIL:

DISTURBANCE PERMIT/TRENCH SAFETY PERMIT

Permission is hereby requested to excavate the surface of: X City Property and/or X Private Property

Provide Sketch

Location of Work: 28 Alva St.Emergency Gas Leak RepairWork will begin (weather permitting) on: February 23, 2022Applicant Name: Kevin O'Sullivan (ra)

Excavator(s) Name: _____

Company Name: Eversource

Hoisting Equipment License Number: _____

Grade: _____ Expiration Date: _____

Contact Number: 508-441-5817

Name & Contact Number of Insurer: _____

Competent Person on Work Site: ON FILEAPPROVED BY: Stephen Cupfusa DATE: 9-11-22TITLE: Asst. City Engineer

This permit shall be posted at the work site, and shall remain until the work is completed. It is subject to inspection at all times.

Work completed prior to D.P.L. approval under
emergency work order for Class II LeakTrenches must be maintained
weekly until final paving is
completedROADWAY CLOSURES WILL REQUIRE
AUTHORIZATION FROM THE
COMMISSIONER OF PUBLIC
INFRASTRUCTURE. TRAFFIC MANAGEMENT
PLANS MAY BE REQUIRED.Permit only valid for three months
from date of approval

DigSafe/ CBYD Number	20220803548	PERMIT #		PROJECT #	GAS-EMGAS2Y	Unique ID :	7885849-10-[TC85]
ADDRESS:	28 ALVA ST	TOWN:	NEW BEDFORD	DATE:	02/23/22	WORK ORDER-	7885849-10
SHEET 18 of 33	LEAK REPORT #	Contractor:		LEAK CLASS		TYPE OF WORK:	GASMAINTENANCE
				WAMFWO:	30292378	WAMCITE #	879892

PIPE RETIREMENT

No

PIPE INSPECTION

FACILITY TYPE	MATERIAL	SIZE	EXT PIPE COND	INT PIPE COND	EXT CORR COND	INT CORR COND	COATING	DEPTH OF COVER
Main	Coated Steel	4	Fair	NA	Fair	NA	Fair	2'6"

PIPE INSTALL

FACILITY TYPE	MATERIAL	SIZE	LENGTH	PRESSURE	METHOD	OVERALL PIPE LENGTH	INSTALLED/ REPLACED	DEPTH OF COVER	CONNECTION AT MAIN	EFV INSTALLED	EFV SUBTYPE	EFV COMMENTS
								0'0"				

PRESSURE TEST

No

RESTORATION

CONSTRUCTION MATERIAL	LOCATION	EXISTING SURFACE FINISH	EXISTING DEPTH	LENGTH	WIDTH	REQUIRED DEPTH	TEMPORARY REPAIR ACTION	COMPACTION METHOD	% COMPACTED
Hot Asphalt	Street	Asphalt	4	12'0"	6'0"	4"	Same day Paving Contractor	DCP	95
Hot Asphalt	Street	Asphalt	4	9'0"	6'0"	4"	Same day Paving Contractor	DCP	95
Hot Asphalt	Street	Asphalt	4	8'0"	6'0"	4"	Same day Paving Contractor	DCP	95

MATERIALS

DESCRIPTION	TYPE	CATALOG ID	SIZE	Q.PLANNED	Q.USED	Unit of Measure	SERIAL NUMBER
Clamp	4				1		

DESCRIPTION OF WORK COMPLETED


Installed a clamp at 28 Alva St., New Bedford. We found corrosion on main and repaired

PERSONNEL

FOREMAN / WORKING LEADER / INSPECTOR

SIGNATURE:

EVERSOURCE									
DAILY ACTIVITY REPORT									
DigSafe/	20220803548	PERMIT #		PROJECT #	GAS-EMGASZY	Unique ID :	7885849-10- [TC85]	ADDRESS:	28 ALVA ST
CBYD Number		TOWN:	NEW BEDFORD	DATE:	02/23/22	ORDER-	7885849-10	URL:	http://CWV-CLKSOPRDI/Repository/Files/007_085001(CGOUNBO).jpg
SHEET 23		LEAK REPORT #		LEAK CLASS		TYPE OF WORK:	GASMAINTENANCE	Contractor:	
of 33				WAMFWO:	30292378	#	WAMCTE		
									879892

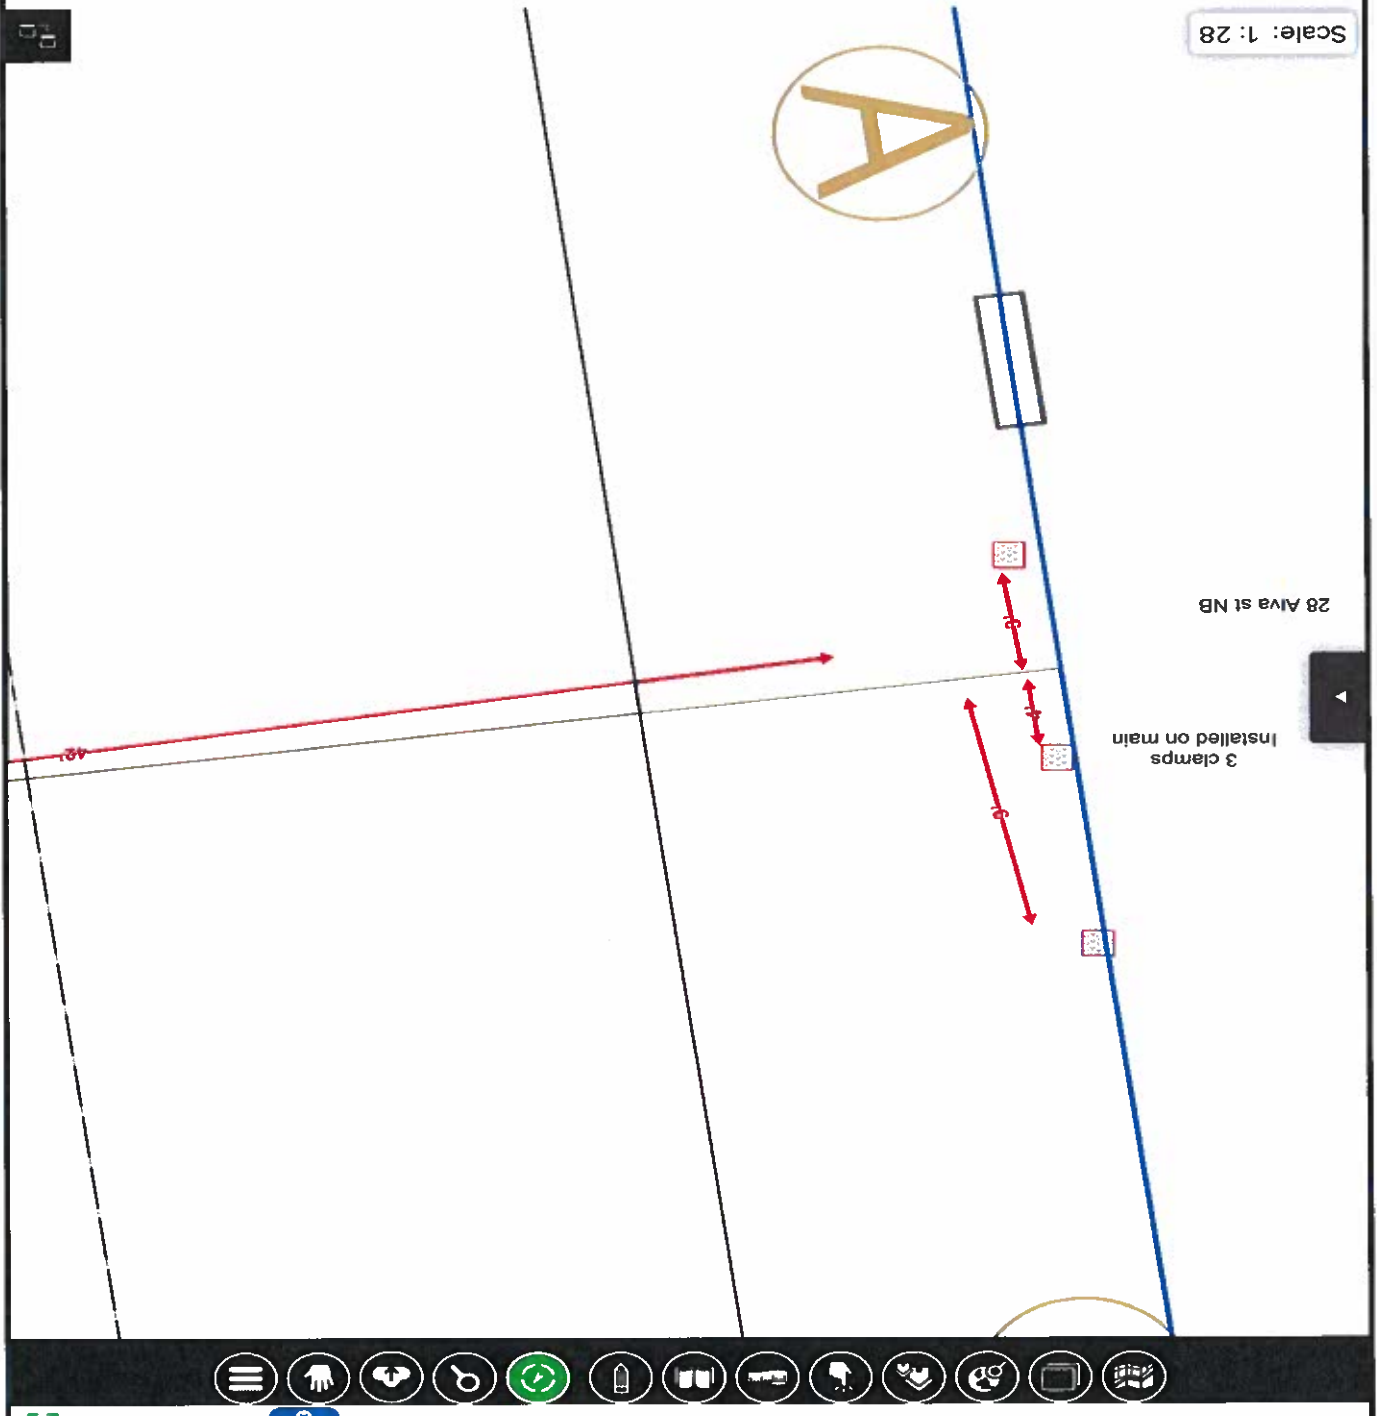

EVERSOURCE DAILY ACTIVITY REPORT									
DigSafe/ CBYD Number	20220803548	PERMIT #		PROJECT #	GAS-EMGAS2Y	Unique ID :	7885849-10- [TC85]	WORK ORDER- TASK:	7885849-10
ADDRESS:	28 ALVA ST	TOWN:	NEW BEDFORD	DATE:	02/23/22	WORK ORDER- TASK:	7885849-10	TYPE OF WORK:	GASMAINTENANCE
URL:	http://CWV-CLKSOPRD1/Repository/Files/006_084955(kMxmXTbx).jpg	LEAK REPORT #		LEAK CLASS		WAMFWO:	30292378	#	WAMCTE 879892
SHEET 25 of 33		Contractor:							

