

APPLICATION/AGREEMENT
For Trench/Disturbance Permit within the City of New Bedford

Permit # 394-2022
Dig Safe# 20221103381
Date: 03/15/2022

TO THE MAYOR AND CITY COUNCIL: DISTURBANCE PERMIT/TRENCH SAFETY PERMIT

Permission is hereby requested to excavate the surface of: X City Property and/or X Private Property
Provide Sketch

Location of Work: 88 Tinkham St
Working in street & street to building on Hathaway St
Emergency gas leak repair

Work completed prior to D.P.L. approval under
emergency work order for Class II Leak

Work will begin (weather permitting) on: March 15, 2022

Applicant Name: Kevin O'Sullivan (gk) Excavator(s) Name: _____ Permit only valid for three months
from date of approval

Company Name: Eversource Hoisting Equipment License Number: _____

Grade: _____ Expiration Date: _____

Contact Number: 508-441-5817 Name & Contact Number of Insurer: _____

Competent Person on Work Site: ON FILE

APPROVED BY: Stephen Cyprian DATE: 3-11-22
TITLE: Asst. City Engineer


This permit shall be posted at the work site, and shall remain until the work is completed. It is subject to inspection at all times.

ROADWAY CLOSURES WILL REQUIRE
AUTHORIZATION FROM THE
COMMISSIONER OF PUBLIC
INFRASTRUCTURE. TRAFFIC MANAGEMENT
PLANS MAY BE REQUIRED.

Trenches must be maintained
weekly until final paving is
completed

Gas metered installed within City
Layout. Must obtain an easement
from City of New Bedford for
this pedestrian obstruction of
path of travel.

EVERSOURCE										DAILY ACTIVITY REPORT											
DigSafe/CBYD Number		20221006979		PERMIT #		PROJECT #		GAS-ATSCRAZY		Unique ID : 4617772-10-[W178]		WORK ORDER-4617772-10		TASK:		TYPE OF WORK:		GASMAINTENANCE		SHEET 1 of 15	
ADDRESS:		88 TINKHAM ST		TOWN:		NEWBEDFORD		DATE:		03/10/22											
LEAK REPORT #				LEAK CLASS				WAMFWO:		30296123		WAMCTE #		884146							
Contractor:																					
FACILITY TYPE		Material		Size		EXT PIPE COND		INT PIPE COND		EXT CORR COND		INT CORR COND		COATING		DEPTH OF COVER					
Main		Cast Iron		6		Poor		NA		Poor		NA		Poor		3'0"					
PIPE INSTALL																					
FACILITY TYPE		Material		Size		Length		Pressure		Method		Overall Pipe Length		Installed/Replaced		Depth of Cover		Connection at Main		EFV Comments	
																0'0"					
PRESSURE TEST																					
MEDIUM		Type		Start Time		Start Pressure (PSIG)		Finish Time		Finish Pressure (PSIG)		Test Duration		Performed By		Soap Tested		Notes			
Air		Service below 200 ft		2022-03-10 14:05:00		100		2022-03-10 14:20:00		100		15min		Tyronne Edwards		Yes		From break at main to riser			
RESTORATION																					
CONSTRUCTION MATERIAL		Location		Existing Surface Finish		Existing Depth		Length		Width		Required Depth		Temporary Repair Action		Compaction Method		% Compacted			
Hot Asphalt		Street		Asphalt		4		8'0"		8'0"		4"				DCP		95			
Hot Asphalt		Sidewalk		Concrete		4		10'0"		3'0"		4"				DCP		95			
Hot Asphalt		Street		Asphalt		4		8'0"		3'0"		4"				DCP		95			
MATERIALS																					
No																					
DESCRIPTION OF WORK COMPLETED																					
Crew installed relayed service with 2" plastic from riser to main																					
PERSONNEL																					
FOREMAN / WORKING LEADER / INSPECTOR																					
SIGNATURE:																					

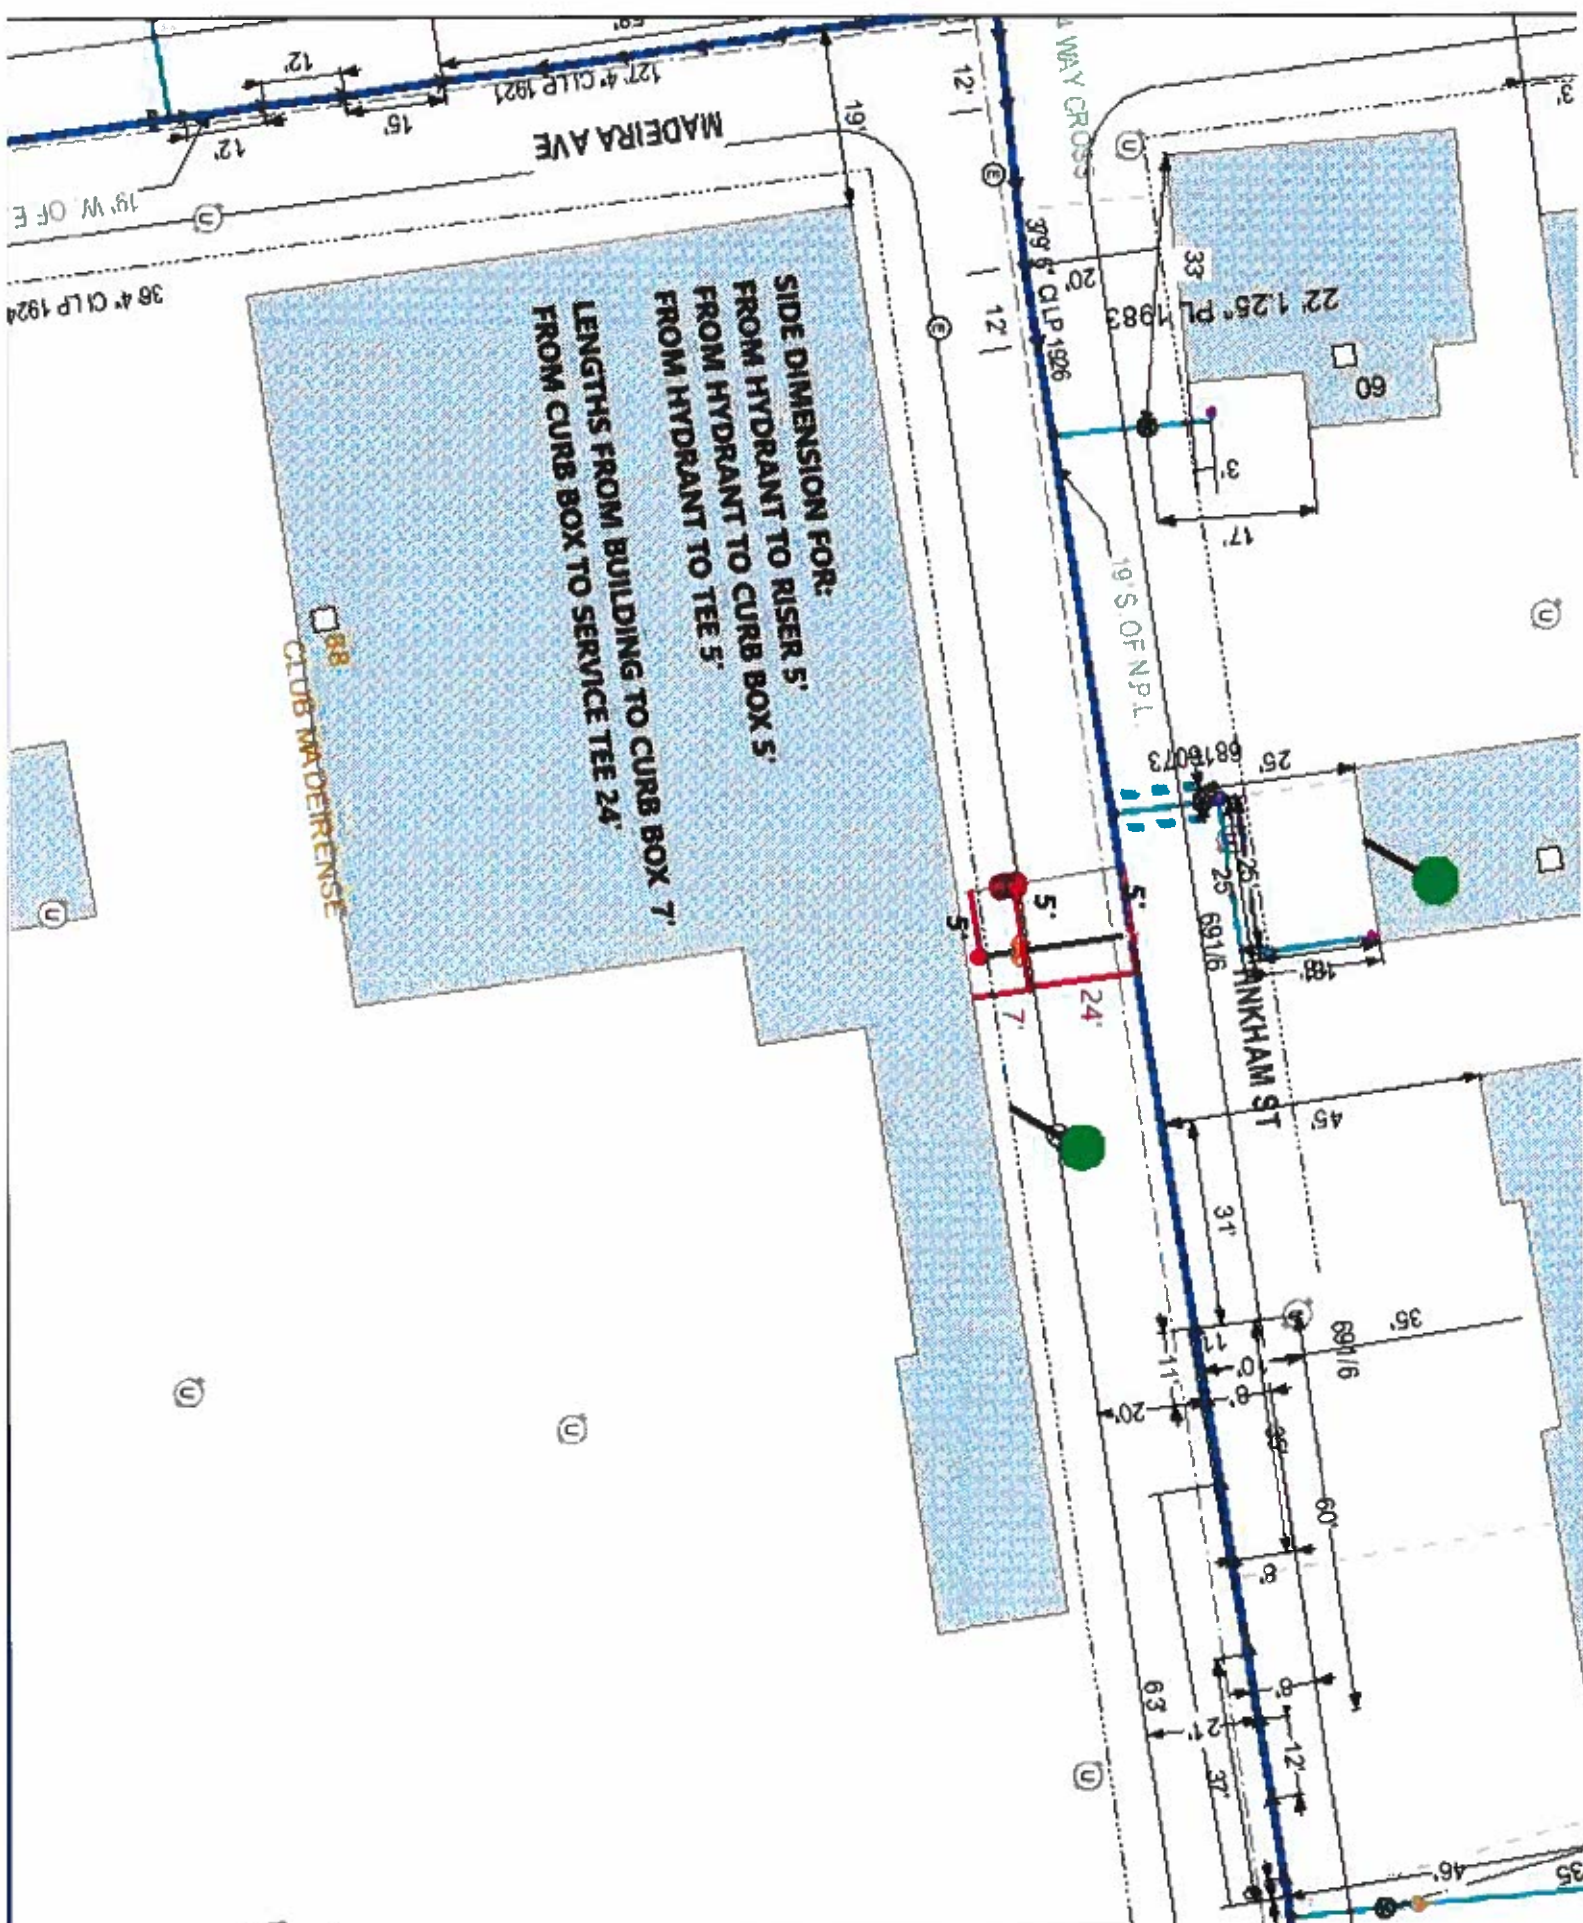

EVERSOURCE									
DAILY ACTIVITY REPORT									
DigSafe/	20221006979	PERMIT #		PROJECT #	GAS-ATSCRAZY	Unique ID :	4617772-10-	WORK ORDER-4617772-10	ADDRESS: 88 TINKHAM ST
Number		TOWN:	NEWBEDFORD	DATE:	03/10/22	WORK ORDER-4617772-10			
URL:	http://CWV-CLKSOPRD1/Repository/Files/cdv_photo_001_031917(06GCAKtp).jpg	LEAK REPORT #		LEAK CLASS		WORK: GASMAINTENANCE	WAMCTE#	884146	
SHEET 2 of 15		Contractor:		WAMFWO#	30296123				

3:06 PM Thu Mar 10
LTE (V) 81%

