

APPLICATION / AGREEMENT

For TRENCH PERMIT within the City of New Bedford

Permit #	802022
Dig Safe #	
Date Issued:	

This permit shall be posted at the work site and shall remain until the work is completed. It is subject to inspection at all times.

TO THE MAYOR AND CITY COUNCIL: ☒ TRENCH PERMIT

Permission is hereby requested to excavate the surface of: ☒ Private Property ☐ Unaccepted or private street

Location of work: 740 Belleville Ave

Substantially as per plan annexed, for the purpose of: install 3 New Storm Drains on Private Property

Work will begin (weather permitting) on: 8-29-2022

Work will end (weather permitting) on: 11-29-2022

Applicant Name: FORGEN LLC

Excavator(s) Name: Paul Mayo

Company Name: FORGEN LLC

Hoisting Equipment License Number: HE-188342
Grade: _____ Expiration Date: 11-25-22

Contact Name: Malik Shabug

Name & Contact Number of Insurer: _____

Approved By: Brandon Amador Date: 8/29/2022
Title: Admin Manager

Provide Sketch


Roadway closures will require authorization from the Commissioner of Public Infrastructure. Traffic management plans may be required. For inspection, 24-hour notice is required and the Contractor / Applicant is required to notify the D.P.I. @ 508-979-1550 Press 4 Repair. Permit Expires in 3 Months from work start date.

CATCH BASIN / MANHOLE DETAIL



NOT TO SCALE

NOTES

1. MINIMUM DEPTH OF SLUMP TO BE 2 FT.
2. REINFORCING STEEL, BASED ON A WALL THICKNESS OF 5".
3. FACE OF PIPE FLUSH OR NOT TO PROJECT MORE THAN 4" FROM FACE OF WALL ALONG CENTERLINE OF PIPE.
4. FOR DESCRIPTION MATERIALS AND CONSTRUCTION METHOD, SEE STANDARD SPECIFICATIONS.
5. ALL CONCRETE TO BE AIR ENTRAINED.

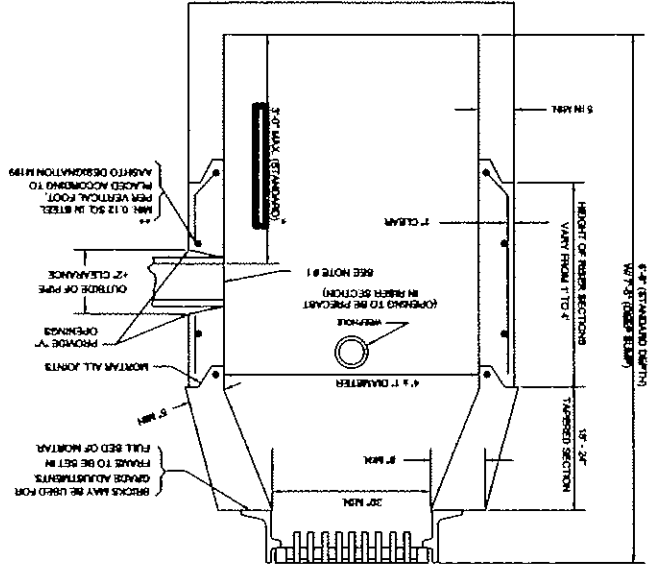

- ## NOTES
1. SITE BOUNDARY SHOWN AS DEPICTED ON EXHIBIT 3.
 2. COOPERATION & SETTLEMENT AGREEMENT, AEROVOX PROPERTY.
 3. BASED ON FIGURE FROM DEPARTMENT OF ARMY NEW ENGLAND DISTRICT CORPS OF ENGINEERS, DATED DECEMBER 2000, CURRENT RTN SITE BOUNDARY EXTENDS BEYOND AEROVOX PROPERTY.
 4. ALL INVERTS SHOWN ARE FOR PIPES. ALL SLUMPS SHALL BE 2'-0" BELOW PIPE INVERTS.
 5. ANY STORM SEWER MODIFICATIONS BEYOND THE EXTENT OF THE SHEETPILE BULKHEAD WALL IS ASSUMED TO BE DONE BY OTHERS.
 6. EXISTING STORM SEWER PIPE SHALL BE DEMOLISHED WHERE IN CONFLICT WITH PROPOSED STORM SEWER SYSTEM INSTALLATION. ALL OTHER PIPE SHALL BE FILLED WITH FLOWABLE FILL AND ABANDONED IN PLACE. ALL EXISTING CATCH BASINS AND MANHOLES SHALL BE DEMOLISHED DOWN TO TWO FEET BELOW EXISTING SURFACE. HOLES DRILLED THROUGH THE BASE SLAB CONCRETE AT 6" ON CENTER AND FILLED WITH CRUSHED STONE AND ABANDONED BENEATH.

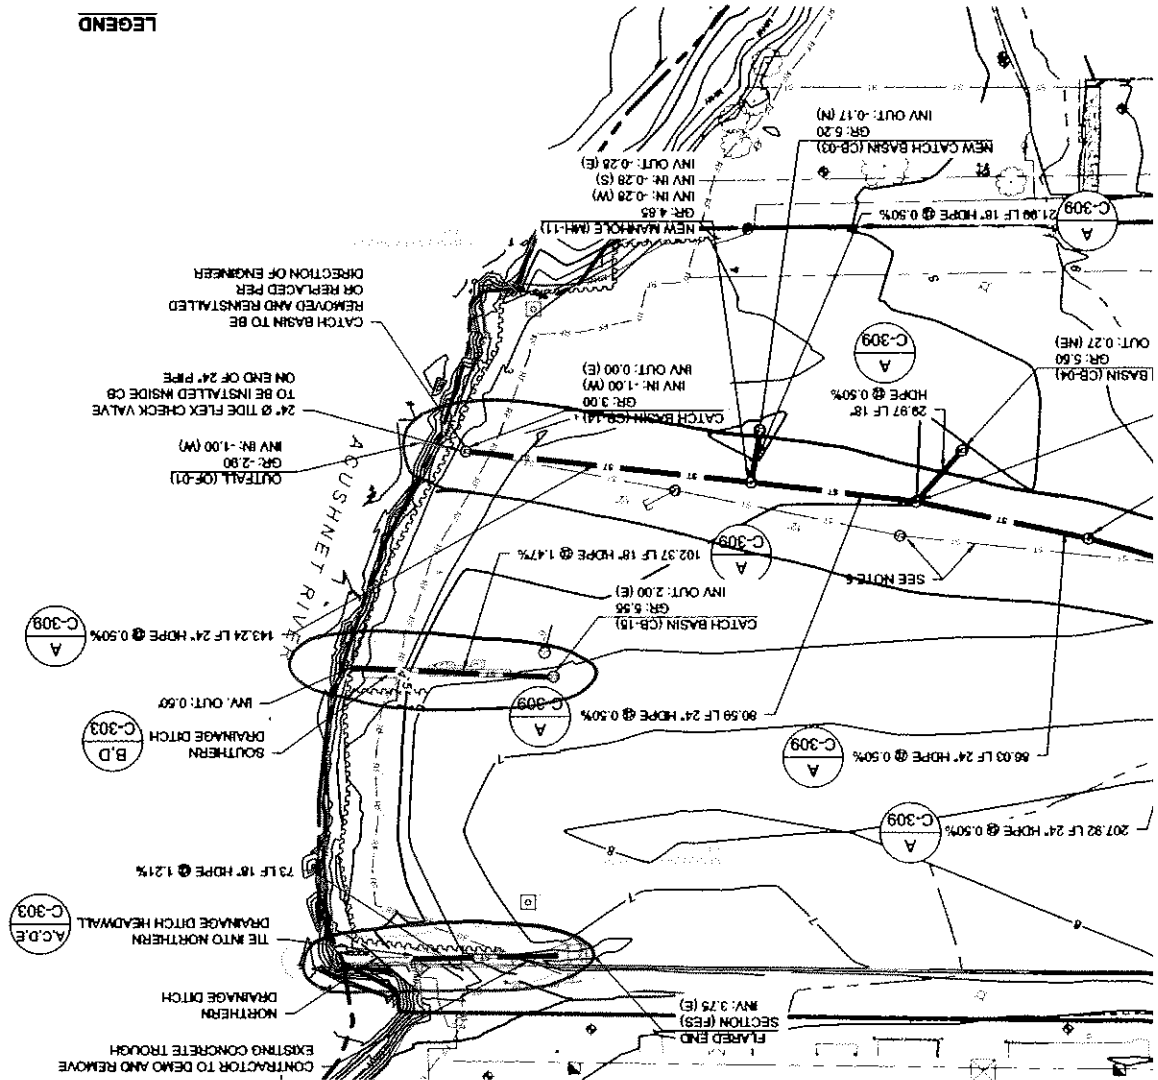

FORMER AEROVOX FACILITY
740 BELLEVILLE AVENUE
NEW BEDFORD, MA

ALAN R. KIRSCHNER
MA PROFESSIONAL ENGINEER
LIC NO. MA 32770

TAUNTON, MASSACHUSETTS
101 INDUSTRIAL PARK ROAD, SUITE 205



CIVIL
AEROVOX STORM SEWER MODIFICATIONS PLAN
DRAWING NUMBER C-309
SHEET NUMBER 24 OF 47

APPROVED: M. WADE
FILENAME: C-309.DWG
BC PROJECT NUMBER: 155041
CLIENT PROJECT NUMBER: 155041

CHECKED: K. DYSON
DRAWN: A. SANTAGO
DESIGNED: J. SPADT / B. PAULSEN
AT FULL SIZE
LINE 18.2 INCHES

REV	DATE	DESCRIPTION
1	7/10/20	ISSUED TO MANAGER
2	4/1/21	REVISED IN RESPONSE TO AERVOX COMMENTS
3	5/2/21	ISSUED FOR CONSTRUCTION
4	7/19/21	REVISIONS FOR DEMOLITION OF EXISTING CATCH BASIN
5	8/2/21	REVISIONS FOR DEMOLITION OF EXISTING CATCH BASIN
6	8/2/21	REVISIONS FOR DEMOLITION OF EXISTING CATCH BASIN
7	7/20/22	REVISIONS FOR DEMOLITION OF EXISTING CATCH BASIN

