

May 17, 1949

#22823


Laurent M. Lacourse  
W.S. Church St., S x Chaffee St.

Please install  $3/4$ " City Meter  
&  $3/4$ " Copper service to supply bungalow.  
Box on taker's land. Trench & box are

ready.  
21-20' trench dug by taker-52 ft. of  $3/4$ " cop. \$20.28--labor \$1.00

|                     |        |
|---------------------|--------|
| N x N Line Lynn St. | 1580.4 |
| E x W " Church St.  | 10.1   |
| S x N " House       | 2.7    |

1-Street cut 2'6" x 2' Tar  
Laid 5-18-1949

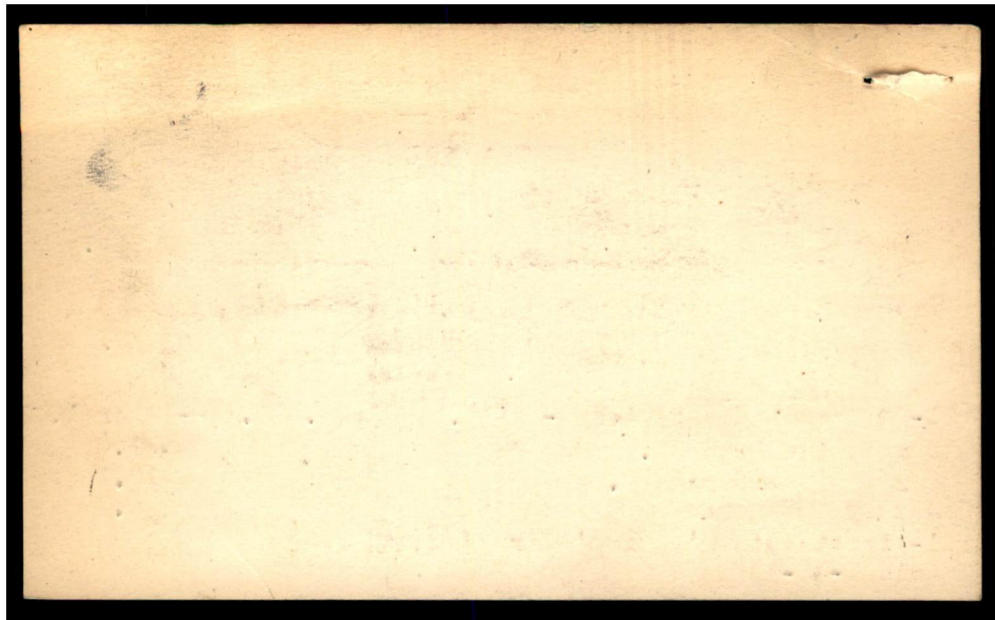

Service Repaired  
845 Church Street

22823

September 15, 1960

|                           |                       |     |
|---------------------------|-----------------------|-----|
| Installed 2nd. curb stop: | E x W line Church St. | 5.7 |
|                           | S x N " House         | 2.4 |
|                           | E x E " Fence         | 7.8 |

1-3/4" copper stop

The old stop is 4 ft. E x the new stop

Stock supplied and installed by Contractors,

Campanella and Cardì

Work done while widening Church Street

