


July 18, 1950

#23233

Walter Majka  
E.S. Church St., S x Brooklawn  
Ave.

Please install  $3/4$ " City Meter  
&  $3/4$ " Copper service to supply bungalow.  
Lay with drain. 20% agreement.

15-14--Laid with drain-29 ft. of $1/2$ " cop.	\$12.76-Labor	\$1.00
S x S Line Brooklawn Ave.		170.0
W x E " Church St.		8.6
S x S " House		2.3
Laid July 25-1950		

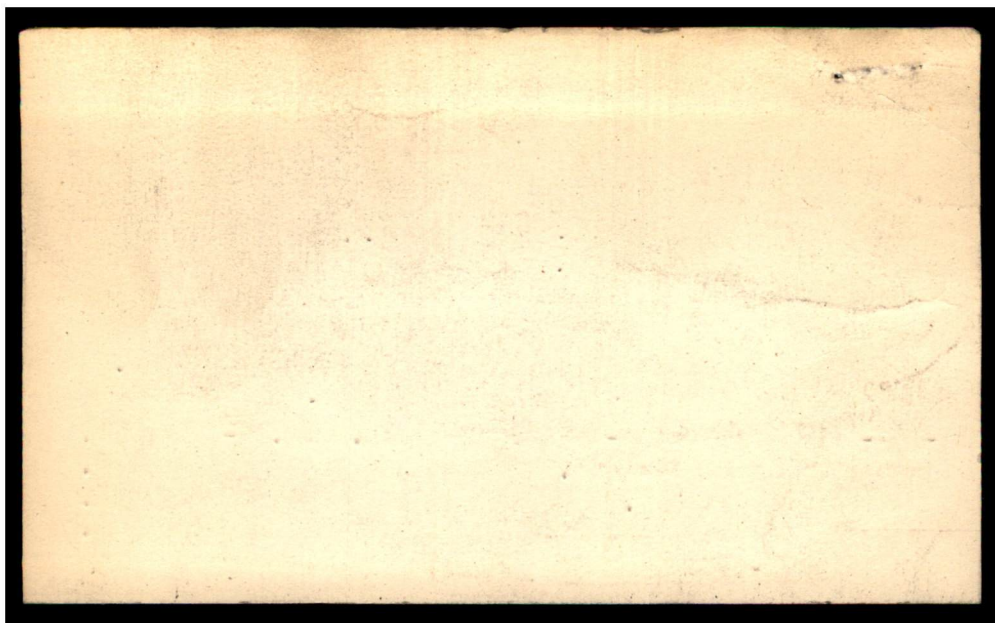

Service Repaired  
450 Church Street

23233 September 21, 1960

Installed 2nd. stop:	W x E line Church St.	5.2
	S x S " House	1.9
	W x W " House	30.4

1-3/4" copper stop, fig. 415

1 C. I. stop box standpipe

The old stop is 4 ft. W x the new stop  
Stock supplied and installed by Contractors,  
Campanella & Gardi

Work done while widening Church Street

