

127B

Sept. 17, 1951

#23613

Alfred Tetreault

E.S. Church St., N x Brockton St.

Please install $3/4$ " City Meter &
 $3/4$ " Copper service to supply cottage.

Will notify when trench is ready.

41-40--Trench dug by taker-18' of $\frac{1}{2}$ Cop \$8.64-Lab \$.75


N x N Line Brockton St. 34.4

W x E " Church St. 8.8

N x N " House 2.4

2 Street cuts: 2' x 4' & 15' x 2 $\frac{1}{2}$ ' Tarred Gravel

Work done October 2, 1951

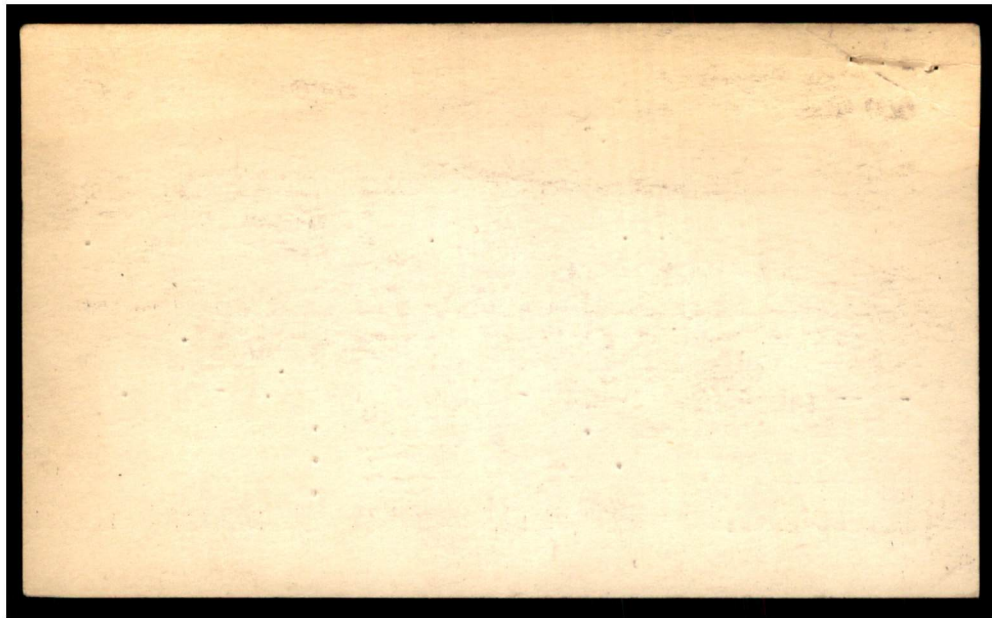

Service Repaired
640 Church Street

23613

September 12, 1960

Installed 2nd curb stop:	W x E line Church St.	6.0
	N x N " House	2.4
	W x W " House	22.0

1-3/4" copper stop, fig. 415

Old stop is 2.5 ft. W x new stop

Stock supplied and installed by Contractor,
Campanella and Cardi

Work done while widening Church St.

