

113

Oct. 15, 1951

#23631

Mrs. Catherine Warren

E.S. Church St., N x Carlisle St.

Please install 3/4" City Meter &
 3/4" Copper service to supply bungalow.
 Taker has 60' type K 3/4" copper and would
 like to use and be credited for. (trench dug)
 20% agreement.

Trench dug by taker - Labor \$1.00

N x N Line Carlisle St.

302.3


Church St.

9.0

S x N " House

8.3

Work done October 16, 1951

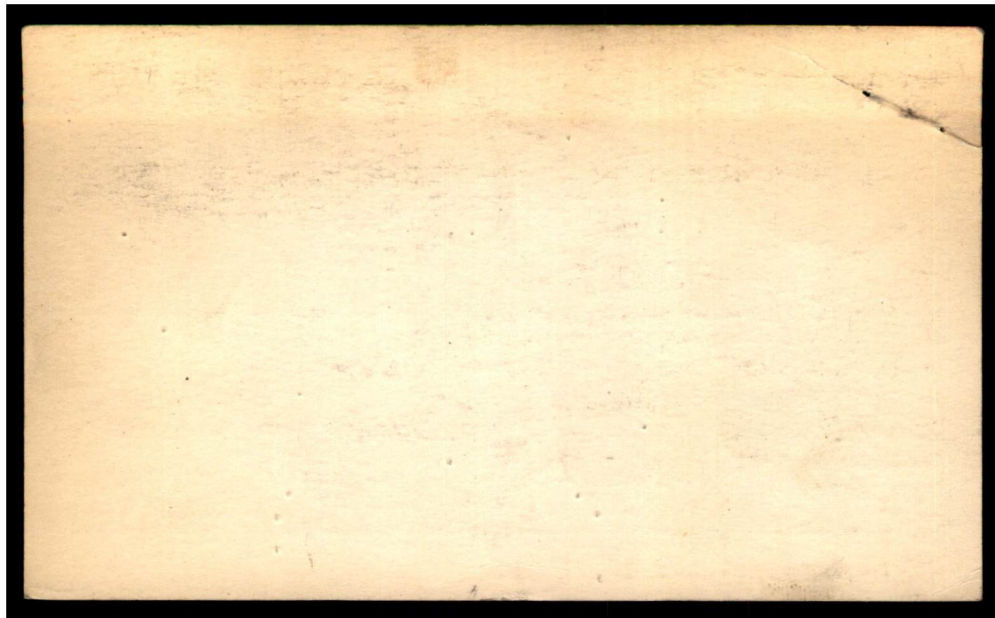

Service Repaired
424 Church Street

23631

September 21, 1960

Installed 2nd. curb stop:	S x N line house	8.7
	W x E " Church St.	4.4
	W x house	29.1

1-3/4" copper stop, fig. 415

1-stop box standpipe

The old stop is 5 ft. W x new stop.

Stock supplied and installed by Contractors,
Campanella & Carli

Work done while widening Church Street.

