

March 9, 1953

127B

23958 Albert Labonte
E. S. Church St., N. x Lynn St.

Please install $3/4$ " City Meter and
 $3/4$ " Copper Service to supply hunga-
low. Lay with drain.

41-40-Laid with drain-22' of $3/4$ " cop \$12.98-Lab \$.75


N x N Line Lynn Street 100.5

W x E " Church Street 11.0

N x S " House 1.2

1 Street cut: 2' x 4' Pen. Mac.

Work done June 25, 1953

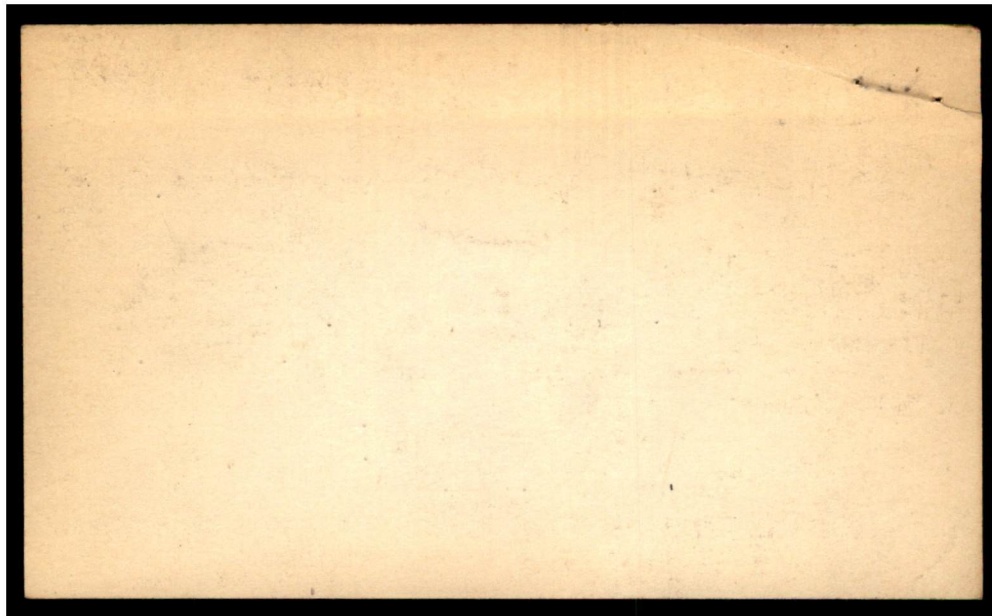

Service Repaired
704 Church Street

23958

September 15, 1960

Installed 2nd curb stop:	W x E line Church St.	6.0
	N x S " House	1.2
	W x W " House	25.8

1-3/4" copper stop, fig. 415

The old stop is 5 ft. W x the new stop

Stock supplied and installed by Contractor,

Campanella and Cardì

Work done while widening Church St.

