


Oct. 6, 1953

#24166 Joseph Topolewski
W.S. Turner St., S x Mt. Vernon St.

Please install $3/4$ " City Meter &
 $3/4$ " Copper service to supply bungalow. Main
to be extended about 50'. Box on taker's
land.

19-18-Trench dug by taker- $3\frac{1}{2}$ ' of $3/4$ Cop	\$2.07-no labor
S x S line Mt. Vernon Street	78.1
E x W " Turner Street	8.4

Work done October 27, 1953

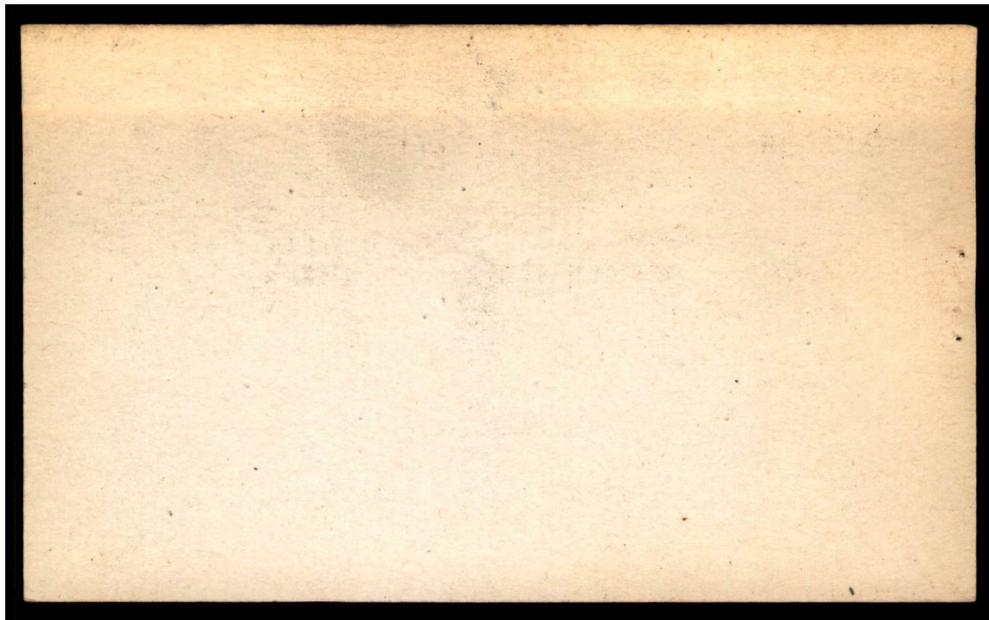

Service Extended

April 21, 1954

W. S. Turner St., S x ~~Wt. Pleasant Street~~

Joseph Topolewski

Wt. Vernon St.

Service #24166 - 3/4" was extended from meter box
inside property line to inside cellar
15 ft. of 3/4" copper tubing type K, soft

