

#282 Oct. 9, 1953

#24170

Mary Corga

E. S. Church St., S x Carlisle St.

Please install 3/4" City Meter &
3/4" Copper service to supply bungalow. 20%
agreement. Main pipe to be laid. Labor....\$2.00


15-14-Excavation (moto-crane)\$5.00-14' of 3/4 Cop \$8.26

S x S Line Carlisle Street 169.6

W x E " Church Street 5.6

S x N " House 3.2

Work done Oc tober 13, 1953

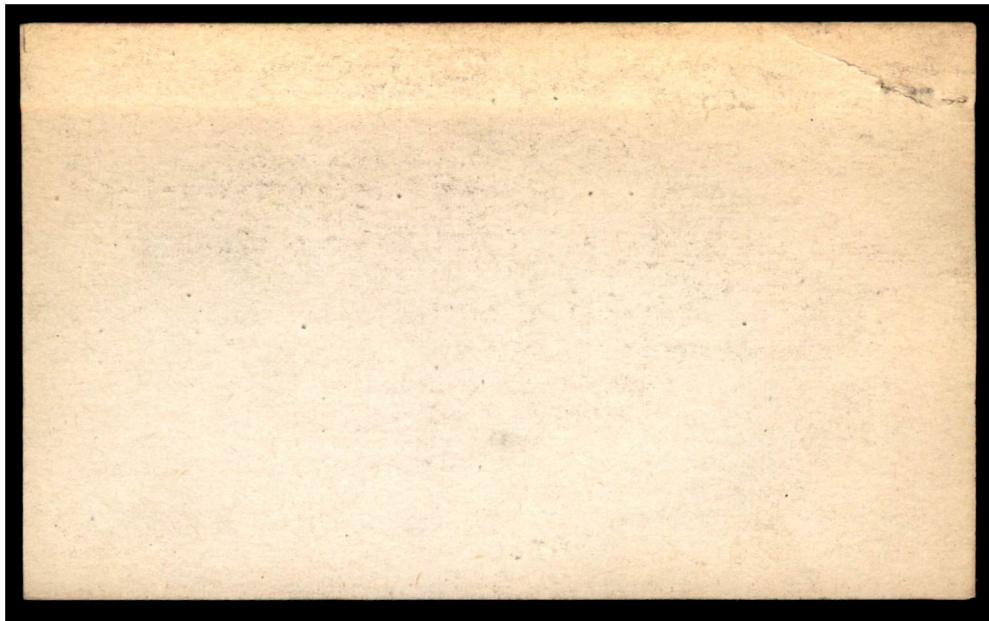

Service Repaired
382 Church Street

241 70

September 21, 1960

Installed 2nd. curb stop:	S x N line house	2.4
	W x E " Church St.	5.6
	W x house	17.3

1-3/4" copper stop, fig. 415

1-stop box standpipe.

Old stop is 3 ft. W x new stop.

Stock supplied and installed by Contractors,
Campanella & Cardé.

Work done while widening Church Street.

