

APPLICATION No.: 10868

TAP CLEARED

LOCATION: 1199 Cove Road

OWNER: ✓

31-313

MEASURES: 1" Copper Service

06/27/2019 Lead Service Line Replacement Program

Phase 1, Contractor P Gioioso & Son

Type CU, Diameter (in) 1, Water Pressure 100

Distance from main to curb stop (ft) N/A

Distance curb stop to meter (ft) 100

Distance from curb face to curb stop (ft) 1

Depth of service (ft) 5

Total Length of new pipe installed (ft) 100

Curb stop replaced: no, corporation replaced: no

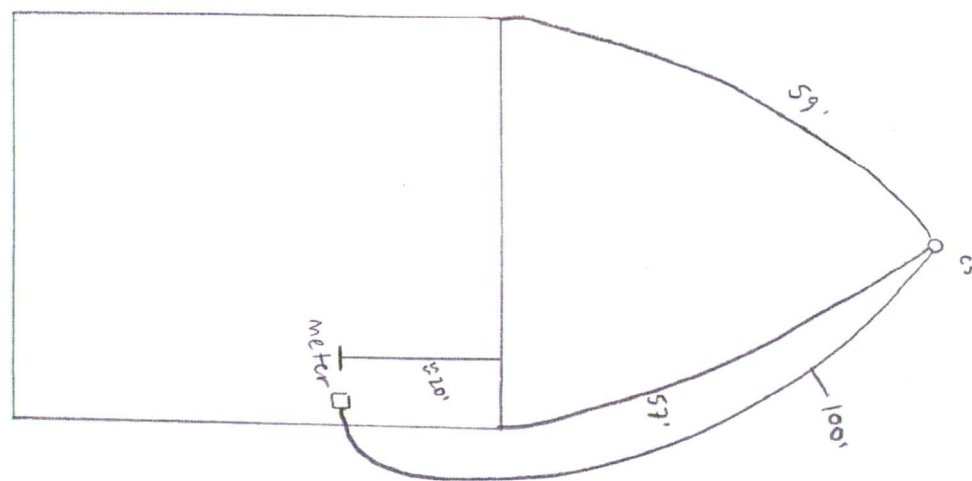
Ball valve furnished: yes, size 1"

DATE

BEF.

AFT.

REMARKS

[illegible]

APPLICATION No.: 10868

TAP CLEARED

LOCATION: 1199 Cove Rd.

OWNER: Joseph Souza Et. Ux

MEASURES: 3/4" Copper Sept. 9, 1904

W from County St. 362.6 ft.

S from N line Cove Rd. 5.5 8.0 ft.

W from E line house 7.7 ft.

Nov. 20, 1950 New from 3 ft. inside of property to meter

✓ 3/4" copper tubing

(Material installed and furnished by owner's plumber)

October 29, 1974 Renewed from the main to a point 4½ ft.
inside curb stop.

✓ 15 ft. - 3/4" Copper tubing 3/4" Curb Stop

5/8" lead to copper adaptor 3/4" x 1" Fig. 413

XXS

Caldwell Stop Box

Contractor supplied all stock except Stop Box

Due to the widening of Cove Rd. the curb stop was
relocated 2½ ft. northerly.

- - -

[illegible]

CHARGE OUTS

[illegible]

APPLICATION No.: 11392C 5/8"

TAP CLEARED

LOCATION: Rear 1199 Cove Rd.

OWNER:

MEASURES: 5/8"
Conn. of Appli. #10869 made by owner

DATE

BEF.

AFT.

REMARKS

[illegible]
