

APPLICATION No.: 15200

LOCATION: 95 - 97 Highland St

TAP CLEARED

OWNER:

31-313

MEASURES: W X Highland St 13.0 ft
N X S Line Mt. Vernon St 7.0 ft
W X E Line House 7.0 ft

1" Copper service

07/02/2019 Lead Service Line Replacement Program
Phase 1, Contractor P Gioioso & Son

Distance from main to curb stop (ft) 10

Distance from curb stop to meter (ft) 15

Distance from curb face to curb stop (ft) 1

Depth of service (ft) 4

Total length of new pipe installed (ft) 25

Curb stop replaced: yes size 1"

Corporation replaced: yes size 1"

Ball valve furnished: yes size 1"

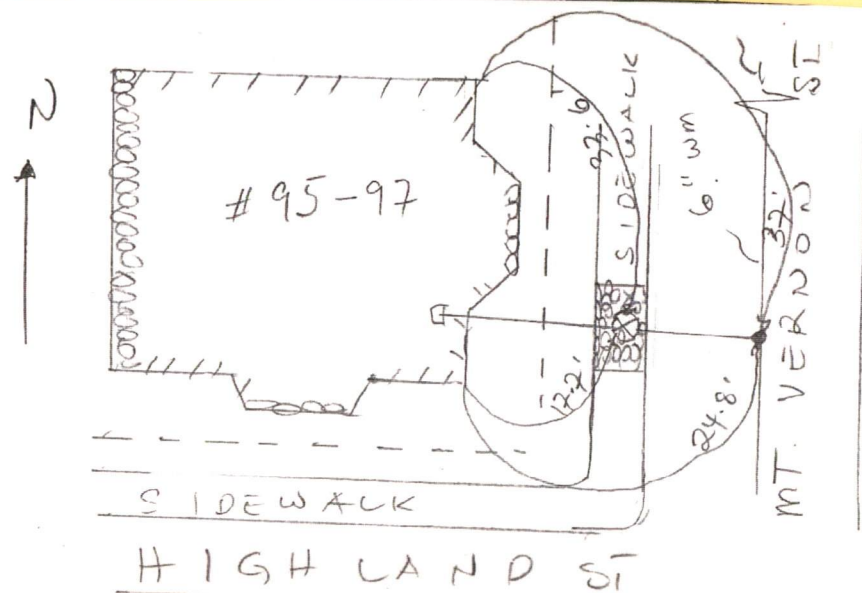
DATE

BEF.

AFT.

REMARKS

11/13/68 Ream

[illegible]

APPLICATION No.: 15200

TAP CLEARED

LOCATION: ⁹⁵ Highland S.W. Cor. Mt. Vernon

OWNER: _____

MEASURES: 3/4"

W from	Highalnd	13.0 ft.
N from S line	Mt. Vernon	7.0 ft.
W from E line	House	7.0 ft.

DATE

BEF.

AFT.

REMARKS



[illegible]

CHARGE OUTS

[illegible]
