


APPLICATION No.: 19117

TAP CLEARED

LOCATION: 103 - 5 Clara St

OWNER: 

31-313

MEASURES:

09.04.2019-Lead Service Line Replacement Program
Phase 1

Contractor: P. Gioioso and Sons

Type Cu, Diameter (in) 1, Water Pressure 100

Distance from main to curb stop (ft) 25

Distance curb stop to meter (ft) N/A

Distance from curb face to curb stop (ft) 2

Depth of Service (ft) 4.8

Total length of new pipe installed (ft) 25

Curb stop replaced: Yes, Size 1"

Corporation replaced: Yes, Size 1"

Ball Valve furnished: No

DATE

BEF.


AFT.

REMARKS

METER HISTORY

CHARGE OUTS

DATE	SET OUT	SIZE	MAKE	NUMBER	READING	TEST			REMARKS

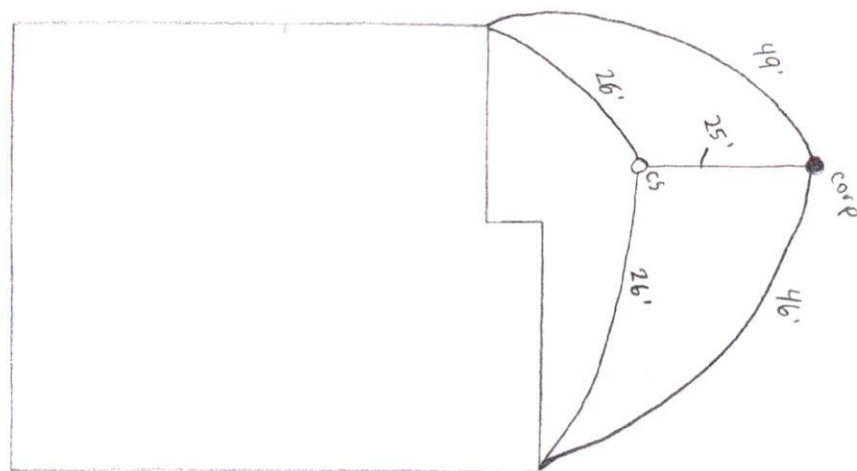

APPLICATION No.: 19117

TAP CLEARED 12-3 86491637

LOCATION: 103-5 Clara St.

OWNER: John F. Pacheco

MEASURES: 3/4" Copper Dec. 2, 1922

E from Cleveland St. 278.0 ft.

S from N line Clara St. 8.9 ft.

W from E line house 10.6 ft.

July 16, 1962 Renewed from curb stop, to meter inside bldg.
 29 ft. of 3/4" copper tubing type K, soft
 1 lb. of wiping solder.
 1 sidewalk cut: 10' x 5' cement
 125 compressor: 1 hr.

Abraham
 Fernandes

12/4/86: Renewed from curb stop to a point 4 ft. outside
 Stock: 5ft. 3/4" copper tubing 2-3/4" curb stop 1-Caldwell stop
 box 1-3/4x5/8 lead to cop adapt. xxs.
 =====

[illegible]
