

APPLICATION No.: 6898

TAP CLEARED

LOCATION: 124 Cove St

OWNER: V

31-313

MEASURES: Aug 25, 1891

E X French Ave 104.4 ft

N X S line Cove St 7.4 ft

W X E line House 7.1 ft

1" Copper Service

3/25/2019 Lead Service Line Replacement Program

Phase 1, Contractor P. Gioioso & Son

Type CU, Diameter (in)1, Waterpressure 100

Distance from main to curb stop (ft) 8

Distance from curb stop to meter (ft) 17.7

Distance from curb face to curb stop (ft) 1.3

Depth of service (ft) 3.5

Total length of new pipe installed (ft)17.7

Curb stop replaced: no, size 3/4"

Corporation r eplaced 3/4"

Ball Valve furnished: yes size 1"

Remarks: 1-3/4" union installed 1lf outside curb stop

DATE

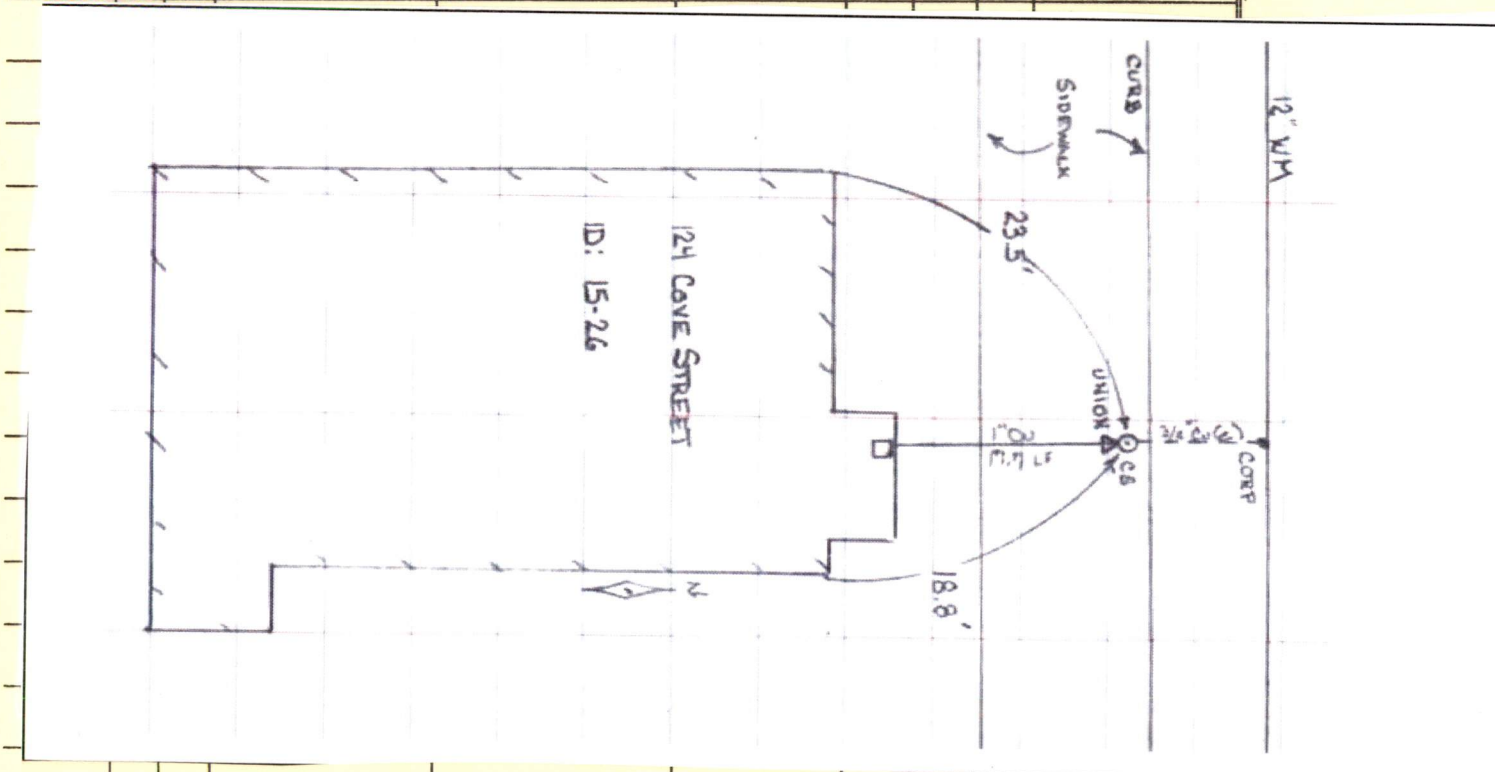
BEF.

AFT.

REMARKS

[illegible][illegible]

CHARGE OUTS

[illegible]
