

7256

LOCATION: 41 Winsor St

OWNER:

31-313

MEASURES:	W X County St	380.8 ft
	S X N Winsor St	7.7 ft
	W X E House	11.6 ft

1" Copper Service 7/16/2019

Lead Service Line Replacement Program

Phase 1, Contractor P Gioioso & Son

Type Cu, Diameter 1in, Water pressure 100

Distance from main to curb stop (ft) 25

Distance from curb stop to meter (ft) 19

Distance from curb face to curb stop (Ft) 2.1

Depth of service (ft) 3.8

Total length of new pipe installed (ft) 19

Curb stop replaced: No size 3/4"

Corporation replaced" No size 3/4"

Ball valve replaced: Yes size 1"

Remarks: new tap at main, exisiting corp abandoned

1-3/4" union installed 1ft outside curb stop

TAP CLEARED

DATE _____

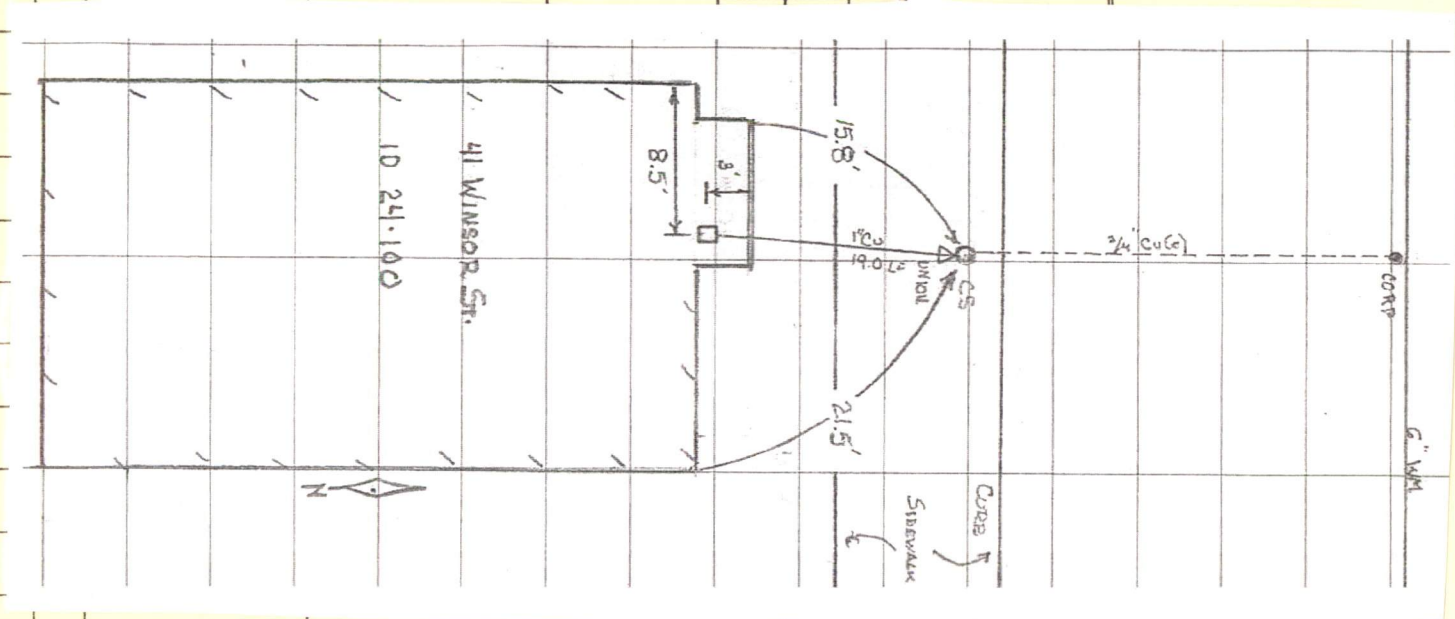
BEF.

AFT.

REMARKS

4/27/1982 Ream

8/4/1998

[illegible][illegible][illegible]
