

✓
LOCATION: 39 Independent St

APPLICATION No.: 8586

TAP CLEARED

OWNER:

31-313

MEASURES: 1" Copper Service

05/09/2019 Lead Service Line Replacement Program

Phase 1, Contractor P Gioioso & Son

Type CU, Diameter 1in, Water pressure 100

Distance from main to curb stop (ft) N/A

Distance from curb stop to meter (ft) 20

Distance from curb face to curb stop (ft) 1

Depth of service (ft) 4

Total length of new pipe installed (ft) 20

Curb stop replaced: No size 3/4"

Corporation replaced: No size 3/4"

Ball vavle furnished: yes size 1"

DATE

BEF.


AFT.

REMARKS

METER HISTORY

CHARGE OUTS

DATE	SET OUT	SIZE	MAKE	NUMBER	READING	TEST		REMARKS

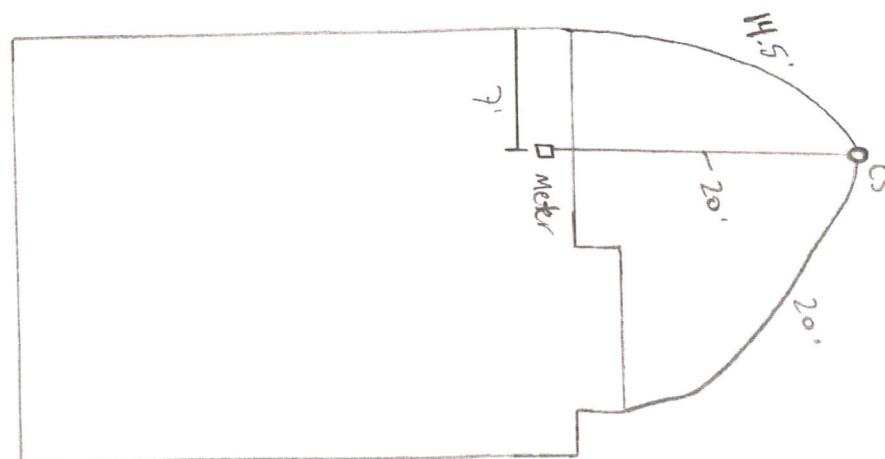

APPLICATION No.: 8586

TAP CLEARED

LOCATION: 39 Independent St.

OWNER: Anibal Medeiros Et Ux

MEASURES: 1/2"

H lead

May 22, 1896

E from

Crapo St.

436.2 ft.

S from N line

Independent St.

8.8 ft.

W from E line house

6.5 ft.

11/15/77: Renewed 6" outside to 6 1/2 ft. inside of line.
7 ft. - 3/4" copper; 3/4" curb stop; 2-5/8" x 3/4" lead to
cop. adapt. XS; Caldwell stop box;

Sept 6, 1996: Renewed from main to curb stop
Stock: 22ft 3/4" copper tubing 1-3/4" curb stop
1- Caldwell stop box 1-3/4x5/8 Fig 413

=====

DATE

BEF.

AFT.

REMARKS

9/6/96

963605195

9/6/96: tap reamed

[illegible]

CHARGE OUTS

[illegible]
