

wednesday 11:00 AM
cut + cap:

APPLICATION/AGREEMENT

For Trench/Disturbance Permit within the City of New Bedford

Permit # 115-16
Dig Safe # 20161500840

Date 4-11-16

TO THE MAYOR AND CITY COUNCIL: DISTURBANCE PERMIT/TRENCH SAFETY PERMIT

Permission is hereby requested to excavate the surface of: ✓ City Property and/or ✓ Private Property
Provide Sketch

Location of Work: 106 James Street
Service # 33871 F.S. # 33872

ROADWAY CLOSURES WILL REQUIRE
AUTHORIZATION FROM THE
COMMISSIONER OF PUBLIC
INFRASTRUCTURE. TRAFFIC MANAGEMENT
PLANS MAY BE REQUIRED.

Substantially as per plan annexed, for the purpose of: water service + fire supply
installation

FOR INSPECTION ONLY A 24 HOUR
NOTICE IS REQUIRED AND THE
CONTRACTOR/APPLICANT IS
REQUIRED TO NOTIFY THE D.P.I.
@ 508 979-1550 Press 3 Repair

Work will begin (weather permitting) on: 4/13/16

Work will end (weather permitting) on: 7/13/16

Applicant Name: Eric Smith Excavator(s) Name: on file


Company Name: WC Smith & Son Hoisting Equipment License Number: HE-039659
Grade: 2A Expiration Date: 12-13-16

Contact Number: 508-995-1449 Name & Contact Number of Insurer: Sylvia Company Insurance
508-995-4553

Competent Person on Work Site: Eric Smith APPROVED BY: Dennis M. Amadio DATE: 4/11/16
TITLE: Chief of the Works

This permit shall be posted at the work site, and shall remain until the work is completed. It is subject to inspection at all times.

56789



Department of Public Infrastructure

Ronald H. Labelle
Commissioner

Water
Wastewater
Highways
Engineering
Cemeteries

CITY OF NEW BEDFORD
Jonathan F. Mitchell, Mayor

NEW WATER SERVICE

DATE OF INSPECTION: 4 14 16 TIME OF INSPECTION: _____

CONTRACTOR: Eric Smith CONTACT # _____

LOCATION: 106 James LOT # _____ SERVICE # 33872

SIZE OF SERVICE: 4" KIND OF PIPE: Ductile

FOREMAN SIGNATURE: _____

NEAREST STREET TO BOX	<u>N x N</u>	<u>Line</u>	<u>Union St</u>	<u>131</u>
OTHER LOCATION TO BOX				
PROPERTY LINE TO BOX	<u>W x E</u>	<u>Line</u>	<u>James</u>	<u>23.5</u>
CORNER OF BUILDING TO BOX	<u>N x S</u>	<u>Line</u>	<u>Build</u>	<u>77</u>
CORNER OF BUILDING TO BOX	<u>S x N</u>	<u>Line</u>	<u>Build</u>	<u>3</u>
HOUSE TO BOX	<u>W x W</u>	<u>Line</u>	<u>Build</u>	<u>23.5</u>
MAIN TO PROPERTY LINE				<u>24'</u>
PIPE INSIDE PROPERTY				<u>4'</u>
MEASUREMENTS OF DUCTS OR CABLES				

REMARKS: _____



Department of Public Infrastructure

Ronald H. Labelle
Commissioner

Water
Wastewater
Highways
Engineering
Cemeteries

CITY OF NEW BEDFORD
Jonathan F. Mitchell, Mayor

NEW WATER SERVICE

DATE OF INSPECTION: 4-14-16 TIME OF INSPECTION: _____

CONTRACTOR: Eric Smith CONTACT # _____

LOCATION: 106 James LOT # _____ SERVICE # 33871

SIZE OF SERVICE: 1" KIND OF PIPE: Copper

FOREMAN SIGNATURE: _____

NEAREST STREET TO BOX	<u>N x N line Union</u>	<u>130'</u>
OTHER LOCATION TO BOX		
PROPERTY LINE TO BOX	<u>W x E line James</u>	<u>7'</u>
CORNER OF BUILDING TO BOX	<u>N x S line Build</u>	<u>76'</u>
CORNER OF BUILDING TO BOX	<u>S x N line Build</u>	<u>4'</u>
HOUSE TO BOX	<u>W x W line Build</u>	<u>7'</u>
MAIN TO PROPERTY LINE		<u>25'</u>
PIPE INSIDE PROPERTY		<u>4'</u>
MEASUREMENTS OF DUCTS OR CABLES		

REMARKS: _____



Department of Public Infrastructure

Ronald H. Labelle
Commissioner

CITY OF NEW BEDFORD
Jonathan F. Mitchell, Mayor

WATER SERVICE REPORT

Water
Wastewater
Highways
Engineering
Cemeteries

FOREMAN'S NAME: Percy DATE: 4-14-16

LOCATION: 106 James SERVICE # 18079

1. How did you find out about this break or leak? What time was it? _____

2. What time was service shut down? was off

3. What time was service turned back on? _____

4. What damage, if any, to adjacent properties did you observe? _____

5. Reason for dig-up? Service killed

6. Was meter removed: yes yes or no

If yes, meter # 87719577 Meter reading 000 328 178

↑
N

APPLICATION No.: 118079

TAP CLEARED

LOCATION: 106-110 James E.S., S. of Court

OWNER: Leo T. Kavanaugh

MEASURES: 5/8"

S from Court 100.6 ft.
W from E line 6.6 ft.
S from N line 17.7 ft.

Apr 11 7, 1959 Renewed from 1/2 ft. outside curb stop to 3 ft. inside curb stop.
3 1/2 ft. - 3/4" copper tubing 3/4" oppper stop
2# wiping solder

6-15-98 Biszko Cont renewed service from the newly installed 8" ductile main to a point from the main. Stock supplied by Contractor: 2 ft - 3/4" Copper tubing, 1 - 5/8" x 3/4" lead to cop. adapt. X.S., 1 - 3/4" Corporation tap, Contractor to maintain cut.

8-19-98 Service was repair @ point 7' west, of C/S (1 ft out-side to 1 ft inside buried with-out c/s box) Stock: 2 ft. - 3/4" Copper tubing, 1 - 3/4" Curb Stop, 2 - 5/8" x 3/4" lead to cop. adapt. X.S.

2-11-99 M. Pavao Const. renewed from main to property line. Stock: 26 ft. - 3/4" Copper tubing, 1 - 3/4" Curb Stop, 1 - Caldwell Stop Box, 1 - 5/8" x 3/4" lead to cop. adapt. X.S. M. Pavao Const. to maintain cut.

Served
Killed

REMARKS

AFT.

BFF.

DATE



Department of Public Infrastructure
Ronald H. Labelle
Commissioner
Water - Wastewater - Highways - Engineering
Cemeteries

CITY OF NEW BEDFORD
Jonathan E. Mitchell, Mayor

NOTIFICATION OF CHARGES

CUSTOMER: _____ DATE: 4-14-16

ADDRESS: 106 James ACCT #: _____

JOB ☐ Rodding ☐ Mark Out ☐ Sewer Repair
WASTE - ☐ Gas Rodder ☐ Flush ☐ Survey Garage Sewer Acceptance
WATER ☐ Electric Rodder ☐ Hook & Plunger ☐ Investigate Problem
☐ Jetting ☐ Sewer Filming ☐ Festival Hook-Up

JOB ☐ Repair Meter ☐ Water Repair ☐ Hydrant Repair
☐ Test Meter ☐ Renewal ☐ Additional work (see below)
WATER ☐ Change Meter ☐ Hook up plumbing
☐ Per request ☐ Inside ☐ Main Pipe Repair
☐ Shut Off ☐ Sample Collection ☐ Inspection of water main installation
☐ Turn On ☐ Pressure Test ☐ Chlorine Test

JOB ☐ Cement - Sidewalk ☐ Loam & Seed ☐ Remove Curb
HIGHWAYS ☐ Cement - Driveway Brow ☐ Install Curb ☐ Reset Curb

DESCRIPTION OF JOB: inspect 2 services 33871
33872

1/2 deposit required check # _____ deposit amount: _____

Foreman: _____

CUSTOMER APPROVAL

I authorize the Department of Public Infrastructure to investigate my water/sewer problem, and I further authorize and agree to pay any and all charges required to fix the problem, once it has been established. I further understand and authorize that I will be responsible for the initial fee of \$60.00 for the investigation ONLY.

Jonathan E. Mitchell

Customer _____ Telephone # _____ Date _____

PLEASE DO NOT WRITE BELOW THIS LINE

DATE ENTERED:

AMOUNT ENTERED:

NOTES: _____

BILL CODE	COMPLETED		
3SSB			
2SB1			
MARS	HWY	WW	WATER
	434	439	450



CITY OF NEW BEDFORD
Jonathan E. Mitchell, Mayor

Department of Public Infrastructure

Ronald H. Labelle

Commissioner

Water – Wastewater - Highways - Engineering
Cemeteries

NOTIFICATION OF CHARGES

CUSTOMER: _____ DATE: 4 13 16
ADDRESS: 106 James ACCT #: 18079

JOB WASTE - ☐ Rodding ☐ Mark Out ☐ Sewer Repair
WATER ☐ Gas Rodder ☐ Flush ☐ Survey Garage Sewer Acceptance
☐ Electric Rodder ☐ Hook & Plunger ☐ Investigate Problem
☐ Jetting ☐ Sewer Filming ☐ Festival Hook-Up

JOB WATER ☐ Repair Meter ☐ Water Repair ☐ Hydrant Repair
☐ Test Meter ☐ Renewal ☐ Additional work (see below)
☐ Change Meter ☐ Hook up plumbing ☐ Main Pipe Repair
☐ Per request ☐ Inside ☐ Inspection of water main installation
☐ Shut Off ☐ Sample Collection ☐ Chlorine Test
☐ Turn On ☐ Pressure Test

JOB HIGHWAYS ☐ Cement – Sidewalk ☐ Loam & Seed ☐ Remove Curb
☐ Cement – Driveway Brow ☐ Install Curb ☐ Reset Curb

DESCRIPTION OF JOB:

Kill AT main

meter CRACKED

1/2 deposit required check # _____ deposit amount: _____

Foreman: _____ CUSTOMER APPROVAL

I authorize the Department of Public Infrastructure to investigate my water/sewer problem, and I further authorize and agree to pay any and all charges required to fix the problem, once it has been established. I further understand and authorize that I will be responsible for the initial fee of \$60.00 for the investigation ONLY.

Am [Signature]

Customer Alan Smith Telephone # _____ Date _____

PLEASE DO NOT WRITE BELOW THIS LINE

DATE ENTERED:


AMOUNT ENTERED:

NOTES: _____

BILL CODE	COMPLETED
3SSB	
2SB1	
MARS	HWY
	434
	439
	WATER
	450

TAP CLEARED				APPLICATION No.: 18079
DATE	BEE.	AFT.	REMARKS	LOCATION: 106-110 James E.S., S. of Court
				OWNER: Leo T. Kavanaugh
				MEASURES: 5/8"
				S from Court
				W from E line
				S from N line
				Garage
			100.6 ft.	
			6.6 ft.	
			17.7 ft.	
				April 7, 1959 Renewed from 1/2 ft. outside curb stop to 3 ft. inside curb stop.
				3 1/2 ft. - 3/4" copper tubing
				2# wiping solder
				6-15-98 Biszko Cont renewed service from the newly installed 8" ductile main to a point from the main. Stock supplied by Contractor: 2 ft - 3/4" copper tubing, 1 - 5/8" x 3/4" lead to cop. adapt. XXS, 1 - 3/4" Corporation tap, Contractor to maintain cut.
				8-19-98 Service was repair @ point 7' west, of C/S (1 ft out-side to 1 ft inside burried with-out c/s box) Stock: 2 ft.- 3/4" Copper tubing, 1 - 3/4" Curb Stop, 2 - 5/8" x 3/4" lead to cop. adapt. XXS
				2-11-99 M. Pavao Const. renewed from main to property line. Stock: 26 ft. - 3/4" Copper tubing, 1 - 3/4" Curb Stop, 1 - Caldwell Stop Box, 1 - 5/8" x 3/4" lead to cop. adapt. XXS. M. Pavao Const. to maintain cut.



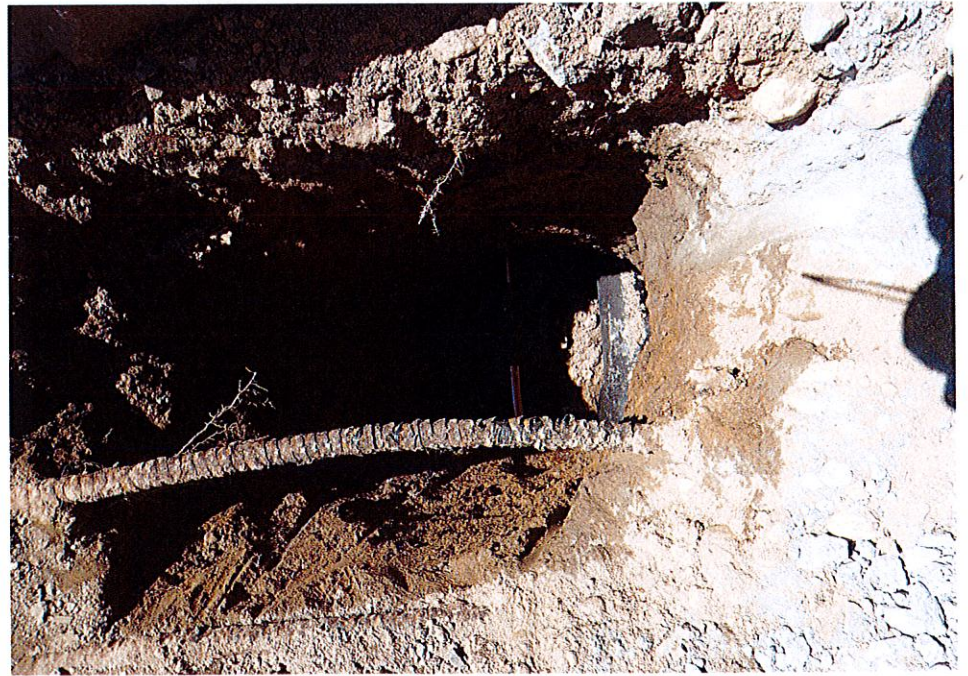

Work Order Number: 16-003557

4/19/2016
3:55 PM

Category: Water Service Priority: _____
Problem: Locate Request Crew: _____
Cause: _____ Supervisor: DANIEL PERRY
Main Task: Inspect Status: New Work Order
Work Order Start Date/Time: _____ Work Order End Date/Time: _____

Location (s) _____
106 JAMES ST

Comments from Request _____
water pressure test 4/20/16 8am w.c. smith

Task Start Date/Time: _____ Task End Date/Time: _____

Task Code: WDT300 Task Description: Inspect


Employee Number	Employee Name	Time Type			Units Hours
		Reg	OT	Normal	
11404	PERCY REYNOLDS	0.00	0.00	0.00	REGULAR TIME
_____	_____	_____	_____	_____	1.15
_____	_____	_____	_____	_____	_____
_____	_____	_____	_____	_____	_____

Equipment Code _____ Equipment Description _____ Units _____
125

Material Code _____ Material Description _____ Units _____

Fluid Code _____ Fluid Description _____ Units _____

PR
4 20-16



City of New Bedford

Department of Public Infrastructure

PRESSURE TEST & DISINFECTION

Client: ERIC Smith

Site Location: 106 James

Date of Test: 4 20 16

Length of Main 27'

Number of Hydrants 0

Number of Gate Valves 1

Number of Services 1

Test Pressure: 150 PSI

Static Pressure: 60 PSI

Leakage: 0

Test Conducted by: Aaron Smith

Chlorination: _____

Samples taken by: _____

Disinfection was conducted in accordance with AWWA specification C651. The line was flushed and a sample of the water was taken to the lab for analysis. The sample was found to be free of coliform and a copy of the lab report is attached.

D.P.I. Inspector on site Percy Reynolds

1105 Shawmut Ave., New Bedford, MA 02746

Tel (508) 979-1550 Fax (508) 961-3054
