

# R-004F

RIVET ST  
New Bedford

Inspection Status: Remote Inspection  
Inspection Level: Level 2

	Quick	Index	Rating
Overall	311A	1.2	14
Structural	3116	1.3	9
O&M	1500	1	5

**Project:** | New Bedford 3D Regulator Inspections  
**Owner:** New Bedford, MA  
**Customer:** CDM Smith

## MANHOLE

**MH Use:** Sanitary

**Year Constructed:**

**Evidence of Surcharge:** No

**Access Type:** Manhole

**Year Renewed:**

## MEASUREMENTS

**Rim to Invert:** 8.5ft

**Northing:**

**GPS Accuracy:**

**Rim to Grade:**

**Easting:**

**Additional Information:**

**Grade to Invert:** 8.5ft

**Elevation:**

**Rim to Grade Exposed:**

**Vertical Datum:**

## COVER

**Type:** Solid

**Center Cover Size:**

**Bearing Surface Diameter:** 28"

**Shape:** Circular

**Cover Material:** Cast Iron

**Bearing Surface Width:** 1"

**Size:** 26"

**Hole Diameter:**

**Cover/Frame Fit:** Good

**Size Width:**

**Hole Number:**

**Cover Condition:** Sound

## COVER INSERT

**Insert Type:** None

**Insert Condition:**

## COVER ADJUSTMENT RING

**Ring Type:** Solid

**Ring Condition:** Sound

**Ring Material:** Cast Iron

**Ring Height:**

## FRAME

**Frame Material:** Cast Iron

**Clear Opening Width:** 24"

**Seal Inflow:** None

**Bearing Surface Width:** 1"

**Frame Depth:**

**Frame Condition:** Sound

**Bearing Surface Depth:** 9"

**Offset Distance:**

**Clear Opening Diameter:** 24"

**Seal Condition:** Sound

CHIMNEY

<b>Chimney Present:</b> Yes	<b>Chimney I/I:</b>	<b>Lining Interior:</b>
<b>Chimney Depth:</b> 0.5ft	<b>First Material:</b> Concrete (precast)	<b>Lining Exterior:</b>
<b>Clear Opening:</b>	<b>Second Material:</b>	<b>Chimney Condition:</b>

CONE

<b>Cone Depth:</b> 2ft	<b>First Material:</b> Brick	<b>Lining Exterior:</b>
<b>Cone Type:</b> Conical centered	<b>Second Material:</b>	<b>Cone Condition:</b>
<b>Clear Opening:</b>	<b>Lining Interior:</b>	

WALL

<b>Wall Diameter:</b>	<b>First Material:</b> Brick	<b>Lining Exterior:</b>
<b>Wall Width:</b>	<b>Second Material:</b>	<b>Wall Condition:</b>
<b>Wall Depth:</b> 5.4ft	<b>Lining Interior:</b>	

BENCH

<b>Bench Present:</b> Yes	<b>Lining:</b>
<b>Material:</b> Brick	<b>Bench Condition:</b>

CHANNEL

<b>Channel Present:</b> Yes	<b>Type:</b> Pipe	<b>Channel Condition:</b>
<b>Material:</b> Brick	<b>Exposure:</b> Fully Opened	

STEP

<b>Number:</b> 0	<b>Material:</b>
------------------	------------------


PIPE CONNECTION INFORMATION

Pipe No.	Clock	Rim to Inv.	Direction	Material	Shape	Height	Width	Cond.	Seal Cond.	Pipe Type	Struct. ID	Comments
1	6	8.5"	Out	Concrete Pipe (non-reinforced)	Circular	25"		Sound	Sound	Gravity Connection		
2	12	8.5"	In	Concrete Pipe (non-reinforced)	Circular	25"		Sound	Sound	Gravity Connection		

GENERAL INFORMATION

<b>Surveyed By:</b>	<b>Reviewer Number:</b> P0035145122021	<b>Sheet No.:</b>
<b>Reviewed By:</b> M. Bierman	<b>Precleaning:</b> No Pre-Cleaning	<b>Date Cleaned:</b>
<b>Weather:</b>	<b>PO Number:</b>	<b>Work Order:</b>
<b>Purpose of Survey:</b> Routine assessment	<b>Media Label:</b>	<b>Consequence of Failure:</b>
<b>Certificate Number:</b> U0219070304856	<b>Date &amp; Time</b> 2023-12-14	

# Condition Report

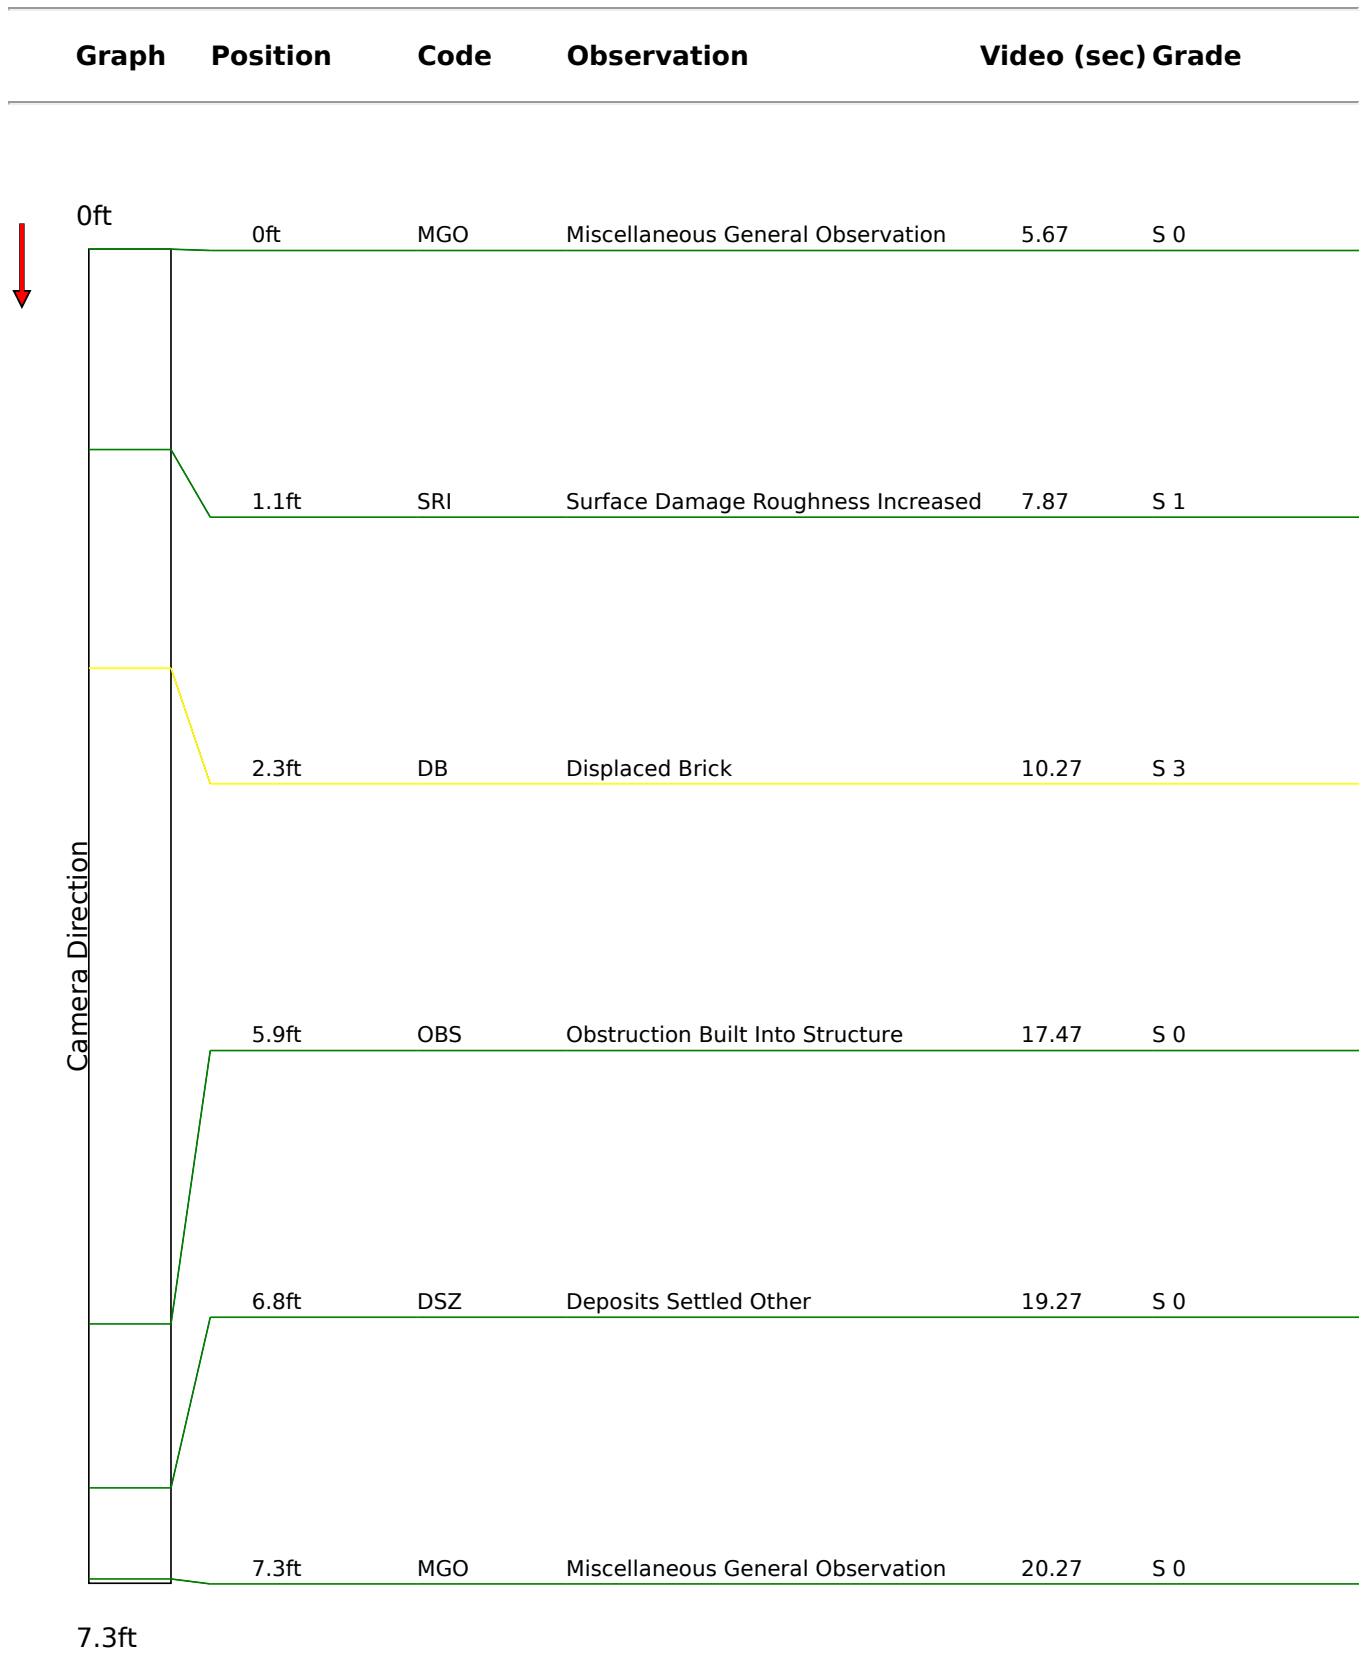



Code: **MGO**  
Description: **Miscellaneous General Observation**

Distance: **0ft**  
Structural Grade: **0**  
O&M Grade: **0**  
Clock Start/From:  
Clock To:  
1st Value:  
2nd Value:  
Value Percent:  
Continuous Index:  
Within Eight" of Joint: **False**  
Remarks: **Start inspection**



Code: **SRI**  
Description: **Surface Damage Roughness Increased**

Distance: **1ft**  
Structural Grade: **1**  
O&M Grade: **0**  
Clock Start/From: **12**  
Clock To: **12**  
1st Value:  
2nd Value:  
Value Percent:  
Continuous Index:  
Within Eight" of Joint: **False**  
Remarks:



Code: **DB**  
Description: **Displaced Brick**

Distance: **2ft**  
Structural Grade: **3**  
O&M Grade: **0**  
Clock Start/From: **3**  
Clock To: **9**  
1st Value:  
2nd Value:  
Value Percent:  
Continuous Index:  
Within Eight" of Joint: **False**  
Remarks:





Code: **OBS**  
Description: **Obstruction Built Into Structure**

Distance: **5ft**  
Structural Grade: **0**  
O&M Grade: **0**  
Clock Start/From: **12**  
Clock To:  
1st Value:  
2nd Value:  
Value Percent: **60**  
Continuous Index:  
Within Eight" of Joint: **False**  
Remarks: **gate blocking pipe connection**



Code: **DSZ**  
Description: **Deposits Settled Other**

Distance: **6ft**  
Structural Grade: **0**  
O&M Grade: **0**  
Clock Start/From: **11**  
Clock To: **1**  
1st Value:  
2nd Value:  
Value Percent: **25**  
Continuous Index:  
Within Eight" of Joint: **False**  
Remarks: **debris surrounding gate**



Code: **MGO**  
Description: **Miscellaneous General Observation**

Distance: **7ft**  
Structural Grade: **0**  
O&M Grade: **0**  
Clock Start/From:  
Clock To:  
1st Value:  
2nd Value:  
Value Percent:  
Continuous Index:  
Within Eight" of Joint: **False**  
Remarks: **End inspection**

