

Tel: 7-4343

P.O. Box 624

November 27, 1962

#26228 People's Realty Corp.

E.S.Mt. Pleasant St., N x Nauset St.

Please install 2" Copper service to supply shopping center. Tap 2" main connection of 6" main at junction of Hathaway Rd. Franch in sidewalk with Ser.#26229.

Measures of 2" Mueller Oriseal Valve:

S x S line Building	15.3
E x E Curb Mt. Pleasant St.	14.2
S x S Railroad Tracks	81.1

Work done November 28, 29, 30, 1962


(over)

supervision.....	
187' of 2" copertubing type K, soft.....	\$ 27.02
Labor.....	353.43
1 2" Mueller Oriseal Valve.....	\$201.60
1 Caldwell Valve Box, complete.....	
Carting.....	15.--
1 6" Cast Iron Plug tapped 2".....	8.78
Loader use.....	63.--
Compressor use.....	12.--
1 2" copper cap.....	
1 2"x2"x2" cop. to cop. to cop. tee.....	
8 2" cop. to cop. cplgs., A-1671.....	
1 2" cop. x male adapter.....	
1 2" 90° elbow.....	
11 3/4 lbs. caulking lead.....	
3/4 lb. braided jute.....	
1 street cut: 11' x 2 1/2' Warrenite.....	
3 sidewalk cuts: 90' x 3'; 10' x 6'	
& 6' x 6' Blacktop.....	

ATTENTION: Supt. Nathan Ellis
Service #26228: 2" - Inside

✓ 80 ft. of 2" copper tubing.....	\$149.60
✓ Labor.....	\$ 59.52
✓ 1 2"x2"x2" copper tee.....	\$
✓ 1 2" Mueller Oriseal Valve.....	\$
✓ 1 Caldwell Valve Box, complete.....	\$
✓ 1 2" copper cap.....	\$
✓ 3 2" cop. to cop. cplgs., A-1671....	\$
✓ Carting.....	\$ 7.50
✓ Loader Use.....	\$ 28.00
✓ Compressor use.....(none).....	\$
✓ Supervision.....	\$ 5.40

Work done November 28, 29 & 30, 1962

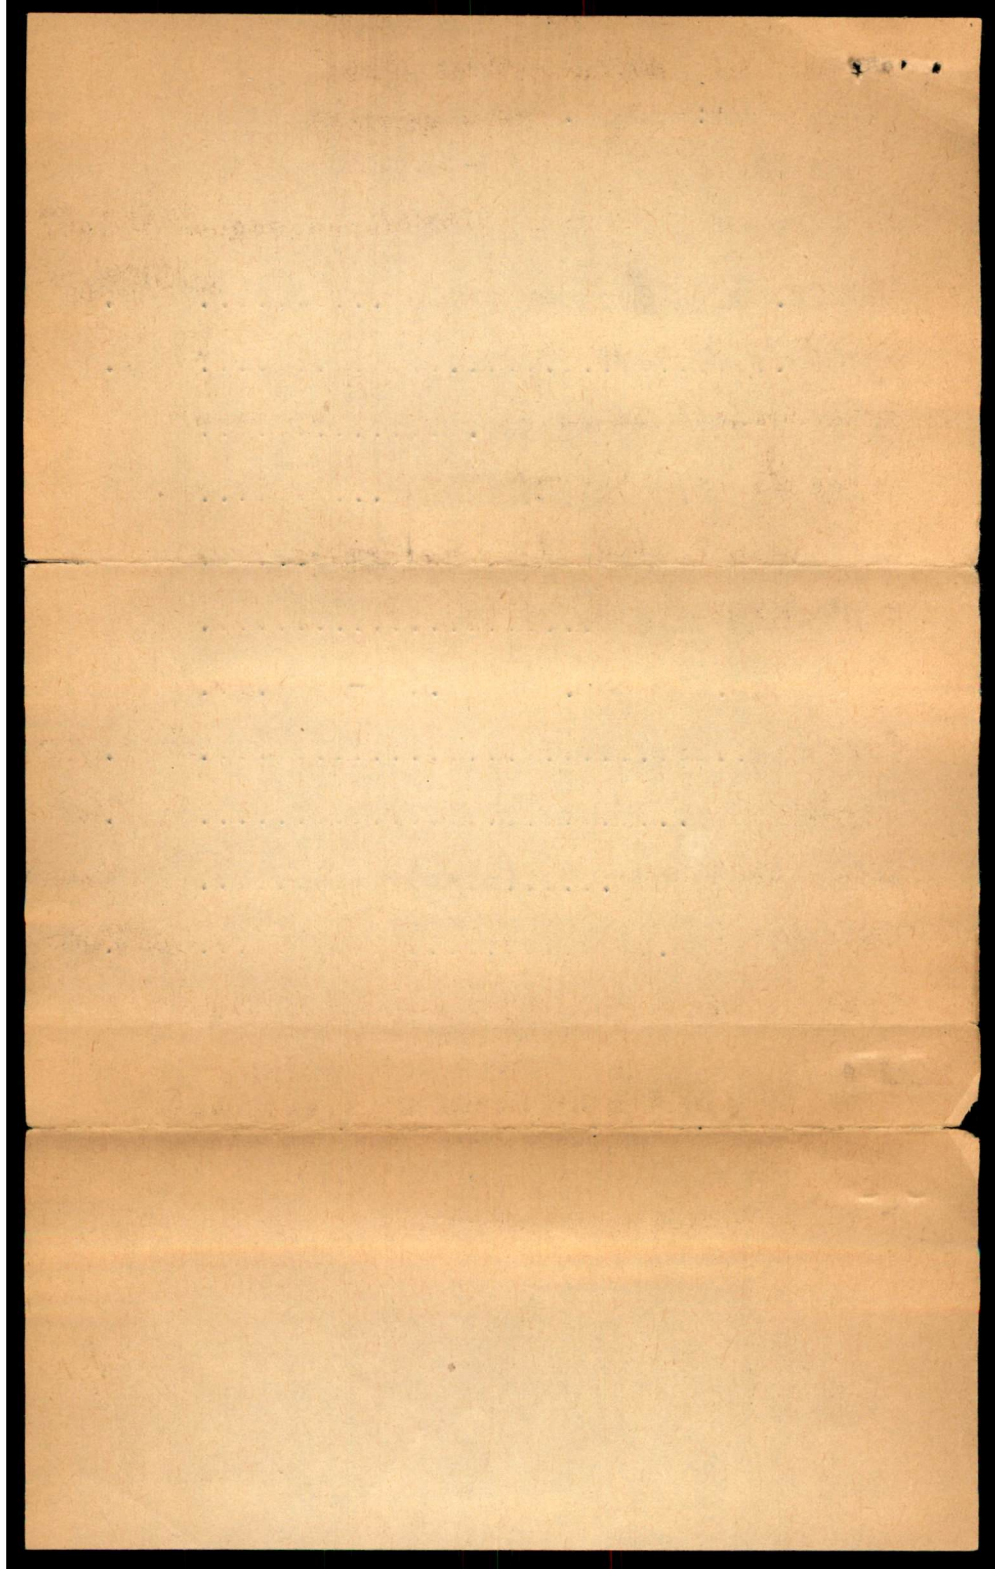

ATTENTION: Supt. Nathan Ellis
Service #26228: 2" - outside

✓ 109 ft. of 2" copper tubing.....	✓	\$ 203.83
✓ Labor.....	✓	\$ 142.08
✓ 11 3/4# baulking lead.....	✓	\$
✓ 3/4# braided jute.....		\$
✓ 6" C. I. plug tapped 2".....	✓	\$ 8.78
✓ 1 2" cop. x male adapter.(cplg.).....		\$
✓ 5 2" cop. to cop. cplgs., A-1671.....		\$
✓ 1 2" 90° elbow.....		\$
✓ Carting.....	✓	\$ 7.50
✓ Loader use.....	✓	\$ 35.--
✓ Compressor use.....	✓	\$ 12.--
✓ Supervision.....	✓	\$ 21.62
✓ 1 St. cut: 11' x 2½' Warrenite.....	✓	\$
✓ 3 sidewalk cuts: 98' x 3½'; 10' x 6' & 6½' x 6' Blacktop.....	✓	\$

Work done November 28, 29 & 30, 1962

