

c/o Coholan Plumb.
699 Belleville Ave.


February 13, 1969
#27909 County of Bristol
NW cor. #505 Pleasant St. & Spring St.
Please install 4" CIGL service to supply
courthouse. To replace 3" Ser. #15253. 3"
Taker's meter - inside bldg.

Measures of 4" Darling Tapping Gate Valve:

E x E line	Sixth St.	59.0 ft.
N x S	" Spring St.	24.9 ft.
E x W	" Building	20.1 ft.
S x S	" "	37.0 ft.

Main is 26 ft. N x S line.
Work done Oct. 21 & 22, 1970

26 ft. - 4" C.I.C.L. Pipe @ 1.73 ft.	\$ 44.98
Labor.	223.84
1-8"x8"x4" A.P.Smith Tapp. Sleeve . . .	83.46
1-4" Darling Tapp. Gate Valve.	73.20
1-4" Offset B.S 18" C to C C.L.. . . .	51.60
1-4" Reg. Gate Box, complete.	58.94
2-1/16 Bends B.S.-4" C.L. @ 26.04 . . .	52.08
1-4" Solid Sleeve.	16.44
1-4" Plug	2.54
34# Mineralead @ .24#	8.16
2 1/2# - 5/8" Asb. Yarn. Rope @ 2.28# . .	5.13
Carting.	20.00
A.P.Smith Drilling Machine Use	25.00
Loader Use: 3 hrs. @ 7.00 hr.. . . .	21.00
Compressor Use: 3 hrs. @ 6.00 hr. . . .	18.00
St. cut: 19' x 2 1/2' Warr. @ 1.78 LF+5. . .	38.82
Sidewalk cut: 10' x 5' Cam @ 5.75 S.Y. .	31.97
Supervision	\$819.93 - TOTAL
	<u>44.77</u>

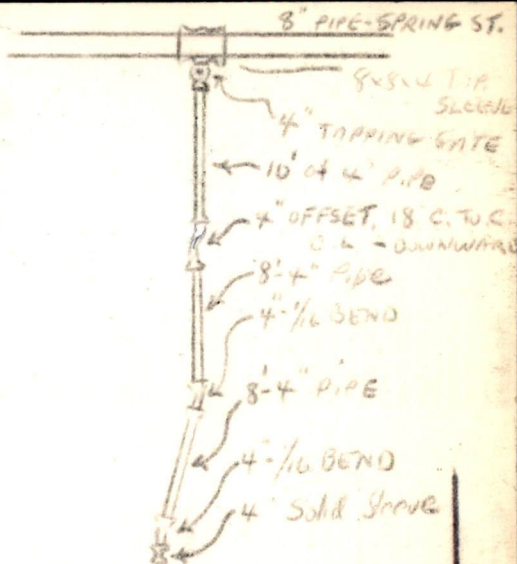

N

