

897 Kempton St.

55

June 9, 1972

#28640

Pacific Oil Heat, Inc

#897 Kempton St.; junction of
Kempton & Mill Sts.

Please install 1½" copper service to supply
office bldg. Meter in boiler room. Service
from Kempton St. Replaces service #21407 (915
Kempton St.) to be discontinued.

Measures of 1½" Curb Stop:

W x E line	Hussey St.	6.5	22.0	ft.
S x N "	Kempton St.		6.0	ft.
W x W "	Bldg.	41.5	45.0	ft.


Main is 62 ft. S x N line.

Work done June 13-14, 1972

✓ 117 ft. - 1½" Copper tubin by Owner (62' out-
55' ins.)

Labor.....	\$ 99.98
1 ✓ 1½" Hays Corporation.....	\$ 25.25
1 ✓ 1½" Hays Curb Stop.....	\$ 46.00
1 ✓ Buffalo Stop Box, complete.....	\$ 12.00
Carting.....	\$ 10.00
D-4 Drilling Machine Use.....	\$ 20.00
✓ 8" x 1½" Dresser Saddle.....	\$ 16.56
Loader Use: 3 hrs. @ 7.00 hr.....	\$ 21.00
Compressor Use: 4 Hrs. @ 6.-- hr.....	\$ 24.00
St. cut: 12' x 3' Warr. @ 1.78LF + 5.--	\$ 26.36
" " " " " " " "	\$ 26.36
" " 7' x 3' Warr. @ 1.78LF + 5.--	\$ 17.46
Sidewalk cut: 10' x 3' Blacktop @ 2.--SY	6.66
	<u>\$ 351.63</u>

SERVICE - 28640 - 1 1/2" - PACIFIC OIL
N. S. KEMPTON ST. W. X ROCKDALE AVE

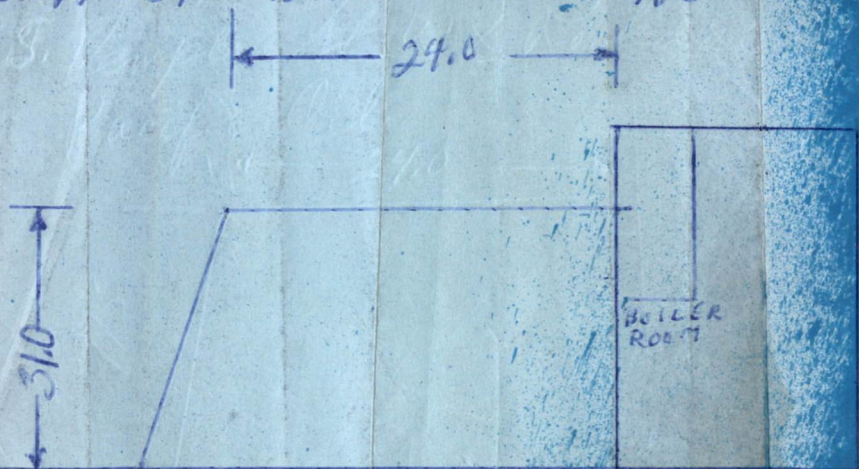

NORTH LINE
KEMPTON

SALES



RENTALS

MAXEL. HOSSEY ST. 6.5
W. W. L. BUILDING 41.5
E. W. L. HOSSEY ST. 44.0

Corrected Measures
897 Kempton S t.

Jan. 25, 1985
Ser.#28640 1½"

W x E line Hussey St .
W x W line Bldg.
E x W line Hussey st.

6.5 ft.
41.5 ft.
44.0 ft.

J. Rodrigues

