

3 Morgan Terrace

of

August 14, 1972

#28707

Mary Souto

41

3 Morgan Terrace

Please install $3/4$ " copper service to supply cottage. Replacing old service #21455. Meter inside cellar wall. Service from 1" main Morgan Terrace.

Measures of $3/4$ " Curb Stop:

E x E line Sixth St.	49.0 ft.
S x N " Morgan Terr.	9.9 ft.
S x N " House	7.8 ft.
W x W " "	16.3 ft.


Main is 48 ft. S x N line.
Work done Aug. 14, 1972

20 ft. - 3/4" Copper by Owner

(Plumber installed the 20 ft. of copper
from the tee to the property line.)

Labor.	\$	4.55
1 2 3/4" Hays curb stop.	\$	11.25
1 Caldwell Stop Box.	\$	12.00
2 - 3/4" Meter cplg. @ 2.00 ea.. . . .	\$	4.00
Carting.	\$	10.00
		<hr/>
	\$	41.80

Owner dug, backfilled & will
maintain trench cuts.

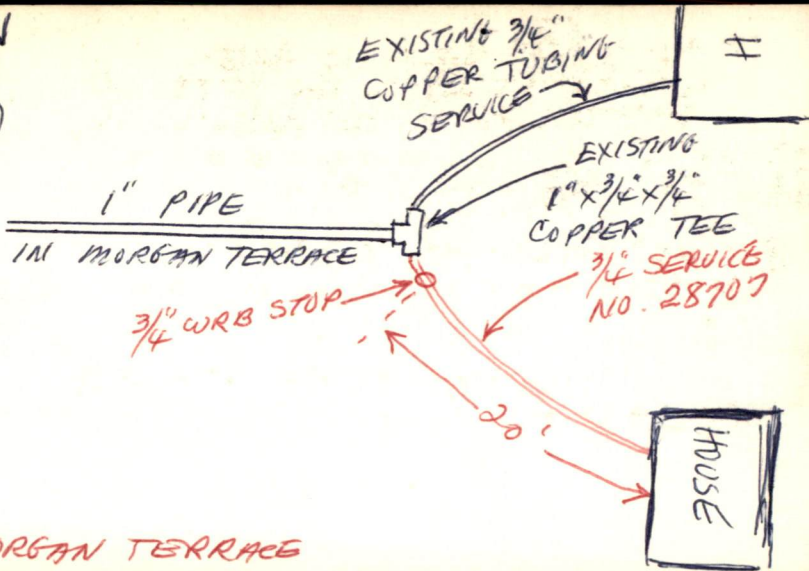

3 MORGAN TERRACE

