

5-8671

910 Stratford St.

#28938

August 15, 1973

Porta Call, Inc.

N.S. Ohio St., E. x Ashley Blvd.

Please install 1" copper service to supply
ranch house. Meter inside cellar wall above
floor. Service from Ohio St.


Measures of 1" Curb Stop:

E x E line Ashley Blvd.	433.5 ft.
S x N line Ohio St.	11.0 ft.
W x W line House	29.4 ft.
S x S line House	37.3 ft.

Main is 32 ft. S x N line.

Work done Sept. 11, 1973

74 ft. - 1" Copper tubing (32' out: 42' ins.)	
52 ft. by Owner	
22 ft. by City @ 1.30'.....	\$ 28.60 ✓
Labor.....	\$ 47.52 ✓
1 1" Hays Corporation.....	\$ 8.50 ✓
1 1" Hays Curb Stop.....	\$ 14.00 ✓
1 Caldwell Stop Box.....	\$ 12.00 ✓
Carting.....	\$ 10.00 ✓
D-4 Drilling Machine Use.....	\$ 15.00 ✓
2 1" Meter cplg. @ 2.50 ea.....	\$ 5.00 ✓
6" x 1" Christy Service Saddle.....	\$ 9.08 ✓
Loader Use: 2 hrs. @ 7.00 hr.....	\$ 14.00 ✓
Compressor Use... 1 hr.....	\$ 6.00 ✓
St. cut: 9' x 2' Warr. @ 1.78' + 5.00	\$ 21.02 ✓
Sidewalk cut: 8' x 4' Cement @ 5.75SY	\$ 20.47 ✓
	<u>\$ 211.19</u>

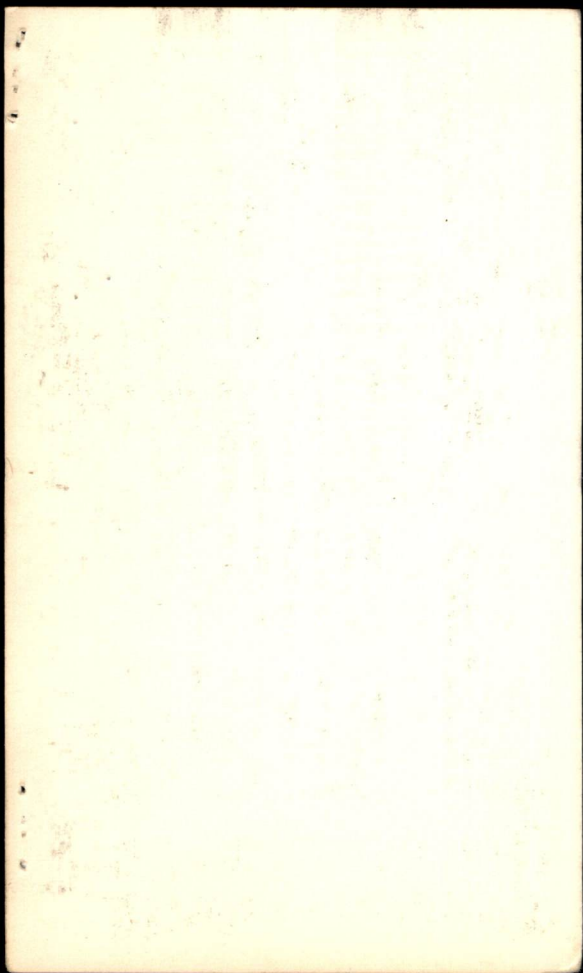

2 11 17

Service No. 28938 - 1"

2 11 17

N. S. Ohio St., E x Ashley
Blvd.

