

2121 W. Main Rd.
Portsmouth, R.I.

July 26, 1974

#29219

Joseph Almeida, Jr.

N.E. cor. Pamela Dr. & Carriage Dr.

Please install 1" copper service to supply
1 family home. Meter inside cellar wall above
floor. Service from Pamela Dr. Lot 1

Measures of 1" Curb Stop:

E x E line Carriage Dr.

S x N line Pamela Dr.

70.0 ft.
~~60.4~~ ft.
5.0 ft.

Main is 36 ft. S x N line.

Work done September 12, 1974

Line Service

36 ft. - 1" Copper tubing by Owner
(36 ft. out:

Labor.	\$	102.62
1" Corporation	\$	8.50
1" Curb Stop	\$	14.00
Caldwell Stop Box, complete.	\$	12.75
Carting.	\$	10.00
B-100 Mueller Tapping Mach. Use.	\$	14.00
2 1" Meter cplg. @ 2.50 ea.	\$	5.00
Loader Use: 3 hrs. @ 7.00 hr.	\$	21.00
Compressor Use: 1 hr.	\$	6.00
St. cut: 30' x 3' Dirt	\$	N/C
Side. cut: 8' x 3' Dirt.	\$	N/C
	\$	193.87


7/12/84 Netter picked up
2-1" cplgs

Corrected Measures
N.E. cor. Pamela Dr. &
Carriage Dr.

May 1, 1984
Ser.#29219-1"

E x E line Carriage Dr. 70.0 ft.

L. Souza

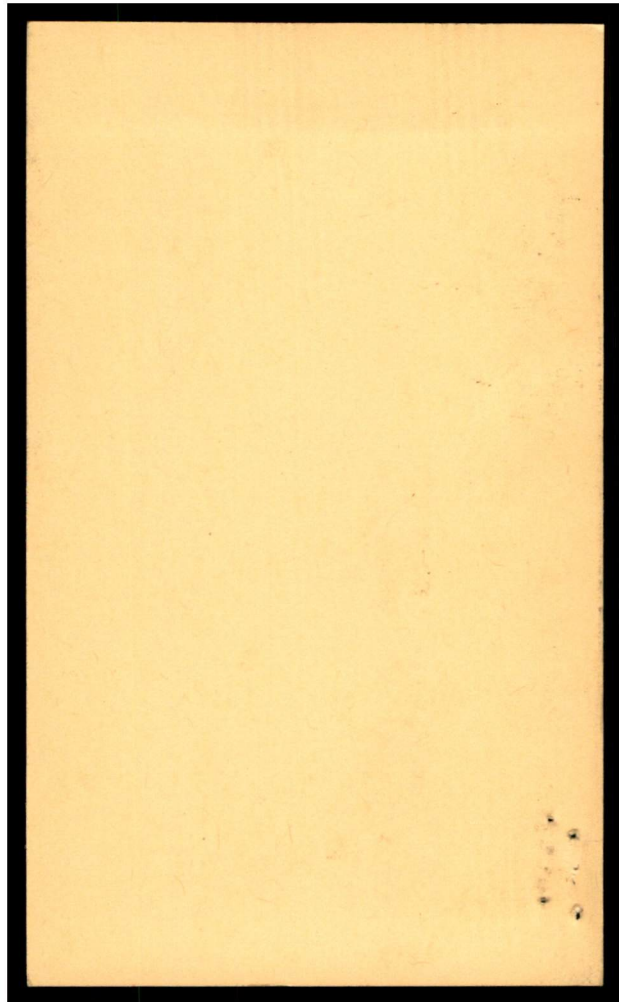

Additional Measures
69 Pamela Dr.

Nov. 5, 1984
Ser.#29219-1"

E x W line house
S x S line house

2.0 ft.
48.5 ft.

J. Rodrigues

