

✓
29319

Sept. 8, 1975

2112 Acushnet Ave.
New Bedford, Mass.

Albert Poczatok

S.S. #30 Whitman St., W x Belleville Ave.


Please install $3/4$ " copper to supply cottage
Meter inside cellar wall above floor. Service
from Whitman St. Replaces $5/8$ " serv. #18106.

Measures of $3/4$ " Curb Stop:

W x W line Desautels St.	6.6 ft.
N x S line Whitman St.	6.3 ft.
W x E line Bldg.	5.3 ft.
N x N line Bldg.	17.3 ft.

Work done November 24, 1975

34 ft. - 3/4" Copper tubing by City	
(20' out: 14' ins.) @ 1.80'	\$ 61.20
Labor.	\$ 56.54
1 - 3/4" Corporation	\$ 5.75
1 - 3/4" Curb Stop	\$ 11.25
Caldwell Stop Box	\$ 16.75
Carting.	\$ 10.00
B-100 Mueller Tapping Machine Use.	\$ 12.00
2 3/4" Meter cplg. @ 2.00 ea.	\$ 4.00
Loader Use: 2 hrs. @ 7.00 hr.	\$ 14.00
Compressor Use: 1 hr. @ 6.00 hr.	\$ 6.00
St. cut: 6' x 9' Warrenite @ 1.78' + 5. --	21.02
Side. cut: 3' x 9' Dirt.	n/c.
	\$ 218.51

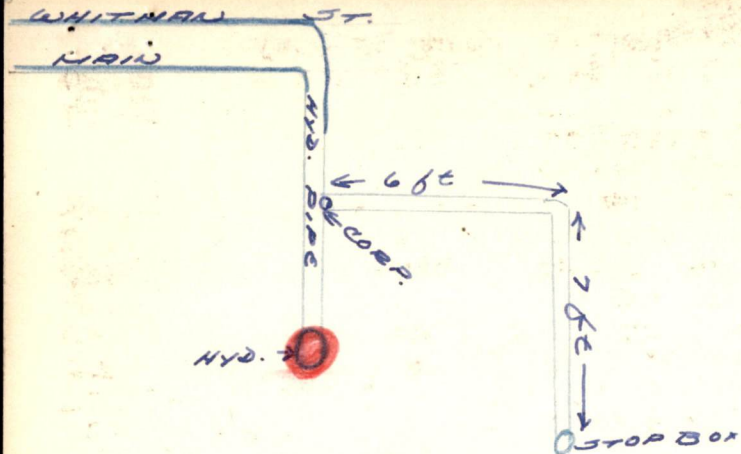

#29319-3/4"

30 WHITMAN ST.

