

Tel. 3-2449

9/22/75

311 Nemasket St.

#29331

New Bedford, Ma.

✓ Rita Farland

N.s. #311 Nemasket St., W x Alva St. 68

Please install 1" copper to supply ranch.  
Meter inside cellar wall.

Measures of 1" Curb Stop:

E x E line Alva St.	6.0 ft.
S x N line Nemasket St.	5.0 ft.
W x E line House	15.0 ft.
S x S line House	24.0 ft.

Main is 34 ft. S x N line.


Work done Sept. 30, 1975

TOTAL 348.12

60 ft. - 1" Copper tubing(total)	
26 ft. by Owner - was already laid	
from the prop. line to inside bldg.	
34 ft. by City @ 2.35'	\$ 79.90
Labor.	\$ 113.09
1" Mueller Corporation	\$ 8.50
1" Mueller Curb Stop	\$ 14.00
1 <del>Aushnet</del> Stop Box, <i>COMPL.</i>	\$ 16.75
Carting.	\$ 10.00
D-4 Drilling Mach. Use	\$ 15.00
2 1" Meter cplg. @ 2.50 ea.	\$ 5.00
Loader Use: 3 Hrs. @ 7.00 hr.	\$ 21.00
Compressor Use: 2 hrs. @ 6.00 hr.	\$ 12.00
8" x 1" Saddle	\$ 15.84
St. cut: 18' x 3' Warrenite @ 1.78'	\$ 32.04
Sidewalk cut: 12' x 12' Dirt	\$ 5.00
	348.12

Ser. # 29331

Stop Box lines up directly with corp. tap.  
This copper comes in straight up to 4 ft.  
south of the curb and then goes around a  
large stone 5 ft. west of  
the stop box.

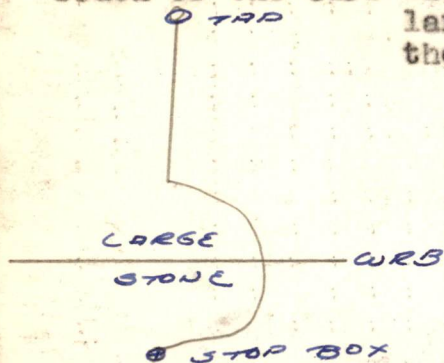

S  
E + W  
N

