

P.O. Box A-2087
New Bedford 02743

29474

12/23/76

Frionor Bridge Freezer

N.s. Bridge St. W x Pope's Island

Please install 8" FIRE SUPPLY to supply
fish house. Service from Bridge St. work to be
done by contractor.


Measures of 8" Gate Valve:

E x W line Bridge	114.0 ft.
N x S line Rte. 6	11.4 ft.
E x Hydrant	24.0 ft.

Work done Oct. 27 & 28, 1976

Contractor supplied & installed all stock.
Contractor dug, backfilled & will maintain
trench.

Insp. by John Medeiros - Labor.	\$ 86.40
Turn On Charge.	<u>\$ 5.00</u>
	\$ 91.40

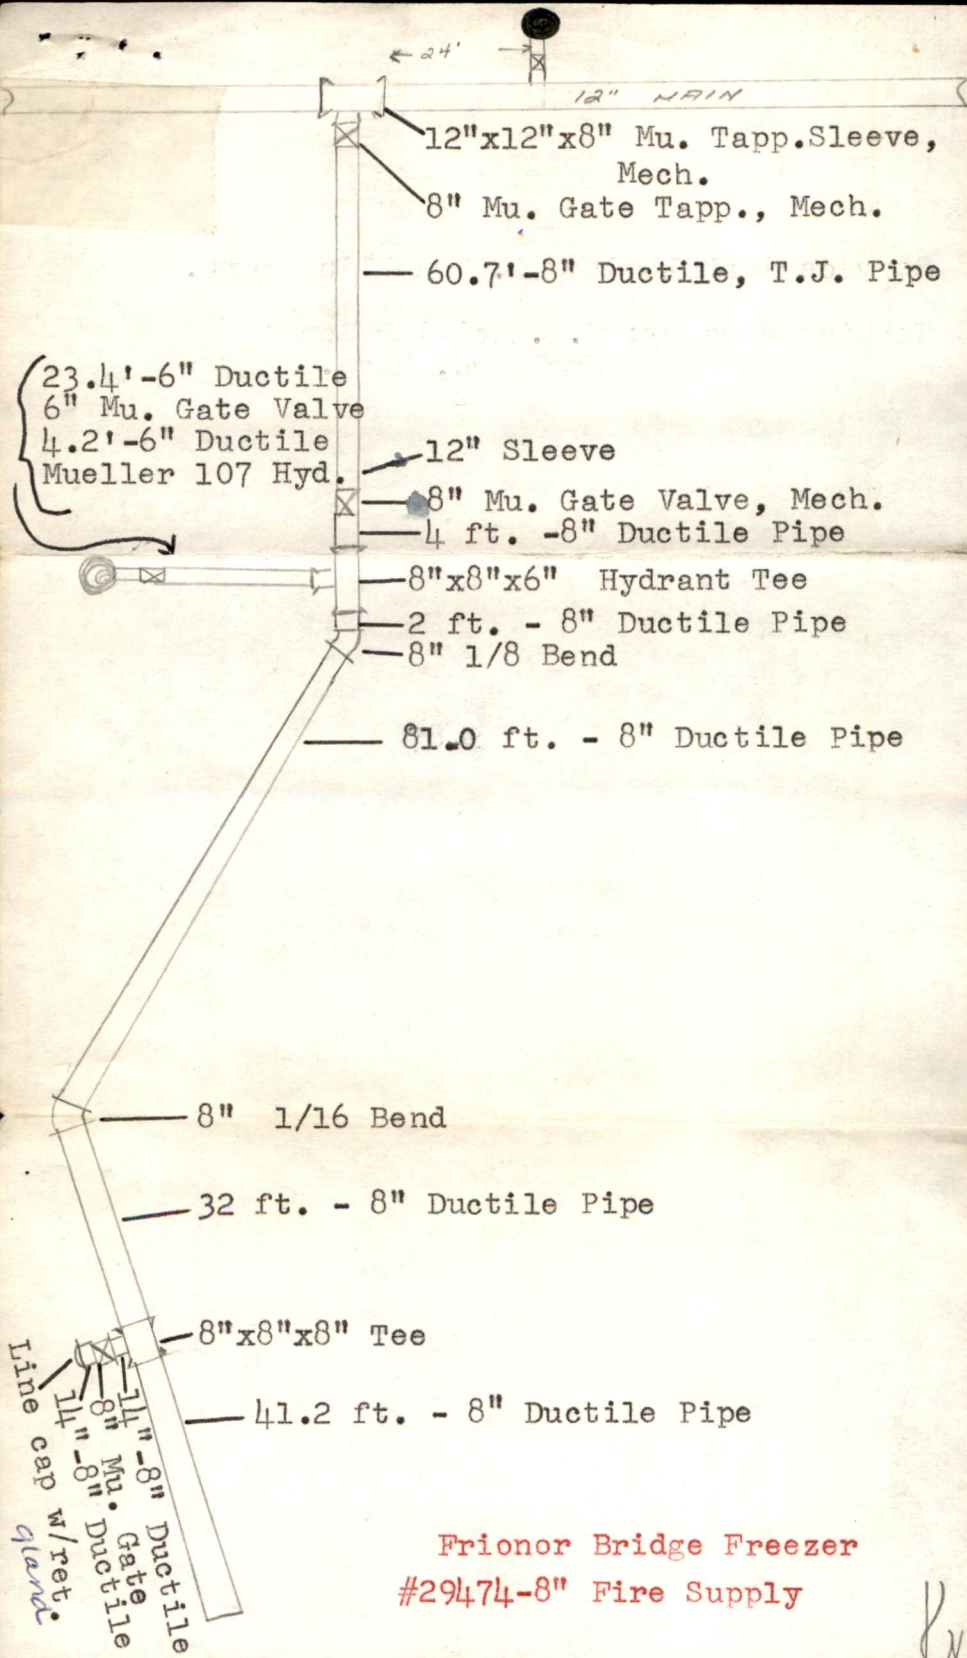

Frionor Bridge Freezer
#29474-8" Fire Supply

82

Service installed by C. Franklin Const.

Tapping done by: F.A. Raini & Son
Marlboro, Mass.
