

Tel. (-4501

Ext. 337

11/30/76

25
Cabco Engineer. Co.

372 Central Ave.

Pawtucket, R.I. 02861

Berkshire Hathaway

S.s. Gifford St.; W x Harbor (E x domestic

Please install 8" C.L.C.I. to supply Service
Mfg. Plant. Serv. from Gifford St.

FIRE SUPPLY

Measures of 8" Tapping Gate Valve:

W x W line Harbor St. 195.0 ft.

N x S line Gifford St. 13.0 ft.

W x E line Bldg. 2.0 ft.


Main is 14 ft. N x S line.

Work done May 24, 1977

STOCK SUPPLIED BY WATER DEPT.

Labor	\$	62.64
10" x 10" x 8" Mueller Tapp. Sleeve		231.60
8" Mueller Tapp. Gate Valve . . .	\$	198.00
2 - #664 Gate Boxes @ 34.80 . . .	\$	69.60
15# Mineral lead @ .24#	\$	3.60
1# Asbestos Yarn. @ 2.99#	\$	2.99
Carting	\$	10.00
Smith Tapping Machine Use	\$	40.00
Compressor Use 1 hr.	\$	6.00
Supervision	\$	12.53
Turn On Charge	\$	5.00
St. cut: 10' x 6' Warr. @ 1.78' + 5' . . .	\$	22.80
	\$	664.76

29529-8"
FIRE SUPPLY

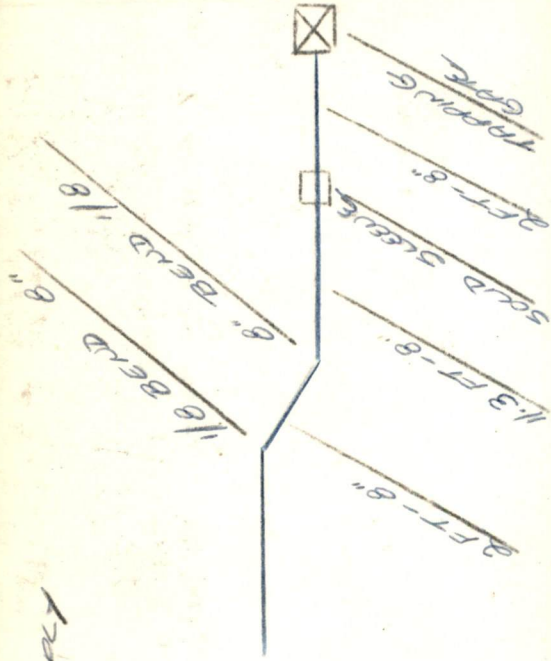

Contractor supplied all pipe & fittings

All fittings are rodded.

(17 ft - 8" CICA)
