

#29768

May 11, 1979

52

Standard-Times, Inc.

S.S. Market St., W. x Pleasant St.

Please install 8" CICI FIRE SUPPLY to supply
bldg. Replaces Ser. #20380 to be discontinued
4".

Measures of 8" Gate Valve, Mech.

W x W line Pleasant St. 73.3 ft.

N x S line Market St. 16.3 ft.

MAY 3,

Work done ~~April 30~~, 1979

Main is on the 18.5 ft. line.

PER JANET HC 6/5/79

8" x 8" x 8" Tee, Mech.
 14 ft. - 8" C.I.C.L. Ductile Pipe
 @ 6.73' \$ 94.22

8" Gate Valve, Mech.
 Caldwell #10 Style 664 Gate Box, compl

8" Offset (1 ft. drop), Mech.

8" S.B. 4 1/2" Cast cplg. - By Owner

6 ft. - 8" C.I.C.L. Ductile Pipe - By Owner

Carting \$ ~~10.00~~ HC

St. cut: 7' x 4' Warr. @ 5.00 SY \$ 15.55

Side. cut: 4 1/2' x 4 1/2' Cement @ 14.50 SY

4 1/2' x 4 1/2' Cement 65.26

Loader use: 3 hrs. @ 7.00 . . . \$ ~~21.00~~ HC

Compressor use: 2 hrs. @ 6.00 . . . \$ ~~12.00~~ HC


Turn on charge \$ 7.50

Labor \$ ~~264.73~~ HC

NEW TOTAL

182.53

\$ 490.25

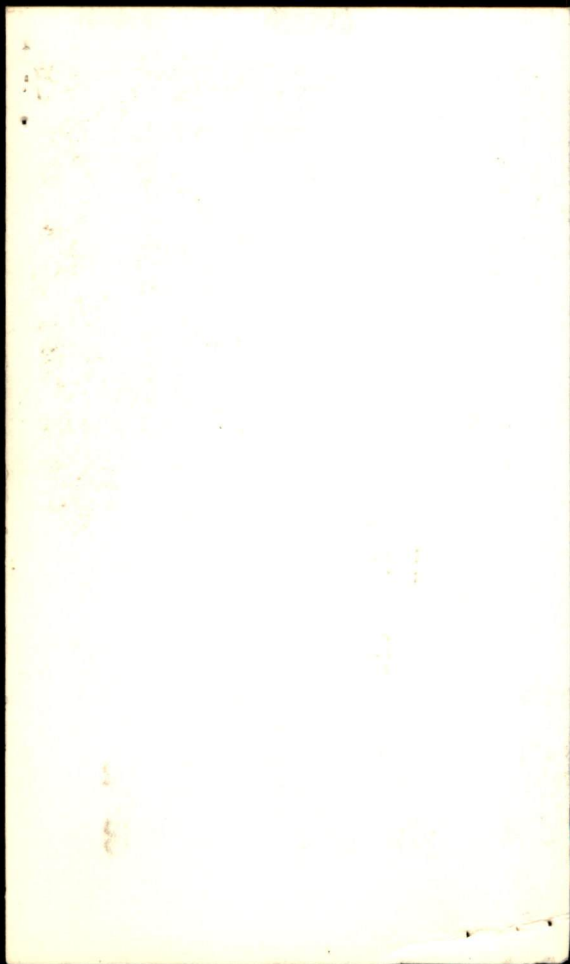

STANDARD TIMES BLDG.

HAZARD
ST.

8" BRANCH
MECH.

18" PC-8"
PIPE

8" GATE,
MECH.

1 FT. - 8"
PIPE

8" OFFSET
(1 FT. DROP)

11 FT. -
8" DUCTILE

441-8"
CPG

6 FT.
FLANGE
PIPE

29768-8"
