

Tel. 992-0953

114 MacArthur Dr.

#29887

October 3, 1980

Ocean Marine Services Inc.

W.S. MacArthur Dr. N X Conway St.

37

Please Install 6" C.L.C.I. fire Supply.
To supply repair Shop Service to come
from MacArthur Drive .

Measures of 6" Gate Valve:

E x N line Conway St.	462.2 ft.
E x W line Mac Arthur Dr.	13.0 ft.
E x N line Bldg.	8.5 ft.

Main is 14 ft. E x W line.

Work done Oct. 17, 1980


Contractor supplied & installed all stock:

- 14 Ft. - 6" C.I.C.L. Pipe
- 16" x 16" x 6" Tapping Sleeve
- 1 - 6" Tapping Gate Valve
- 1 - #10 Gate Box, complete

Contractor dug, backfilled & will maintain trench.

Water Dept.:

A.P. Smith Tapping machine use.	\$	200.00
Labor.	\$	65.15
Turn on Charge.	\$	<u>7.50</u>
100# Mineralead @ .91#	\$	91.00
3# Asbestos Yarning @ 2.99#	\$	8.97
3# Hard gasket @ 2.99#	\$	<u>8.97</u>
	\$	381.59

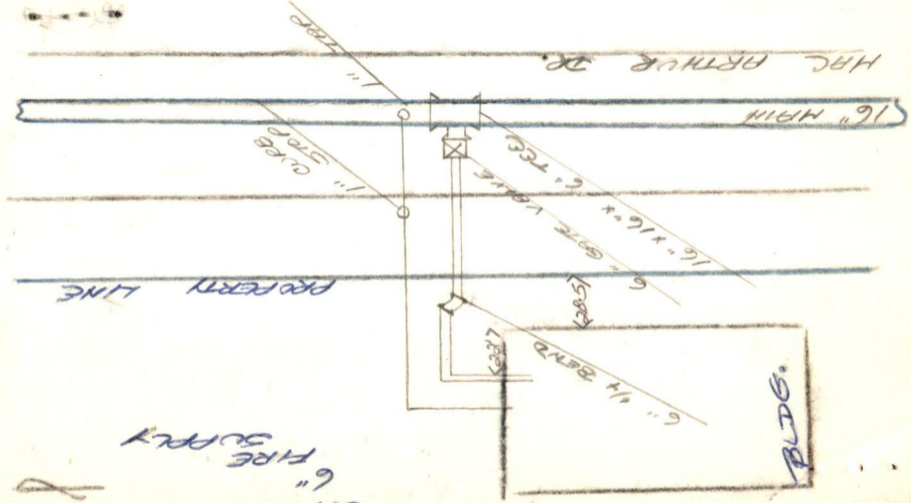

8N

29887
6" FIRE SUPPLY

1 1/2" MAIN

HPC ARTIVE DR.

1" STOP

1 1/2" GATE VALVE

PROPERTY LINE

15887

1/4 BEND

BLDG.

15887

6"

1" STOP

8
2
1
0

8
2
1
0
