

765 Wildwood Rd.

122

29901

November 7, 1980

Joseph M. Goyette

E.S. Shawmut Ave., N. x Nash Rd.

Please install 1" copper service to supply storage bldg. From Shawmut Ave. Bldgs moved from Ft. Rodman. City meter in bldg above floor LAY WITH DRAIN.

Measures of 1" Curb Stop:

N x N line Nash Road 1490 ft.

W x E line Shawmut Ave. 14 ft.

S x S line Bldg. 12 ft.

W x W line Bldg. 61 ft.

Main is 55 ft. W x E line.


Work done April 28, 1981

121 ft. - 1" Copper tubing by Owner
(55' out: 66' ins.)

Labor.	\$ 99.07
1" Corporation	\$ 12.06
1" Curb Stop	\$ 28.42
1 Caldwell Stop Box, complete.	\$ 17.00
Carting.	\$ 10.00
B-100 Mueller tapping machine use.	\$ 14.00
2 1" Meter cpig. @ 4.00 ea.	\$ 8.00
Turn on charge.	\$ 15.00
	\$ 203.55

Contractor dug, backfilled & will
maintain trench.

GOYETTE'S

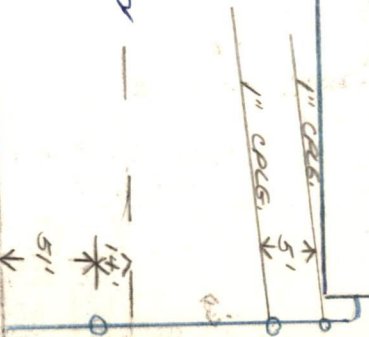

29901-1"

