

Tel. 997-5266 Doro Dev. Corp., 991 Kempton St., NB

July 11, 1985

#30269 S.E.cor. Rounseville & Bartlett Sts. 132 A

Please install 1" copper serv. to supply one-family home. From Rounseville St. Meter inside cellar wall.

LOT #1 Contractor to install.

Measures of 1" Curb Stop:

E x E line Bartlett St.	49.4 ft.
N x S line Rounseville St.	6.0 ft.
E x W line Bldg.	12.0 ft.
N x N line Bldg.	35.3 ft.

Main is 12 ft. N x S line.

Work done Aug. 21, 1985

Contractor supplied & installed all stock:

12.5 ft. - 1" Copper tubing (12.5' out:

1" Corp. tap


1" Curb stop

1 Caldwell Stop Box, compl.

Doro Devel. dug, backfilled & will maintain
trench.

B-100 Mueller tapping mach. use.....	\$	14.00
2 1" meter cplg. @ 4.00	\$	8.00
Turn on charge.....	\$	15.00
Labor.....	\$	12.37
	\$	<u>49.37</u>

ROUNSEVILLE ST.

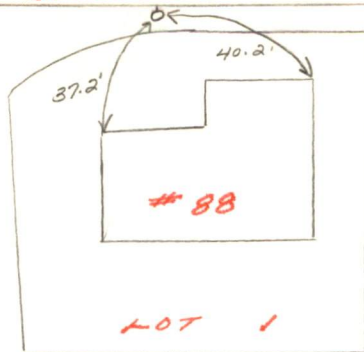

111

111
