

Tel. 995-1449 W.C. Smith, 58 Ridgewood Rd, NB 02745

August 1, 1985

68

#30306 W.S. Westview St. Ext. N x Gifford's La.

Please install 1" copper serv. to supply one-family home. From Main in easement. Meter inside cellar wall. Lot 13 - line serv. by B. Smith.

Measures of 1" Curb Stop:

(S x lot 12 service box 72.6 ft.)

N x S line Giffords La. (stone wall) 764.6 ft.

Work done June 1986

over

3/30/87 no house yet

W.C. Smith supplied & installed all stock:

8 ft. - 1" copper tubing ( 8 ft. main to curb stop:

1" Corporation tap

1" Curb Stop

1 Caldwell Stop Box, compl.

-----

Insp.....\$ 8.18

2 1" meter cplgs. @ 4.00 ea.....\$ 8.00

Turn on charge.....\$ 15.00

\$ 31.18

NOTE: Lot 13 sold to owner of house on Cornell St.  
may not build house on this lot for privacy only.

New Service  
W.S. Westview St. Ext.  
N x Gifford's Lane

Nov. 7, 2001  
Ser. #30306 1"

Eric Smith Cont. extended service from curb stop to  
house 50 ft. - 1" copper tubing


Measures:

N x n line Gifford's Lane	76.0 ft.
S x house #140 Westview St.	28.0 ft.
W x house #148 Westview St.	28.1 ft.
N x N line building	28.4 ft.
E x E line house	16.0 ft.

Measures taken: 11/7/01

See sketch attached

Insp: Rose

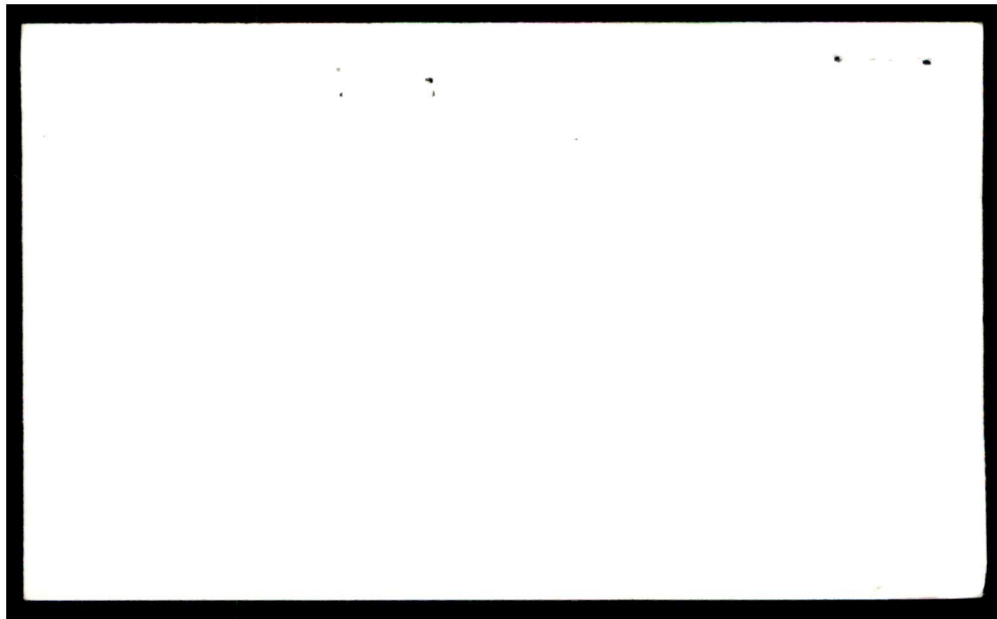

REMARKS

DATE    BEF.    AFT.

Gifford's Lane

#148  
30307

WEST VIEW  
XIN,  
281.6'

8" MAIN

76.5'

28.4'

28.6'

#140  
30305

N

