

Tel. 997-5266

Doro Dev. Corp. 991 Kempton St. NB

Nov. 12, 1986

#30692 S.S. Doreen St. WxMcCombs Blvd.

132 E²

Please install 1" copper serv. to supply one-family home. From Doreen St. Contr. to dig & maintain trench. Meter inside cellar wall. Lot ~~675~~ 108

Measures of 1" curb Stop:

N x S line Doreen St.

6.0 ft.

E x W line house

40.0 ft.

W x E line house

8.0 ft.

N x N line house

34.0 ft.

Main is 14 ft. N x S line.

Underground utilities N x curb boxes.

Work done Nov. 5, 1987

E x LOT 107 → 86.0 FT

Doro Devel. supplied all stock

1" Copper tubing
1" Corporation tap
1" Curb Stop
1 Caldwell Stop box, compl.

B-100 Mu. tapping machine use.....\$ 14.00
2 1" meter cplgs. @ 4.00 ea.....\$ 8.00
Carting.....\$ 10.00
Turn on charge.....\$ 15.00
Labor.....\$ 31.12
\$ 78.12

Doro Devel. dug, backfilled & will maintain trench.

2-1" cplgs given 11/3/87 red truck

30692 S.S. Doreen St. W x McCombs Blvd.


Additional measures:

E x Lot 107 86.0 ft.

S x stop box Lot 129 85.0 ft.

Main to curb stop 9 ft.

Lot 108

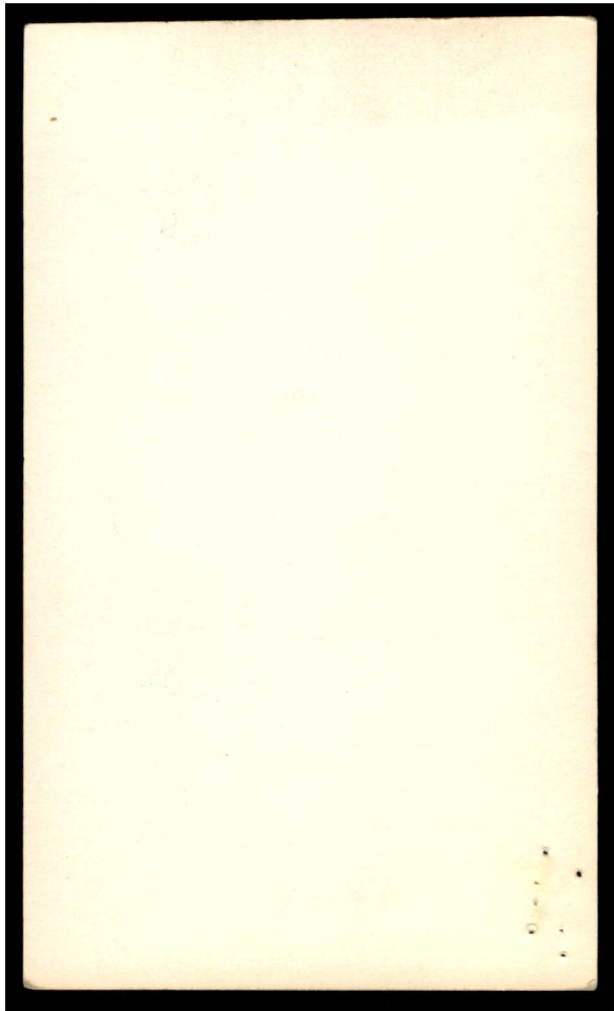

Additional Measures

Oct. 22, 1990

S.S. Doreen St. W x McCombs Blvd. Ser. # 30692 1"

W x W line Mc Combs Blvd.

108.0 ft.

L. Souza

