

Tel. 997-5266

Doro Dev. Corp. 991 Kempton St. NB

Nov. 12, 1986

132 E

#30694 S.E. cor. McCombs Blvd. & Doreen St.

Please install 1" copper serv. to supply one-family home. From McCombs Blvd. Meter inside cellar wall. Contr to dig & maintain trench. Lot 677 110

Measures of 1" curb stop:

E x McCombs Blvd.

E x W line house

35.0 ft.

W x E line house

12.0 ft.

N x N line house

22.0 ft.

Tap to curb stop 33 ft. south

Work done Oct. 30, 1987

E x E line Mc Combs Blvd.

42.0 ft.

W x N x D. 72.6 FT.

Doro Devel. supplied all stock

1" Copper tubing

1" Corporation tap

1" Curb Stop

1 Caldwell Stop box, compl.

B-100 Mu. tapping machine use.....	\$ 14.00
------------------------------------	----------

2 1" meter cplgs. @ 4.00 ea.....	\$ 8.00
----------------------------------	---------

Carting.....	\$ 10.00
--------------	----------

Turn on charge.....	\$ 15.00
---------------------	----------

Labor.....	\$ 31.12
------------	----------

	<u>\$ 78.12</u>
--	-----------------


Doro Devel. dug, backfilled & will maintain trench.

#30694 S.E. cor. McCombs Blvd. & Doreen St.

Additional Measures

W x hydrant

72.6 ft.

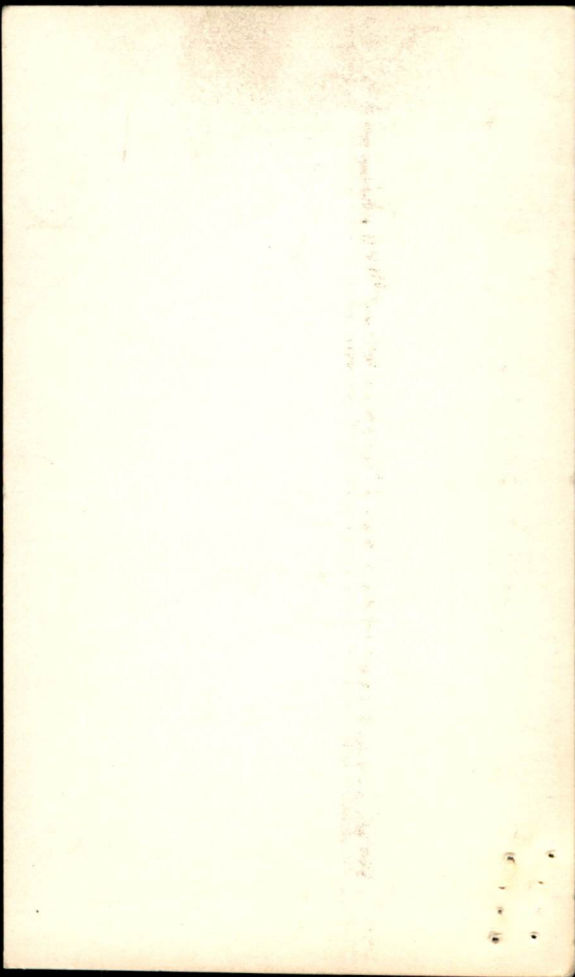

Additional Measure
SE cor. McCombs Blvd. & Doreen

Feb. 23, 1990
Ser. # # 30694 - 1"

E x E line McCombs Blvd.

42.0 ft.

M. Rose

Lot 110

100
