

Tel. 597-5266

Doro Dev. Corp. 991 Kempton St. NB

Nov. 12, 1986

132 E²

#30711 N.W. cor. McCombs Blvd. & Doreen St.

Please install 1" copper serv. to supply one-family home. From McCombs Blvd. Contr. to dig & maintain trench. Meter inside cellar wall. Lot ~~694~~ 127

Measures of 1" Curb Stop:

W x W line McCombs Blvd.

W x E line house

12.6 ft.

E x W line house

31.6 ft.

N x S line Doreen St. (main)

14.0 ft.

S x S line house

31.0 ft.

Work done Oct. 30, 1987

EX LOT 128 - 99 FT.

TAP TO BOX 30 FT.

Doro Devel. supplied all stock

1" Copper tubing
1" Corporation tap
1" Curb Stop
1 Caldwell Stop box, compl.

B-100 Mu. tapping machine use.....	\$ 14.00
2 1" meter cplgs. @ 4.00 ea.....	\$ 8.00
Carting.....	\$ 10.00
Turn on charge.....	\$ 15.00
Labor.....	\$ 31.12
	<u>\$ 78.12</u>

Doro Devel. dug, backfilled & will maintain trench.

2 - 1" cplgs. McGraw 1-22-88


#30711 N.W. cor. McCombs Blvd. & Doreen St.

Additional Measures:

E x lot 128 99 ft.

Tap to stop box 30 ft.

Lot 127

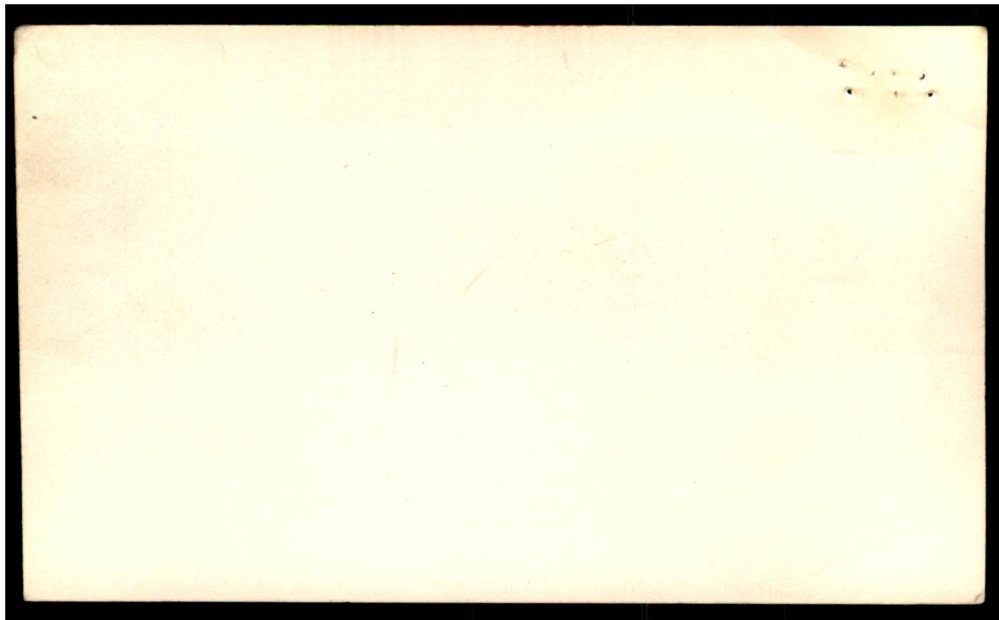

Additional Measures

Oct. 22, 1990

N.W. cor. McCombs Blvd. & Doreen St .

Ser. # 30711 1"

W x W line McCombs Blvd.

27.0 ft.

S x N line Doreen St.

4.5 ft.

L. Souza

