

Tel

Curtis Perry by A. Fournier
129 Princeton St. NB 02745

68

January 9, 1987

#30730 W.S. Cornell St. N x Gifford Lane

Please install 1" copper serv. to supply one-family home. From Cornell St. Meter inside cellar wall. Andre Fournier to dig & maintain trench.

Measures of 1" Curb Stop:

(N x N line Templeton St.	382.0 ft.)
S x N line house	21.5 ft.
E x E line house	48.0 ft.
Tap is S x hydrant gate	29.0 ft.

Work done April 16, 1987

Smith supplied & installed all stock:

40 ft. - 1" Copper tubing (main to p.l.)

1" Corporation tap

1" Curb Stop

1 Caldwell Stop Box , compl.

B-100 Mu. tapping machine use.....	\$	14.00
------------------------------------	----	-------

2 1" meter cplgs. @ 4.00 ea.....	\$	8.00
----------------------------------	----	------


Carting.....	\$	10.00
--------------	----	-------

Labor.....	\$	13.95
------------	----	-------

Turn on charge.....	\$	15.00
---------------------	----	-------

\$ 60.95

Permit 97 Bill Smith dug, backfilled & will
maintain trench.

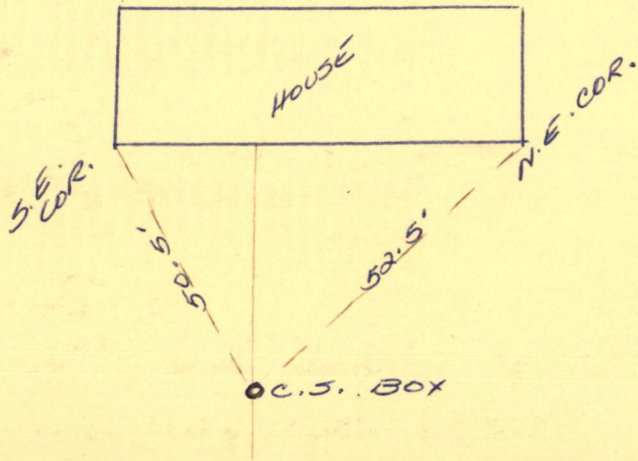

30730

✓

