

Te. 763-3858 William J. Clymer, 244 County Rd.

Dec. 11, 1987 Freetown, MA 02717

83

#30925 S.W. cor. Mt. Pleasant & Canterbury Sts.

Please install 1" copper serv. to supply one-family home. From Chime St. Meter in box @ prop. line in easement. TEMPORARY SERVICE,

Measures of 1" Curb Stop:

W x W line Mt. Pleasant St. 75.0 ft.

S x N line Chime St. 3.0 ft.

S x meter pit (center of) 8.5 ft.


Main to curb stop 30.0 ft.

Work done Dec. 15, 1987

1" Copper tubing by Contractor	
labor.....	\$ 43.11
1" Corporation	\$ 12.06
1" Curb Stop.....	\$ 22.15
1 Caldwell Stop Box, compl.....	\$ 21.00
Carting.....	\$ 10.00
B-100 Mu. tapp. mach. use.....	\$ 14.00
2 1" meter cplgs. @ 4.00 ea.....	\$ 8.00
Turn on charge.....	\$ 15.00
	\$ 145.32

Contractor dug, backfilled & will
maintain trench.

Tapped from Chime St. by way of meter pit.
Temporary Service until Spring 1988

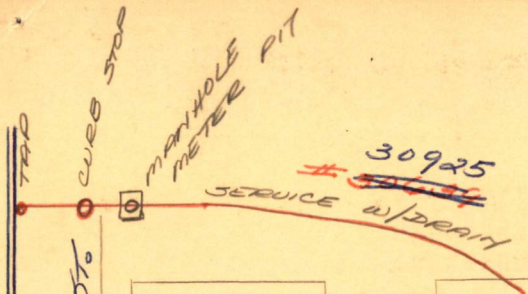

CALME ST.

LOT 21

NO. 179

LOT 8

MT. PLEASANT ST.

CANTERBURY ST.

