

Tel. 997-559

4/4/91

N.B. Housing Authority PO Box A-2081

by Edward Konetchy

NB Ma. 02741

#31559

S.S. Amanda Ave. (S), W x Church S t.

Please install a 3" meter with a 4" ductile service to supply the neighborhood center. from Amanda Ave. (S)

Meter in pit at property line. taker's meter

Measures of 4" Darl. Gate Valvae, mech:

W x W line Church St.

153.0 ft.

W x W line Bldg.

11.0 ft.

N x N line Bldg.

17.0 ft.

N x meter pit

11.6 ft.

S x S outh curb

2.1 ft.

Work done May 13, 1991

Wm. Smith cut in a 4" x 8" tee on old main for
new Community Bldg. W x Church St.

Stock:-

1 - 8" x 4" tee, ductile, mech.

1 - 4" Darl. gate valve, mech.


3 ft. - 8" ductile pipe

18" - 4" ductile pipe

Inspection.....	\$	15.00
Turn on charge.....	\$	25.00
		<hr/>
	\$	40.00

Comm. Bldg.

S
↓

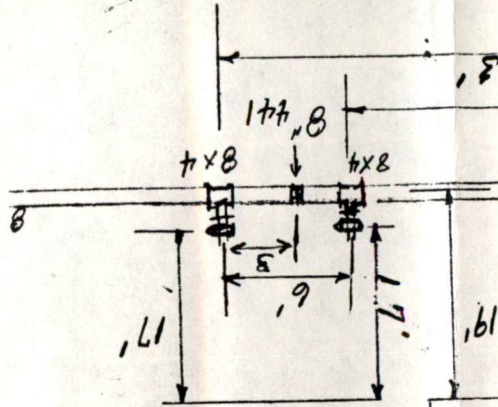

1 Wx11. Chnck 8t. - 147'
2 Wx11. Chnck 8t. - 153'

31559

31570

