

Tel. 993-0547

4/16/91

Grace Church

by William I. Reed

422 County St.

N.B., Ma 02740

#31563 N.S. #131 School St. E x County St.

46

Please install 6" ductile FIRE SUPPLY to supply a church complex. from School St. Norman's Enterprises - contractor. Street Obstruction Permit No:

Measures of 6" Mueller Tapping gate valve, mech.

E x E line County St. 50.0 ft.

S x N line School S t. 23.0 ft.

N x S line School St. 17.0 ft.

E x W line Church 41.2 ft.

S x S line church 34.0 ft.

Main is 16 ft. N x S line School St.

Work done May 8, 1991

J. Hoadley Installed Tapping sleeve & tapping gate.

Normans Enterprise dug road

J. Martin Fire Service installed service from the gate to inside of building.

Stock supplied & installed by Contractor:

8" x 8" x 6" Mueller Tapping sleeve, MJ.

6" Mueller tapping gate valve, MJ

#10 Roadway gate box, compl.

6" Ductile pipe

2 - 6" 22½° Bend, mech.

2 - 6" 45° Bend, Mech.

Inspection.....\$ 15.00
Turn on charge.....\$ 25.00
\$ 40.00

Date May 10, 1991


Fire Safety Services

received the following stock in A-1 condition
from the New Bedford Water Dept. to be
returned:

2 - 6" Retainer glands


*plus
almas
ap*

Received by



JOB SITE:

Grace Church - County & School S t.

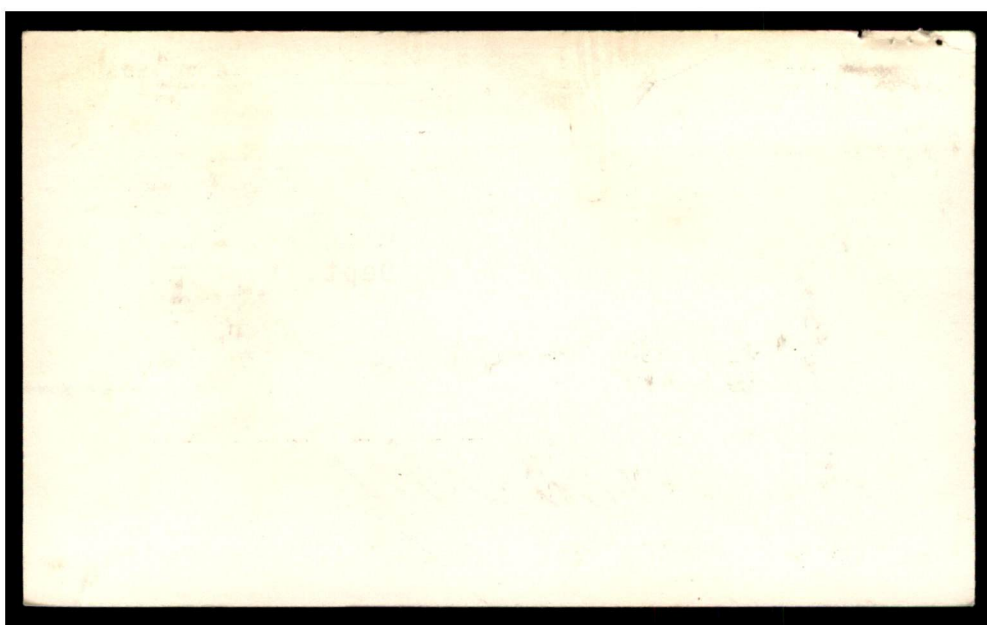



22½° Bends were used to go over brick sewer and under gas main, electric duct, cable t.v.



The 45° bends were used because the pipe was heading straight under the columns which have granite stone supports.

Pipe goes under the east corner of stained glass window.


ALL FITTINGS HAVE RETAINING GLANDS AND ARE RODDED BACK FROM GATE TO INSIDE OF BUILDING.



#31563-6"
FIRE SUPPLY

PN

COUNTY ST.

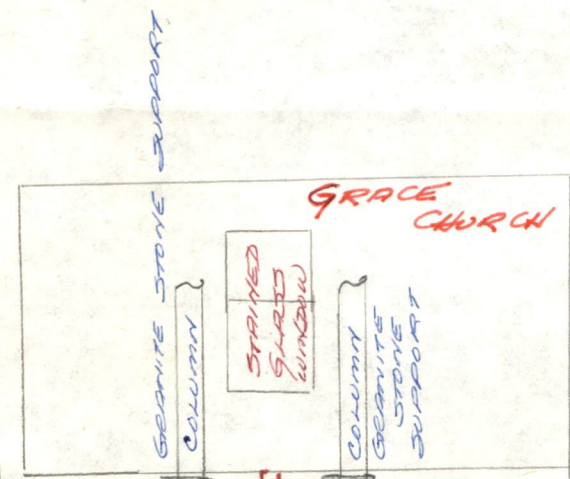

6 FT. - 6" PIPE

6" - 45° BEND, MECH.

7.6 FT. PC. OF 6" PIPE



6" - 45° BEND, MECH.

3 FT. - 6" PIPE

17 FT. - 6" DUCTILE PIPE

5" PC. - 6" PIPE

6" - 22 1/2° BEND

8" PC. OF 6" PIPE

6" - 22 1/2° BEND

6" TAPP. GATE

8 X 6 X 6 TAPPING SLEEVE

SCHOOL ST.
