

Tel. 997-8545

8/23/96

Brook Street Realty
by Robert Bates

P.O. Box 1090
Mattapoisett

#32069 #78 Brook St.

Please install a 1" copper ser. to supply an office
trailer. from Brook St. P98 L250 ⁹²

Measures of 1" Curb Stop:

N x N line Tallman St.

100.6 ft.

E x W line Brook S t.

5.2 ft.

S x gate fence

1.2 ft.

Work done August 8, 1996

✓

Daigle Plumbing supplied the 1" Copper tubing
1 - 8" Mech. Cap

1" Corporation tap.....	\$ 12.06
1" Curb Stop.....	\$ 22.15
1 Caldwell Stop Box, compl.....	\$ 21.00
Turn on charge.....	\$ 15.00
2 1" meter cplgs. @ 5.00 ea.....	\$ 10.00
Inspection.....	\$ 15.00
	\$ 95.21

NOTE: 36 FT. - 1" COPPER
FROM END MAIN TO INSIDE METER
PIT!

J. AUGUST ST. OPEN HYD. #359
(SEWER)

New Service # 32069 1"

August 8, 1996

Daigle Plumber cut off the 8" main at a point 115 ft. N x gate valve on Brook St. N x S line Tallman St. '19.


Removed a #441 Cplg. & 1½" tap. Removed approx. 5 ft. - 8" main & installed an 8" Mech cap with a 1" tap to supply New Service # 32069 1":


This work also cut off all piping northerly which includes: # 21953 8" Fire Supply

21816 1½"

22495 1"


Insp. Frank Bento

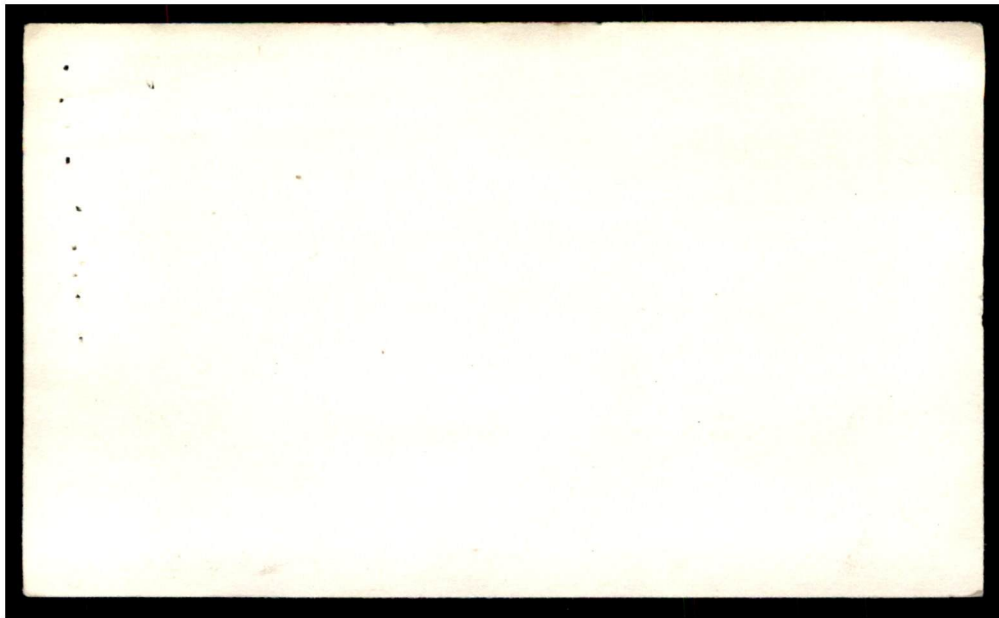

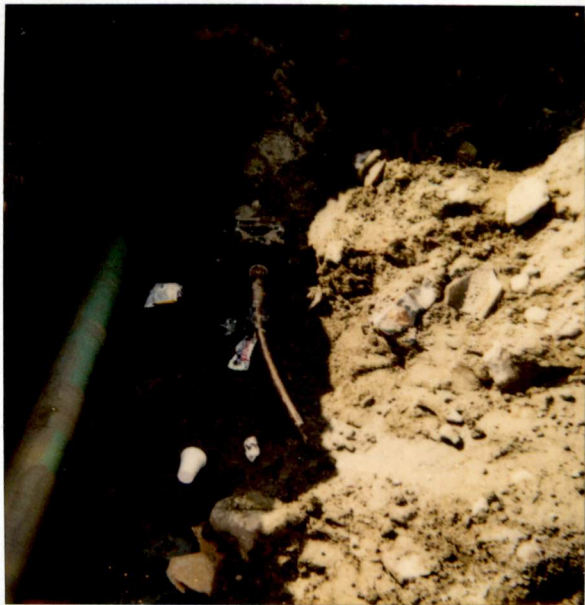

8-8-96 W.S. BROOK ST

N.W. TALLMAN ST
DEAD-END MAIN

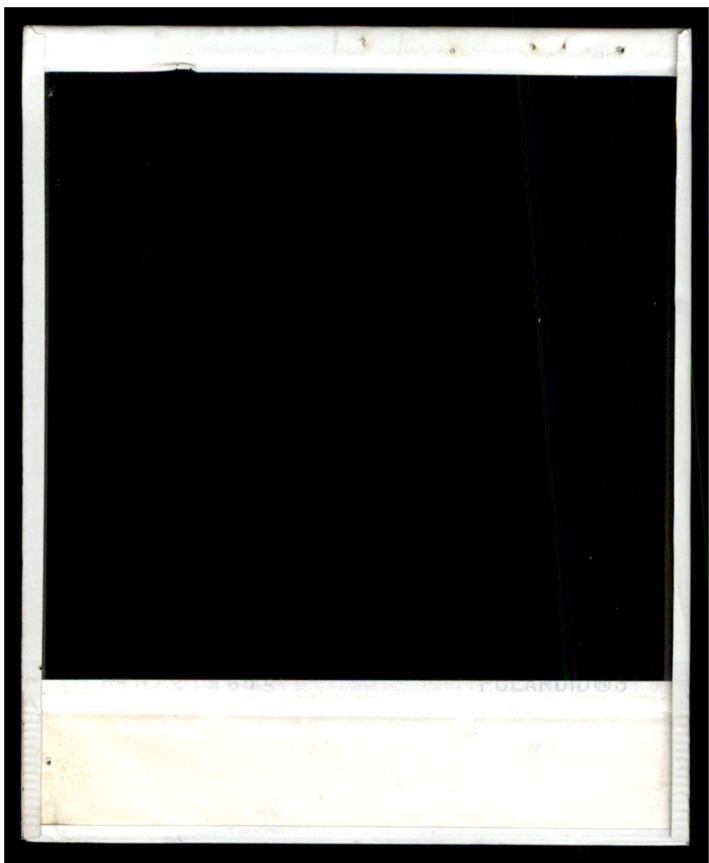

meter



FENCE

P

FENCE

P



115.0

13.200K

TALLMAN

19.6' N x S TALLMAN ST.
15.2' E x W BROOK ST

