

Tel. 678-5274

Carlton Morris

P.O. Box 1227

12/13/96

Fall River, Ma 02722

#32099 N.S. Breault St. W x Lenox St.

125 B

Please install a 1" copper ser. to supply a one-family home. from Lenox St. Meter inside the cellar wall

P125B L348 B & B Contracting - contractor

MAIN TO BE EXTENDED

Measures of 1" Curb STOP:

N x N line Rayno St. 365.0 ft.

W x E line Mt. Pleasant St. 15.0 ft.

W x meter pit 14.0 ft.

N x center line pit 6.0 ft.

Work done May 12, 1997



Pond View Cont. supplied & installed all stock:

44.9 ft. - 1" Copper tubing
1" Corporation tap
1" Curb Stop
1 Caldwell Stop Box, compl.



Inspection.....	\$	15.00
2 1" meter cplgs. @ 5.00 ea.....	\$	10.00
Turn on charge.....	\$	15.00
	\$	40.00

Pond View Excav. St. Open Permit # 177

POND VIEW CONST
SEWER # 22510

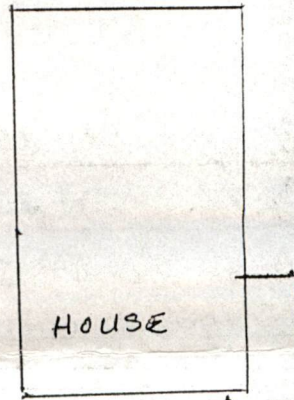

110'



Top. 6: 213'
Tap 122' →
