

SERVICE No 32205

NEW BEDFORD WATER WORKS

APPLICATION FOR SERVICE AND METER

NEW BEDFORD November 13, 1997

I HEREBY ACKNOWLEDGE the receipt of a copy of the Regulations prescribed in the Ordinance of the City, for the use of Water, and I request that the water may be furnished through a

2" ~~1/2~~ inch City meter at warehouse

W.S. Church st at north line Livingston St

at such rates as may from time to time be established by the City.

I hereby agree to pay promptly the bill for the Service pipe laid down for my premises, and to pay all dues for water, and I agree to conform to the said Regulations and to all provisions of the Water Ordinances, until written notice is given by me or my agent to cut off the supply.

has sewer - permit # 22637

P 113 L3 Nelson Cardoso - Contractor

TELEPHONE x 961-2895

x John N Kozlisc

x 314 Church St
New Bedford 508-995-5123

Service laid Work done Dec 18, 19, 1997 Size and kind of pipe

2" Copper

From Church st

- Jan 5, 1998

St.

Turned on

Meter Set

Reading

Location

in meter pit at property line
in bldg above floor - 2

Building rates

Paid

Cost of Service

\$ 88.00

Paid

Measures of 2" Curb Stop:

N x N line Irvington St.

17.0 ft.

W x W line Church St.

7.6 ft.

N x hydrant

20.0 ft.

MEASURES CURB STOP:

N x HYD 20'

W x W LINE CHURCH ST 7.6

JOBS DONE ON:

DEC - 18 - 97

DEC - 19 - 97

JAN - 5 - 98

meter
pit

IGTON ST PRIVATE PROP.

CHURCH ST

12-18-97 NELSON CARDOSO CONTRACTOR REMOVE 8" MECH. PLUG ON EXIST.
8"x8"x8" TEE - INSTALLED 8" MECH PLUG WITH 2" MUEHLER TAP.

4"x2" COPPER BEND FROM 2" MUEHLER TAP TO 2" CURB STOP (MUEL.)
FROM CURB STOP RUNNING COPPER 40' NORTH (BEND WEST TO 1" COUPLING COP. TO COP 1/2")

MEASURES CURB STOP:

N x HYD 20'

W x W LINE CHURCH ST 7.6


JOB DONE ON:

DEC-18-97

DEC-19-97

JAN-5-98

IRVINGTON ST PRIVATE PROP.

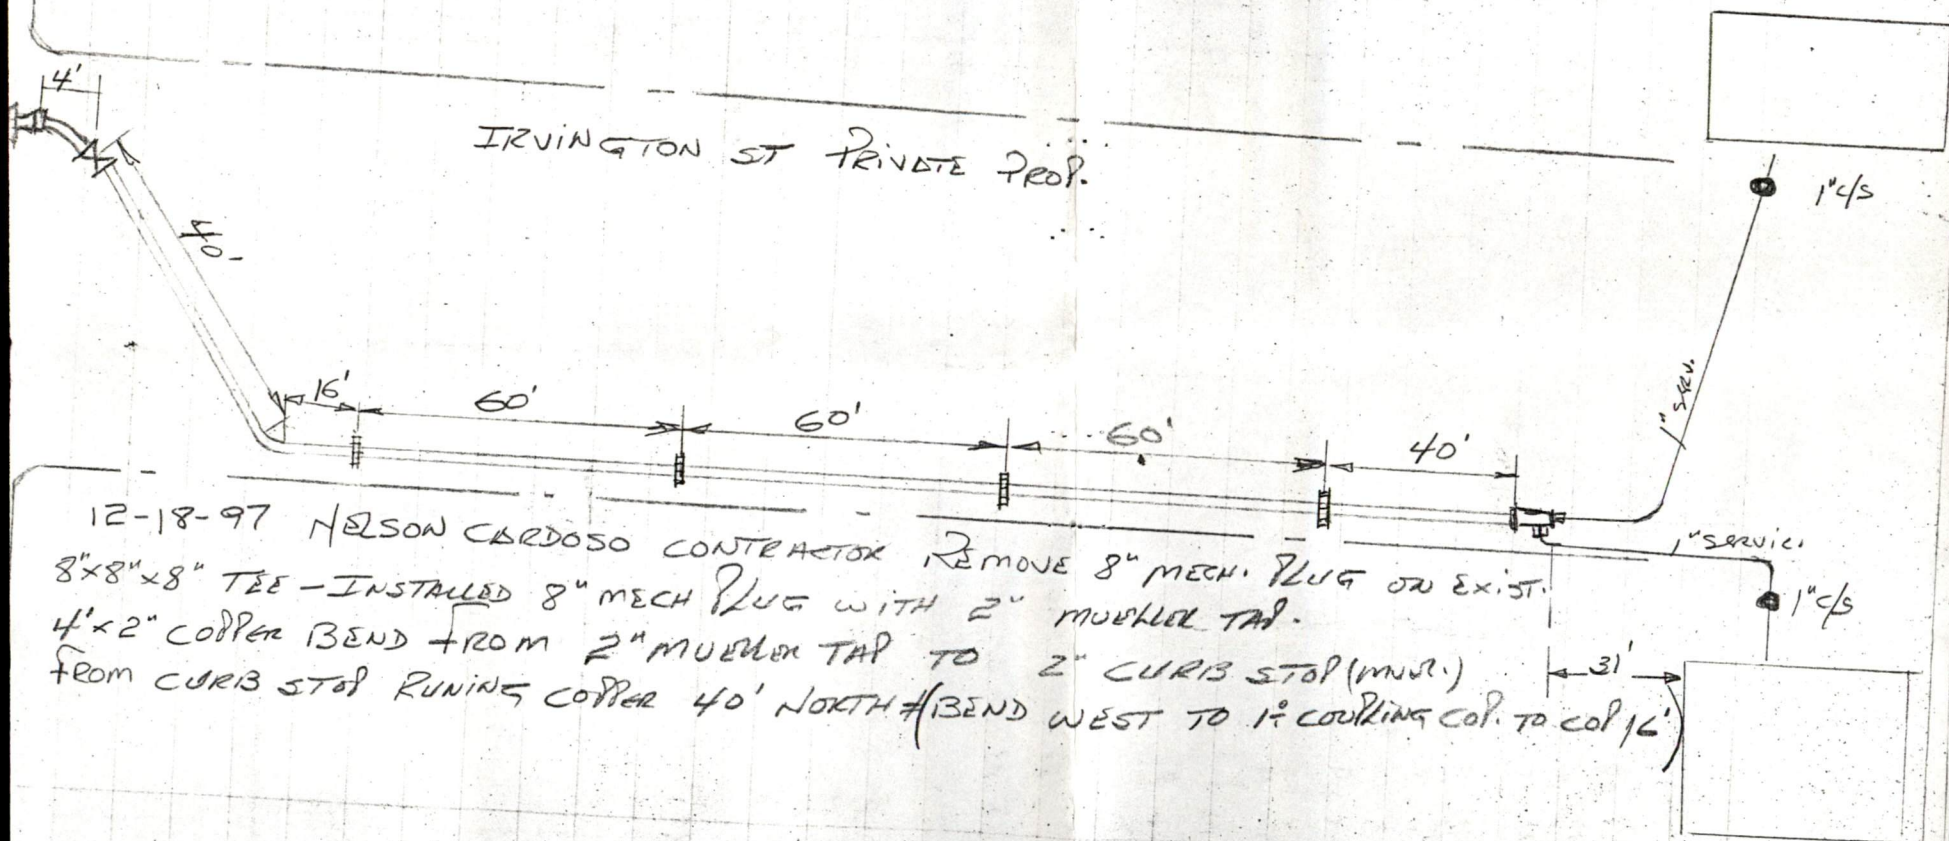

12-18-97 NELSON CARDOSO CONTRACTOR REMOVE 8" MECH. PLUG ON EXIST.
8" x 8" x 8" TEE - INSTALLED 8" MECH. PLUG WITH 2" MUEHLER TAP.

4" x 2" COPPER BEND FROM 2" MUEHLER TAP TO 2" CURB STOP (MNR.)
FROM CURB STOP RUNNING COPPER 40' NORTH (BEND WEST TO 1" COUPLING COP. TO COP 1/2")

Plotted
map
H3

CITY OF NEW BEDFORD

Application for Laying Water Main
on Total Cost BasisSept 10, 1997

To the New Bedford Water Board:

I, the undersigned, hereby make application for the laying of an 8" water main in Irvington Street, from Church St. westerly a distance of approximately 230 ft with a hydrant at the end.

It is agreed that the total cost of performing this work shall be borne by me.

The above described extension shall be made by my contractor according to the specifications of the New Bedford Water Department and is estimated by him to cost \$12,000.00.

It is further understood and agreed that upon application for service from this proposed line of main pipe as described herein, the applicant shall pay the cost of installing the service line from the water main into the property of the applicant within 30 days from the laying of said service line. The Board reserves the right to approve or reject any or all petitions, for the best interest of the City.

John M. Kala
(Property owner)
314 Church St
New Bedford Ma
(Address)

Witness:

Diane Martin

By: _____

_____, 19
(Date of Approval)

The above application has this day been approved by a majority vote of the New Bedford Water Board subject to the terms herein specified.

(Superintendent)_____
(Clerk of the Board)

