

TEL. 997-5266

Doro Dev. Corp. 991 Kempton St. NB

Nov. 12, 1986

132 E 2

#30712 N.S. Doreen St. W x McCombs Blvd.

Please install 1" copper serv. to supply one-family home. From Doreen St. meter inside cellar wall. Contr. to dig & maintain trench. Lot ~~695~~ 128

Measures of 1" Curb Stop:

W x W line McCombs Blvd.

126.0 ft.

S x N line Doreen St.

4.0 ft.

W x E line house

36.0 ft.

E x W line house

8.0 ft.

S x S line house

39.0 ft.

Work done Nov. 5, 1987

Main is 14 ft. N x S line Doreen St .

W x LOT 127 - 99 Ft.
E x LOT 129 74.6 Ft.

Doro Devel. supplied all stock

1" Copper tubing
1" Corporation tap
1" Curb Stop
1 Caldwell Stop box, compl.

B-100 Mu. tapping machine use.....	\$ 14.00
2 1" meter cplgs. @ 4.00 ea.....	\$ 8.00
Carting.....	\$ 10.00
Turn on charge.....	\$ 15.00
Labor.....	\$ 31.12
	<u>\$ 78.12</u>

Doro Devel. dug, backfilled & will maintain trench.

2-1" cplgs - McGraw - 1-22-88


#30712 N.S. Doreen St . W x McCombs Blvd.

Additional Measures:

W x lot 127 99.0 ft.

E x lot 129 74.6 ft.

Lot 128

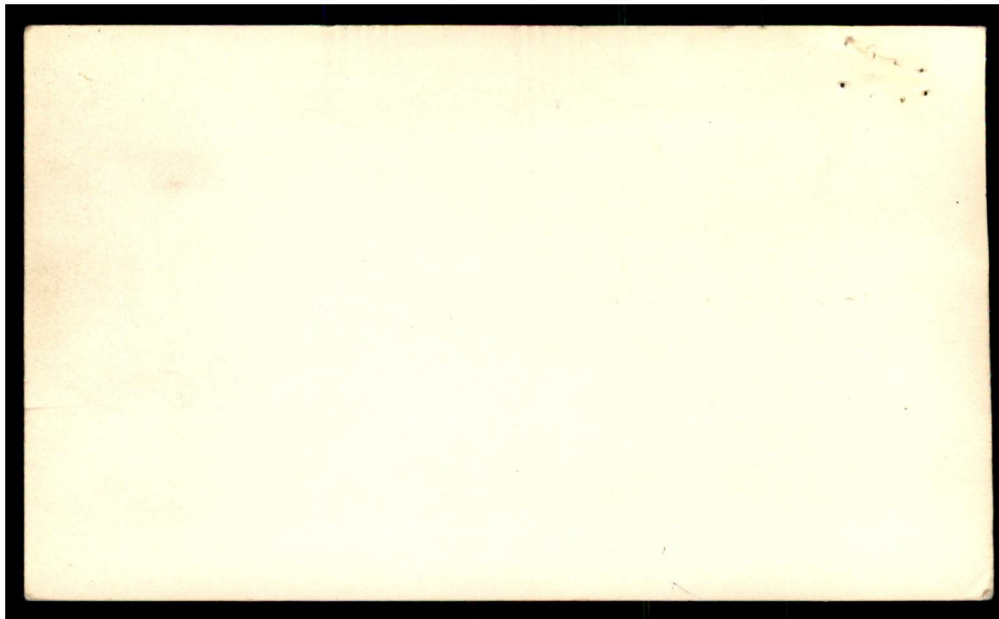

Additional Measures Oct. 22, 1990

· N.S. Doreen St. W x McCombs Blvd.

Ser. # 30712 1"

W x W line McCombs Blvd.

126.0 f t.

L. Souza

