

Record of Water Service Connection

PROJECT: Lead Service Replacement Program - Phase I, New Bedford, MA

STREET: Nelson Street

HOUSE No: 100

Contractor: P Gioioso and Sons, Hyde Park, MA

Date: 7/27/2020

Type: Copper Diameter (in): 1

Distance from main to curb stop (ft): 7.2 Water Pressure (PSI) 100

Distance curb stop to meter (ft): 12.8

Distance from curb face to curb stop (ft): 2.0

Depth of Service (ft): 4.0


Total length of new pipe installed (ft): 20

Curb Stop Replaced: yes Size (in): 1

Corporation Replaced: yes Size (in): 1

Ball Valve Replaced: yes Size (in): 1

Ties:

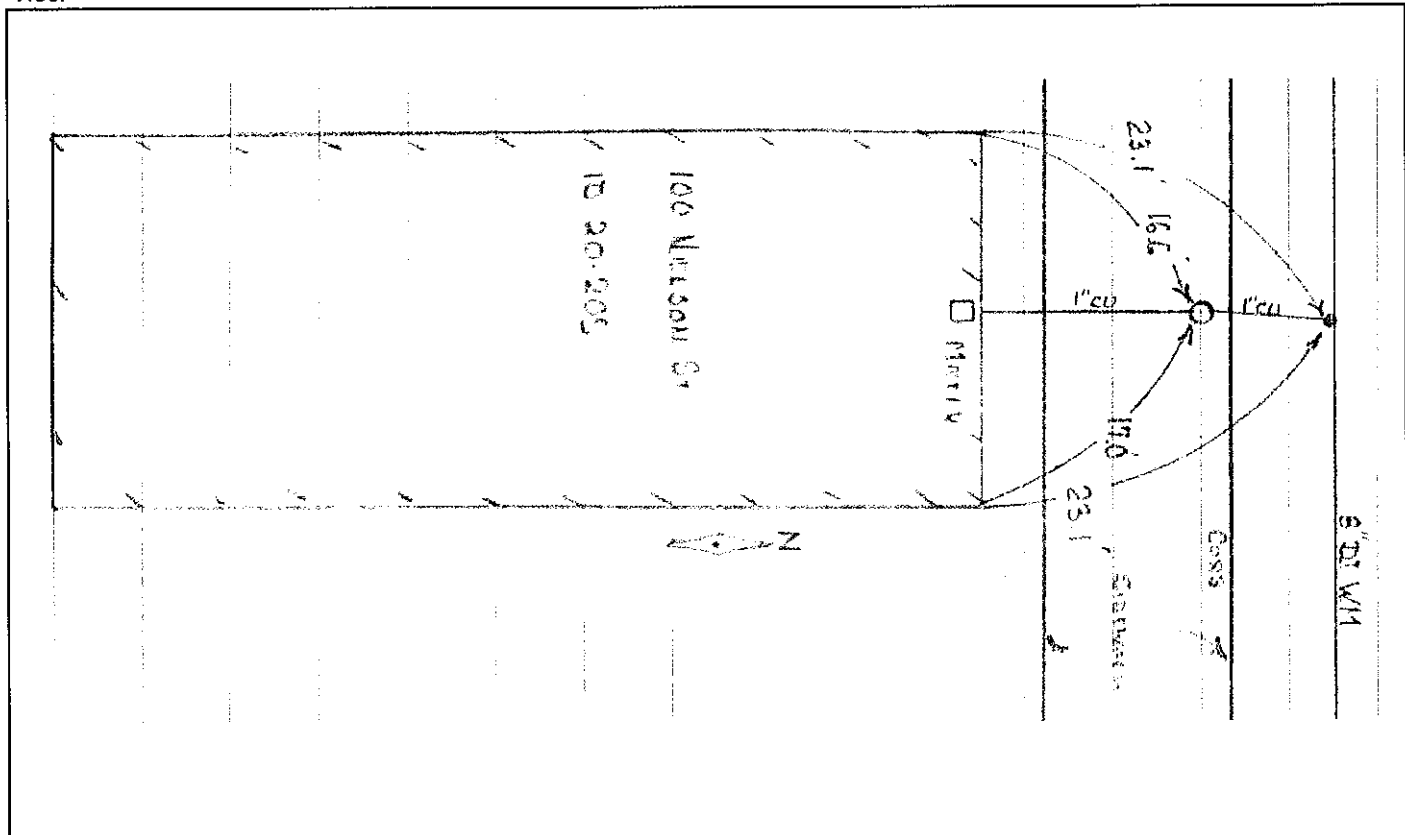

Remarks:
