

Record of Water Service Connection

PROJECT: Lead Service Replacement Program-Phase I, New Bedford, MA

STREET: Nelson Street

HOUSE No: 21

Contractor: P Gioioso and Sons, Hyde Park, MA

Date : 8/6/2020

Type: Copper

Diameter (in): 1"

Distance from main to curb stop (ft): 27.4

Water Pressure (PSI) 100

Distance curb stop to meter (ft): 13

Distance from curb face to curb stop (ft): 1.3

Depth of Service (ft): 3.9

Total length of new pipe installed (ft): 40.4

Curb Stop Replaced: yes

Size (in): 1


Corporation Replaced: yes

Size (in): 1

Ball Valve Replaced: yes

Size (in): 1

Ties:

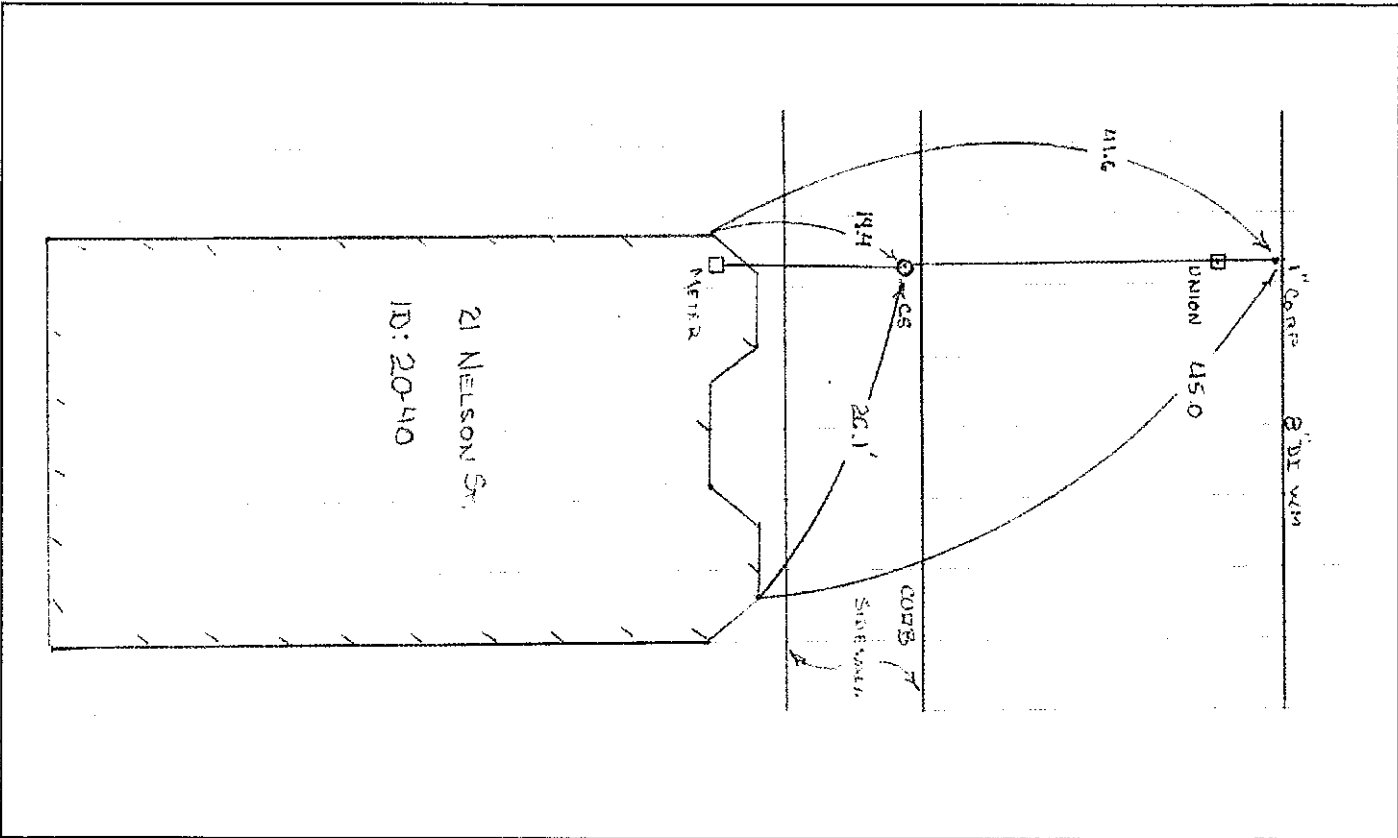

Remarks:

1" union installed where shown
