

## Record of Water Service Connection

PROJECT: Lead Service Replacement Program-Phase I, New Bedford, MA

STREET: Nelson Street

HOUSE No: 38

Contractor: P Gioioso and Sons, Hyde Park, MA

Date: 8/4/2020

Type: Copper

Diameter (in): 1"

Distance from main to curb stop (ft): 9.5

Water Pressure (PSI) 100

Distance curb stop to meter (ft): 13

Distance from curb face to curb stop (ft): 2.7

Depth of Service (ft): 4.5

Total length of new pipe installed (ft): 22.5

Curb Stop Replaced: yes

Size (in): 1


Corporation Replaced: yes

Size (in): 1

Ball Valve Replaced: yes

Size (in): 1

Ties:

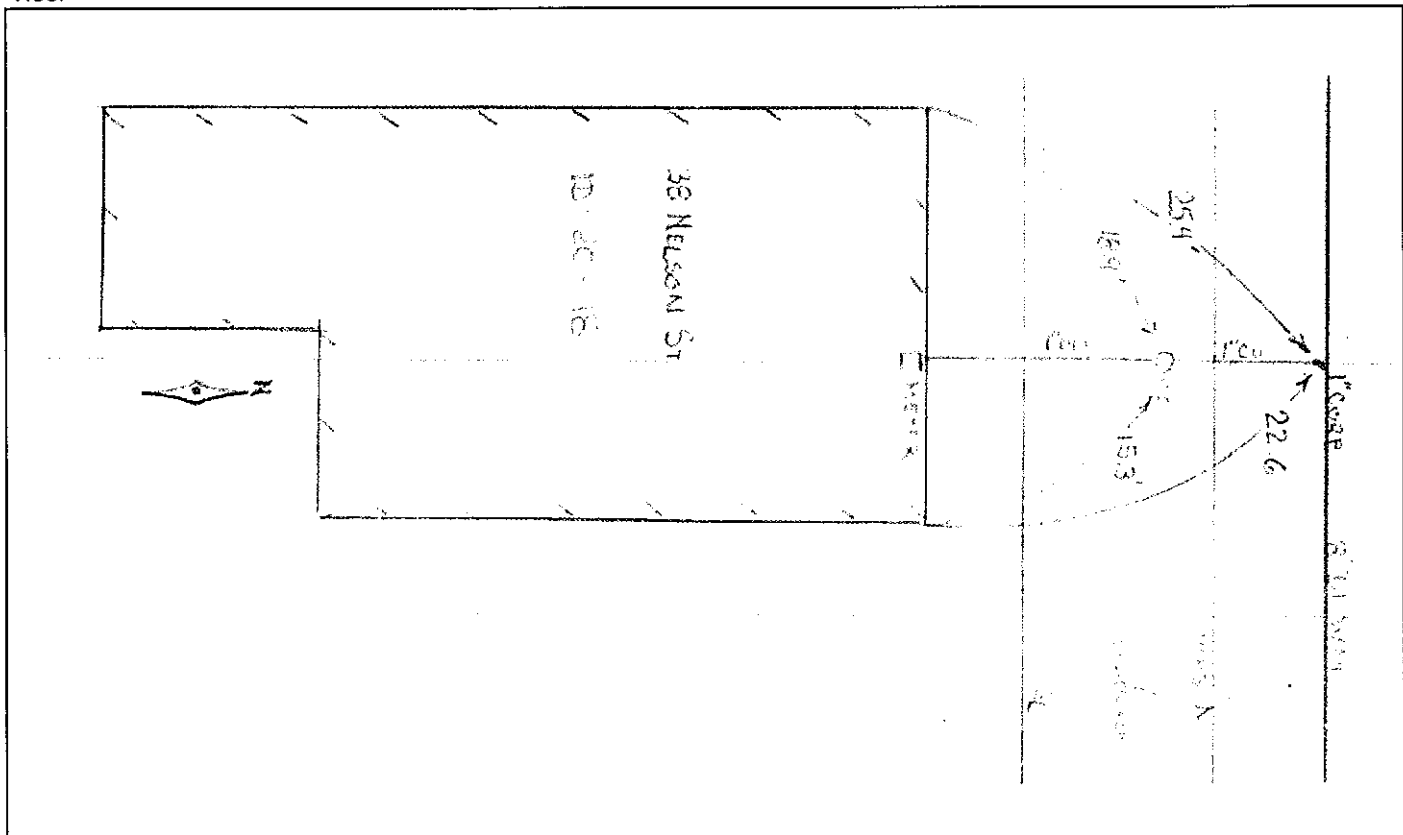

Remarks:
